RPMGLOBAL

AMT - Budgeting & Forecasting

Training Manual

Copyright © 2024 RPM Software Pty Ltd. All Rights Reserved



RPM SOFTWARE – ASSET MANAGEMENT

Table of Contents

Introduction to AMT **5**

Processes **6**

Training Workshops **9**

1. Create a Budget 9
2. Edit a Budget 18
3. Analyse Budgets 32
4. Export the Budget 41
5. Other Budgeting Items 42

Preface

The training workshops are developed to supplement instructor-led training. The guide is constructed in a way that teaches students the key functionality of the application through practical hands-on workshops. Each workshop details tasks that the student is required to complete. The workshops build on each other to help ensure a comprehensive understanding of the application is achieved at the completion of the course. Space is provided at the end of each workshop for learning checks and student notes.

Symbol Library



Note

A note for participants about the task.



Important Reminder

An important reminder for the participant about the task.



Learning Check

Check your understanding on the workshop and ask any related questions.


Course Outline

Prerequisites	Getting Around AMT, AMT Key Concepts, Long-Term Planning, Strategy Optimisation
Target Audience	Long-term Planner, Finance Business Planning
Nominal Duration	2 days
Course Objectives	Create and analyse budgets
Learning Outcomes	At the end of the course, participants will have learned to: • Create a new budget o Use Budget & Forecast Manager o Create a new budget o Import real assets into the budget o Import some modelling assets into the budget o Import overheads o Enter/modify capex details o Understand optimal life indicator o Copy a budget o Run budgeting reports o Forecast reports – that is, compare budget to projections

	• Modify a budget o Set new asset usages o Add/edit asset costs o Reload asset costs o Add/edit downtime o Edit overhead costs o Enter escalations o Add manpower o Review and edit plant hire revenue o Review and override risk o Recalculate a budget o Update budget status o Export a budget • Analyse budgets o Standard reports o Compare budget reports • Compare current performance to budget (special case) o Create new budget o Copy original budget and refresh with actual utilisation, costs and projections o Analyse actual performance vs budget (comparison reports) o Flag the current budget against assets in AMT (site) o Run live AMT budget reports
Assessment Strategy	The completion of workshop tasks
AMT version	8.26


Introduction to AMT

AMT is a comprehensive asset management system consisting of integrated modules as depicted below.

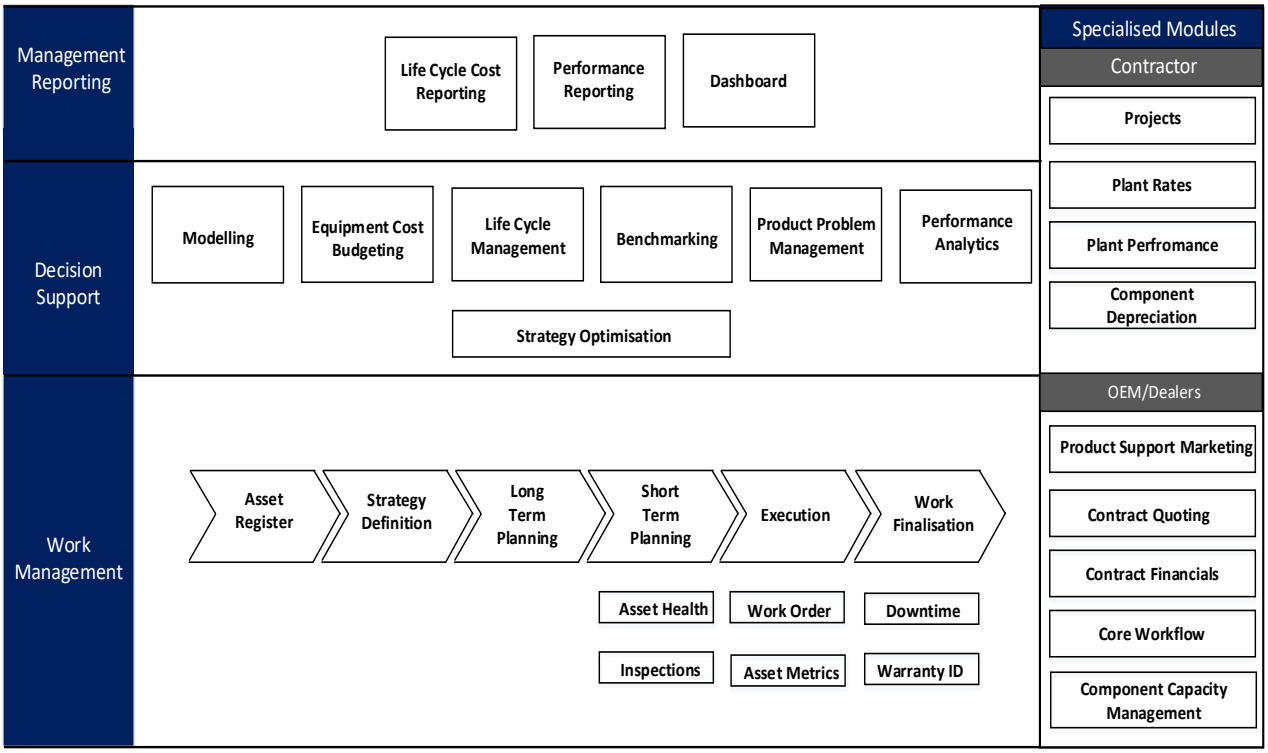

Processes

PROCESS DIAGRAM – CREATE A BUDGET

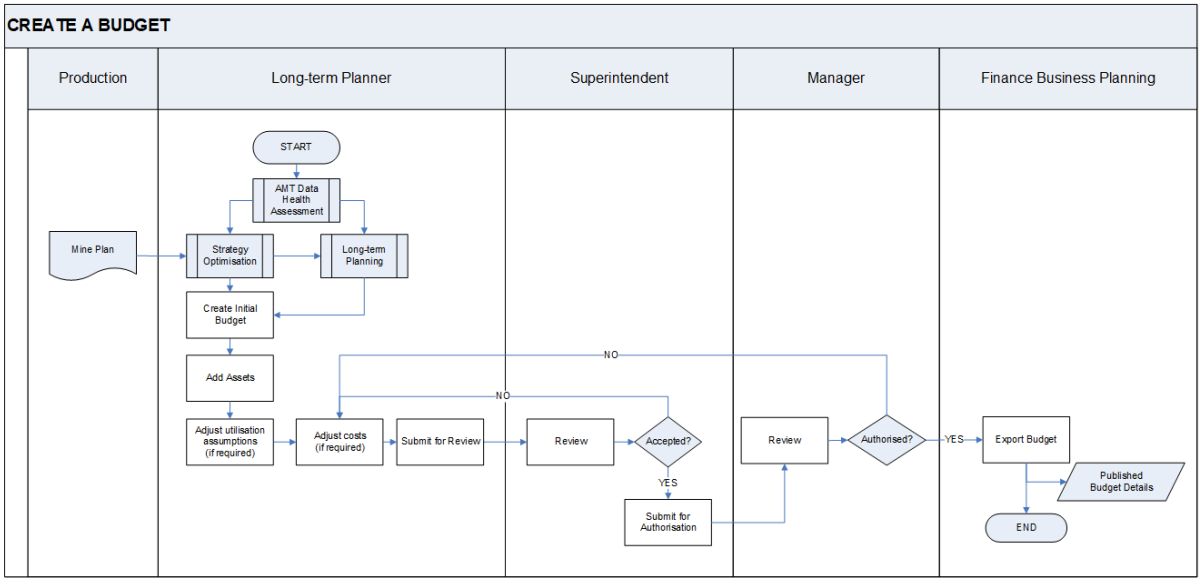

Process Flow Step	AMT Functionality	Notes
AMT Data Health Assessment	N/A	Refer to AMT Health Assessment process
Strategy Optimisation	N/A	Refer to Strategy Optimisation process
Long-term Planning	N/A	Refer to Long-term Planning process
Create Initial Budget	Budget and Forecast Manager screen	Select appropriate Budget Type and Budget Year
Add Equipment	Budget and Forecast Manager screen > Equipment	Real Equipment and/or Modelling Equipment Note, can only add Equipment-Tasks specific to the user's Equipment-Cost Centre permissions within their AMT user account.
Apply utilisation assumptions (if required)	Budget and Forecast Manager screen > Usages	Adjustments made here are not replicated into "live" AMT.
Adjust costs as required	Budget and Forecast Manager screen > Equipment Cost	Adjustments made here are not replicated into "live" AMT.
Submit for Review	Budget and Forecast Manager screen	Update Status to "For Review" (optional).

Process Flow Step	AMT Functionality	Notes
Copy initial budget and create a new budget version	Budget and Forecast Manager screen	Copy and update new version or update existing version - approach is procedure dependent. Note, when copying a Budget, the Start and End Date of the new budget cannot be changed.
Submit for Authorisation	Budget and Forecast Manager screen > Status	Update Status to “For Authorisation” if approved otherwise change status to “In Progress” (optional).
Review	Budget and Forecast Manager screen > Budget Reports	
Authorised	Budget and Forecast Manager screen > Status	Update Status to “Authorised” if approved otherwise change status to “Revoked” (optional).
Export Budget	Budget & Forecast Manager screen	Update Status to “Exported” Costs (per Equipment, cost centre, expense element, per month) Labour Hours (per Equipment, cost centre, expense element, per month)

PROCESS INPUTS

The following inputs are required for this process:


- Strategy Definition: The maintenance strategy has been defined so that AMT is forecasting 100% of the expected costs.
- Long-Term Planning: The long-term plan is maintained and accurate.
- Strategy Optimisation: The initial strategy definition (that is, expected asset utilisation, maintenance plans, and so on) is reviewed and updated on an ongoing basis for both accuracy and risk/optimisation.
- Agreed Approach: The people responsible for determining maintenance strategy have developed and finalised guidelines for, and an approach to, budgeting.

PROCESS OUTPUTS

The following outputs can be expected from this process:

- Direct asset maintenance cost budget
- Approved budget – used to measure Actuals vs Budget
- Published budget – For consumption by other systems

PROCESS DIAGRAM – COMPARE ACTUAL TO BUDGET PERFORMANCE

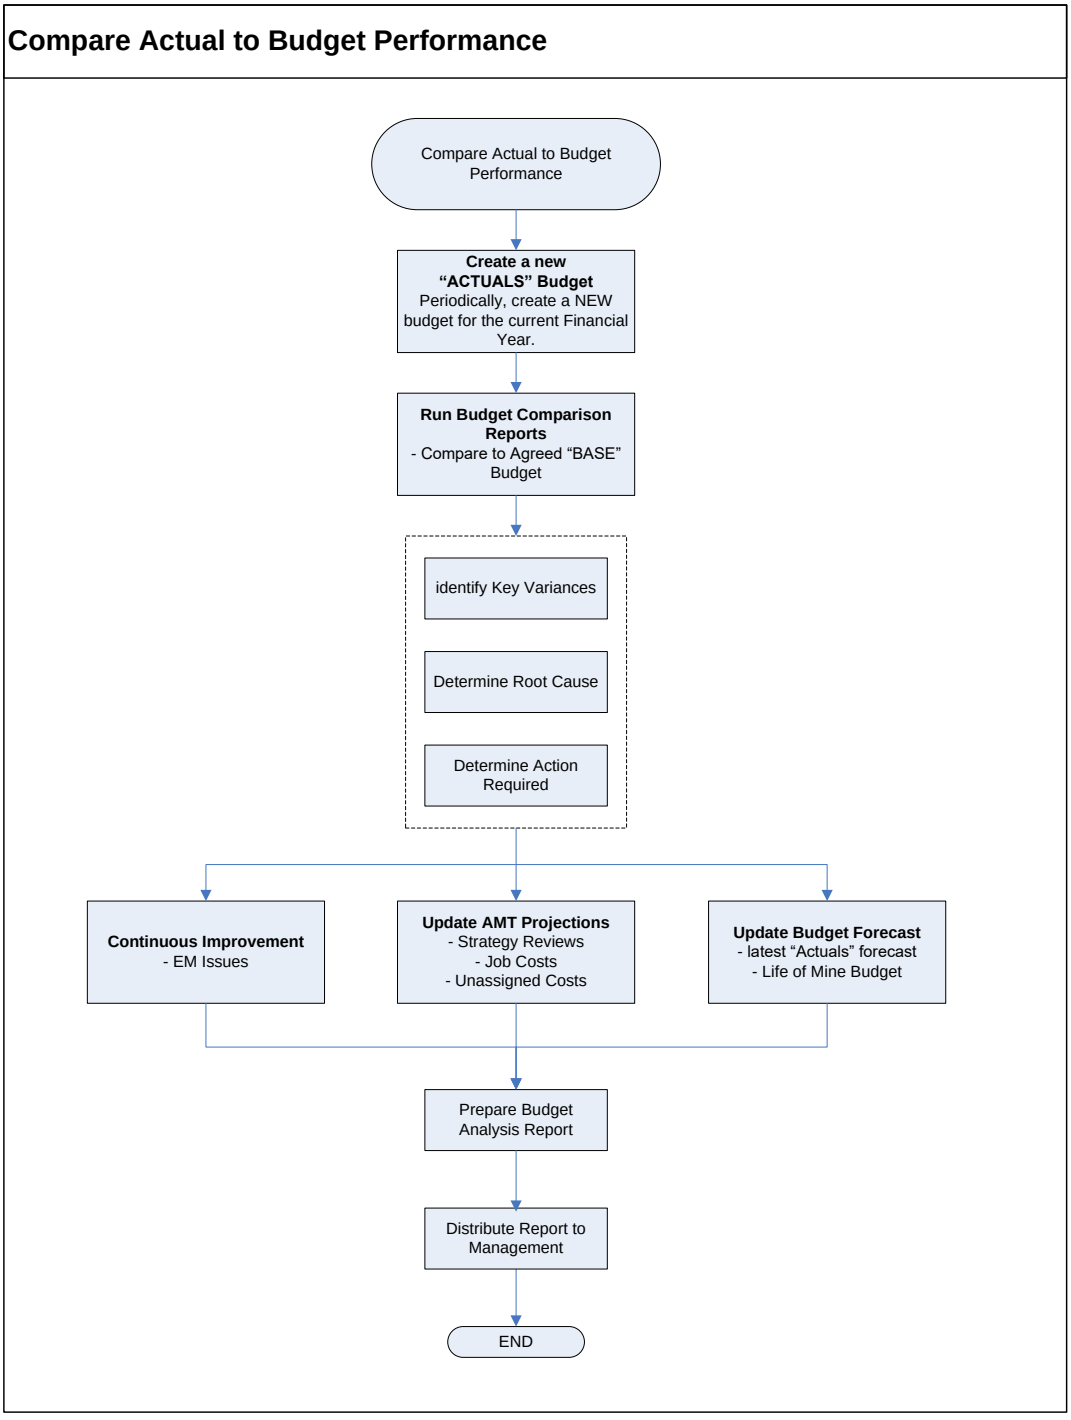


Training Workshops

1. Create a Budget

Procedure – Create Initial Budget

1. Under **Budgeting & Forecasting** > **Budgeting**, double-click **Budget and Forecast Manager**.
2. Click **Add New Budget**.

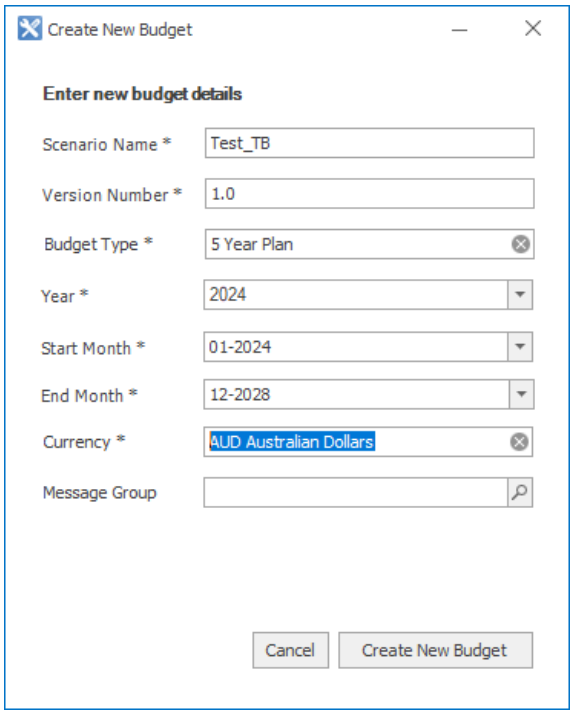

- You define the Scenario Name, Version Number, Budget Type and Year fields; they are only used for descriptive purposes.
- Budget Type can have a defined number of periods which will determine the End Month when the Start Month is updated.
- The Start Month and End Month fields determine the period for which data will be brought into the budget from the current projection when items with a corresponding budget code are added.
- Message Groups are set up under **System Administration** > **User Profiles**.

*The budget's message group will be notified each time the **Edit Status** changes. The users who receive the email are notified about the progression, but not about the details of the changes.*



The budget status system table needs to be configured for which statuses a budget can change to, based on its current status.

The budget status an individual user can change is set at the budget status permission of the user's account.




A user can only select budgets with statuses for which they have permissions within their AMT user account.

Certain budget statuses are read-only. That is, if Under Review is configured as read-only, then the details within the budget cannot be changed.


Procedure – Add Assets

Perform the following steps to add equipment to a budget:


1. In **Budget Header Manager**, click **Equipment**.
2. Click **Add New Equipment**.
3. Filter for the correct assets, then click **Add Equipment to Budget**.

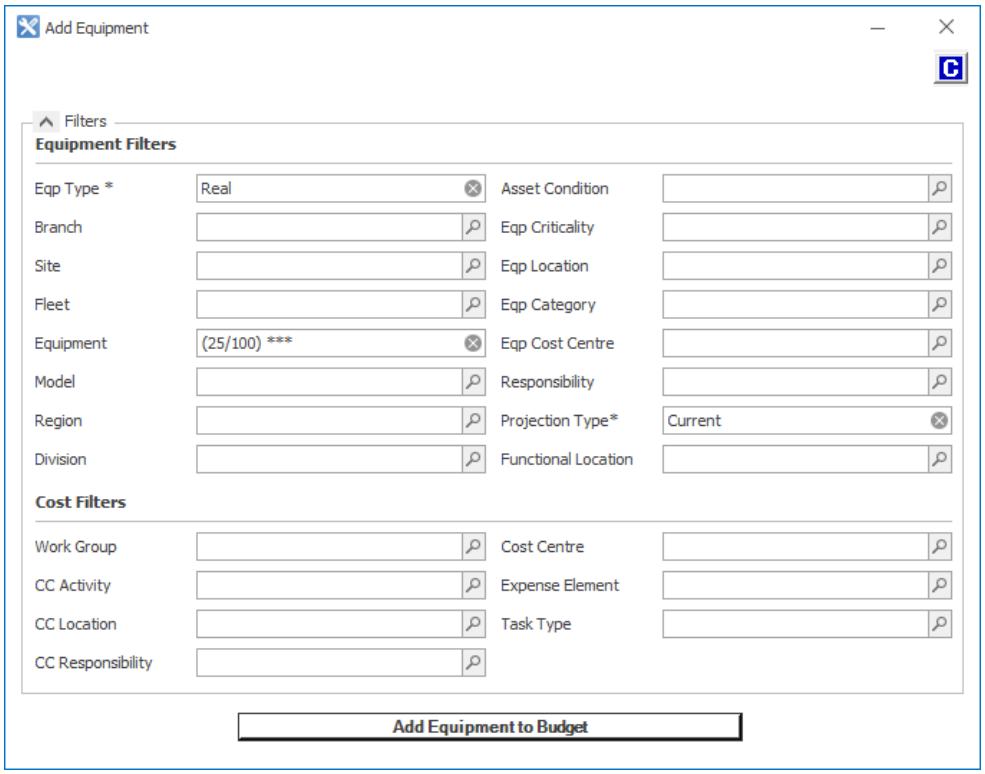

4. The summary form advises of the number of equipment to be added to the budget.
5. Click **OK**.

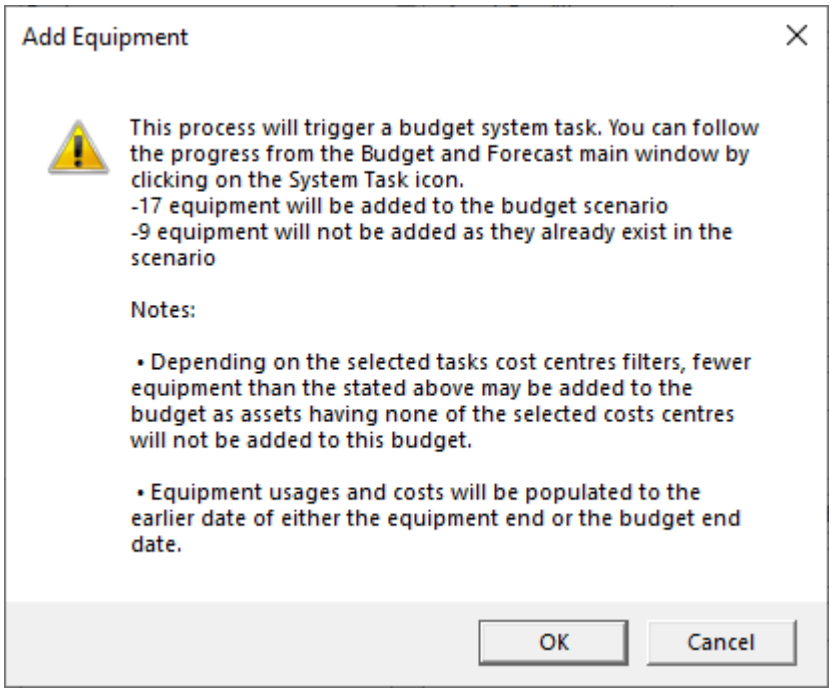


A message box informs you that your request has been added to a queue for processing.



6. Click **OK**.

7. On the **Budget & Forecast Manager**, select  to view the queued budgets.

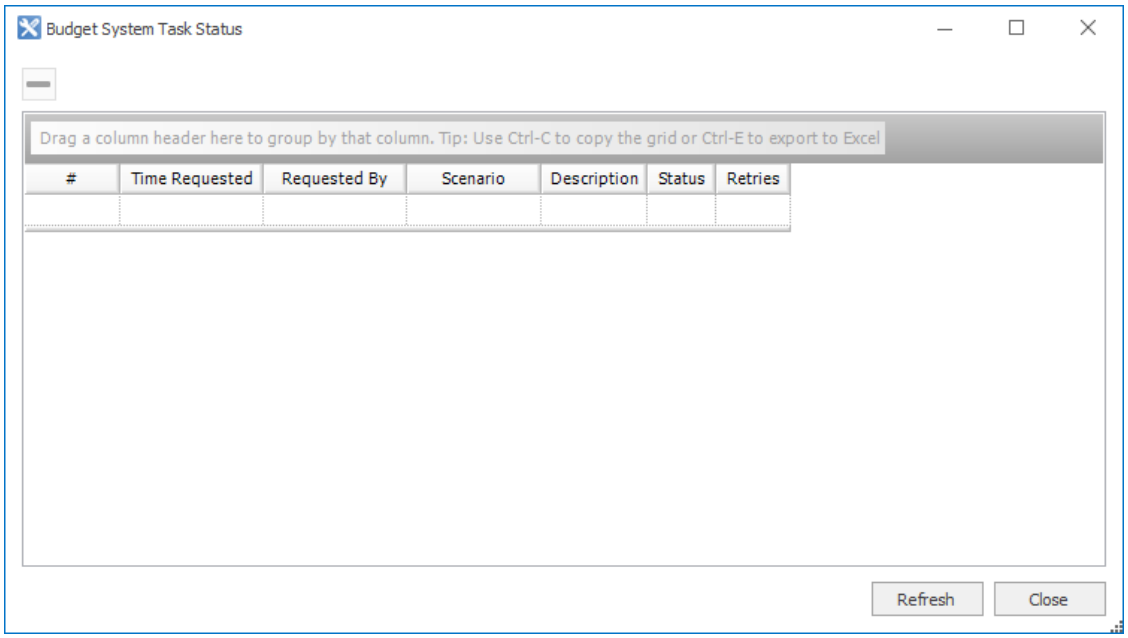

You cannot delete a calculating budget from this queue.

8. After your budget has left the queue, on the **Budget Equipment Manager** apply the filter to see the added equipment.

9. Edit asset data if required.

Changes made to equipment details are not replicated to "live" AMT.

Procedure – Add Overhead Projection

1. Navigate to **Overhead Cost Category**.
2. Add the categories of overheads that need to be budgeted.



If the company categorises certain overheads as Cost of Sale or Capex, these overhead categories should be flagged as Cost of Sale or Capex.




If actual overhead costs will be imported from an external system, Cost Centre, Expense Element and Code fields must align to the external system.

3. Navigate to **Overhead Navigator** to create the overhead projection.
4. Click **Add new overhead projection**.
5. Complete all mandatory fields. Special fields are explained below:
   a. **Overhead Level**: The level at which the overheads are costed and the overhead billing (management fee) is charges.
   b. **Level Description**: The options available depend on the overhead level chosen.
   c. **Overhead ERP ID**: Unique identifier that links the overhead schedule in AMT to the overhead billing in the ERP.



When an overhead billing is sent to AMT by the ERP, AMT needs to know to which set of overheads it applies. For equipment billings, the equipment's serial number and model are the linking fields; for overheads, it is the Overhead ERP ID.

Check with Accounting as to what this identifier should be, and also check with the AMT Administrator.

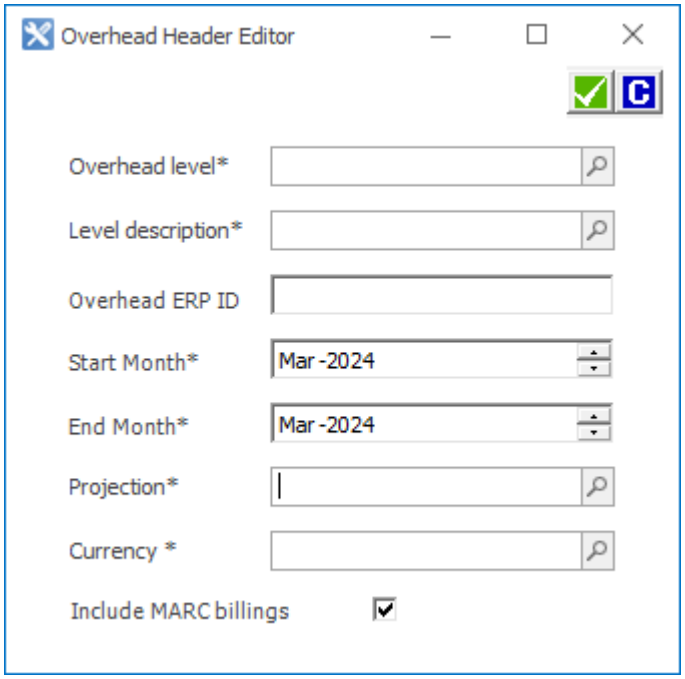

d. **Include MARC billings**: Only applies to maintenance contract equipment. If a non-equipment utilisation fee is charged to recover overhead costs (that is, the overheads are recovered through a monthly fee that is not usage based). This box should be enabled. If this box is not enabled, the user will be able to set up a schedule of overhead costs, but not management fees.

6. Populate the overhead's schedule with costs and billings. You can enter values in the grid directly or copy and paste from Microsoft Excel.


To copy the overhead schedule to Excel, right-click the overhead grid and select Copy the Table.

To paste from Excel, the overhead schedule has to be created in AMT in terms of the correct number of rows (representing billing and cost categories) and columns (representing month)

To paste from Excel, select only the data rows, right-click the first data cell in the Overhead grid and click Paste.

Procedure – Add Overhead to Budget

1. Navigate to **Budget Header Manager**.
2. Click **Overheads Manager**.
3. Click **Add new overhead level**.



4. Select an **Overhead**, by clicking the search, then click **Save**.

If the text is BLUE, the cost is an actual cost. Actual costs cannot be edited.

If the text is RED, the cost has been manually overwritten.


If the field is GREEN, a comment has been added.

Even though you can copy the data from the grids into Excel, edit it and paste it back, we do not recommend this action with the following forms. If there is a large volume of data to change, that indicates the live AMT health data is not accurate and it should be corrected at the source.

If you're having problems pasting the data back into AMT, ensure you're pasting into a future month.

5. Navigate to **Budget Header Manager**.
6. Click **Equipment Costs**.
7. In **Cost Occurrence Manger**, right-click the existing occurrence of the strategy task.

8. Click **Edit Occurrence**.
9. Click **Save**.

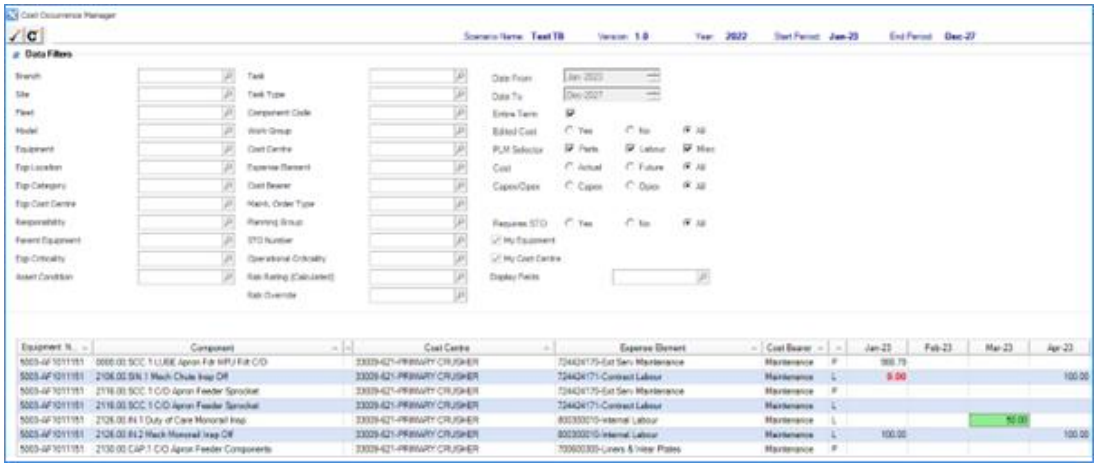

Learning Check



Check your understanding of the workshop and ask any related questions.

Notes

2. Edit a Budget


Procedure – Deleting and Re-importing Assets

Perform the following steps to delete and re-import equipment into the budget:

1. Navigate to **Budget Header Manager**.
2. Click **Equipment**.
3. Use filters to find the required assets.
4. Highlight the required assets, then click **Delete**.
5. To re-import, follow the steps to add a new asset.


Procedure – Change Asset Header Details

1. Navigate to **Budget Header Manager**.
2. Click **Equipment**.
3. User filters to select the required asset.
4. Select the asset and click **Edit**.
5. Modify as required.

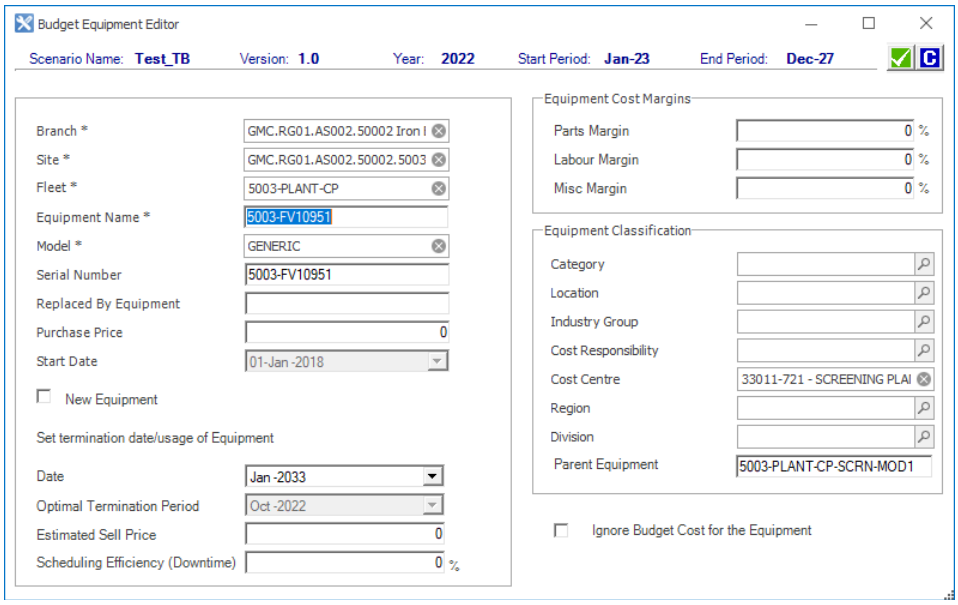

Procedure – Update Asset Costs

1. Navigate to **Budget Header Manager**.
2. Select **Equipment Costs**.
3. Filter for costs.
4. View additional, relevant fields on the grid using the **Display Fields** option (for example to view STOs associated to tasks, maintenance order types).
5. Edit the costs.

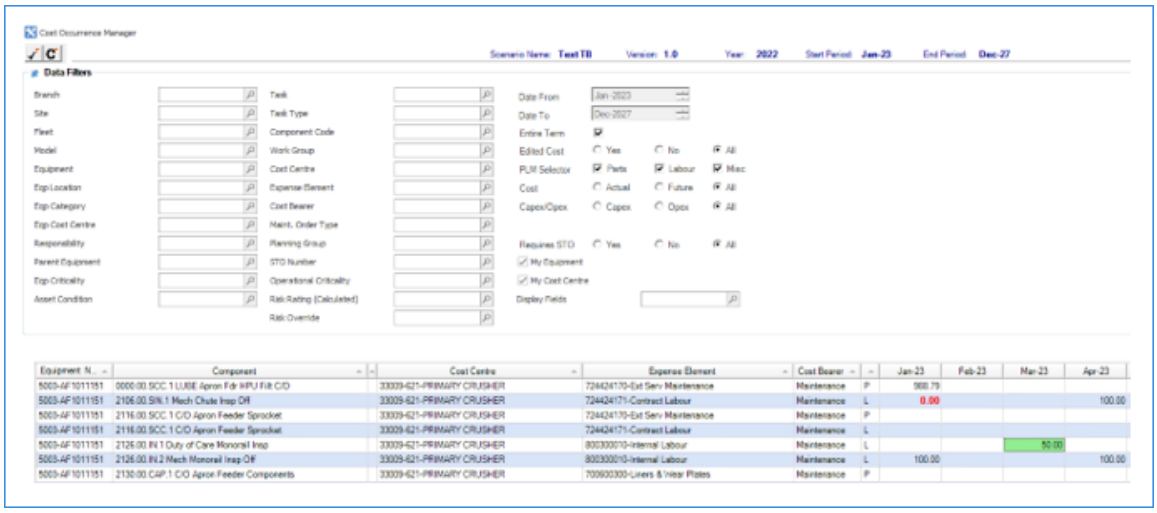

If the text is RED, the cost has been manually overwritten.

If the field is GREEN, a comment has been added.

Even though you can copy the data from the grids into Excel, edit and paste it back, we do not recommend this action with the following forms. If there is a large volume of data to change, that indicates the live AMT health data is not accurate and it should be corrected at the source.

If you're having problems pasting data back into AMT, ensure you're pasting into a future month.


Procedure – Change the Component Schedule

1. Navigate to **Budget Header Manager**.
2. Click **Equipment Costs**.
3. In **Cost Occurrence Manager**, right-click the existing occurrence of the strategy task.
4. Click **Edit Occurrence**.
5. Select and edit the date if necessary.
6. Click **Save**.

Procedure – Override the Risk Rating of a Strategy Task


1. Navigate to **Budget Header Manager**.
2. Click **Equipment Costs**.
3. In **Cost Occurrence Manager**, add **Risk Rating (Calculated)** and **Risk Override** to the display fields filter. Apply the filter to return these fields.
4. Populate the **Risk Override** field with the required value.
5. Click **Save**.

Changing the override value on one line item of a Strategy Task will apply that value to all line items of that Strategy Task and all occurrences of that strategy task within the Budget.

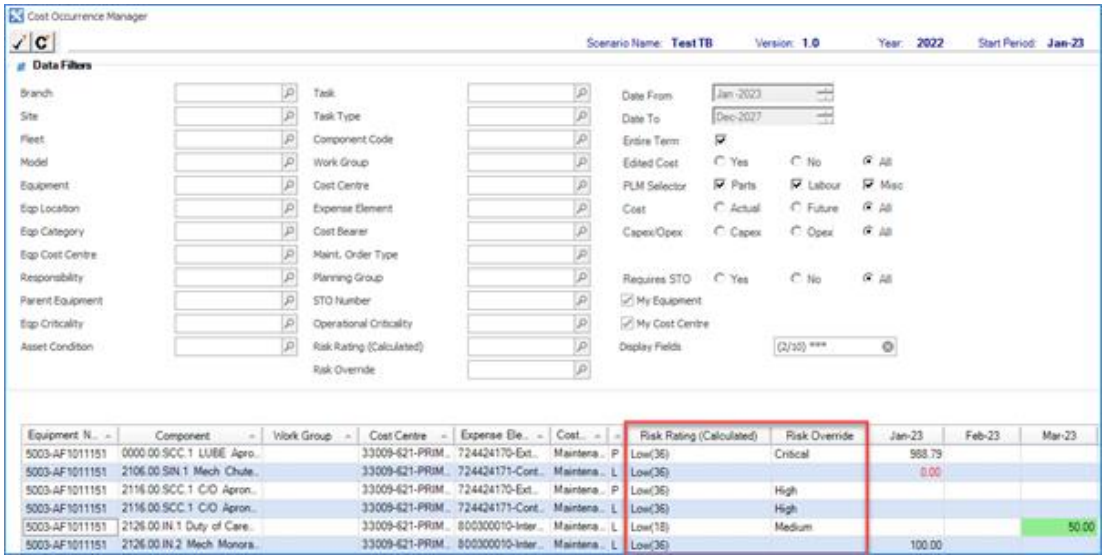

Procedure – Update Financial Codes

1. Navigate to **Budget Header Manager**.
2. Click **Equipment Costs**.
3. In **Cost Occurrence Manager**, financial codes can be changed in bulk. Filter for the required occurrences.
4. Populate the **Cost Centre, Expense Element or Cost Bearer** fields with the required value.
5. Click **Apply Changes**.

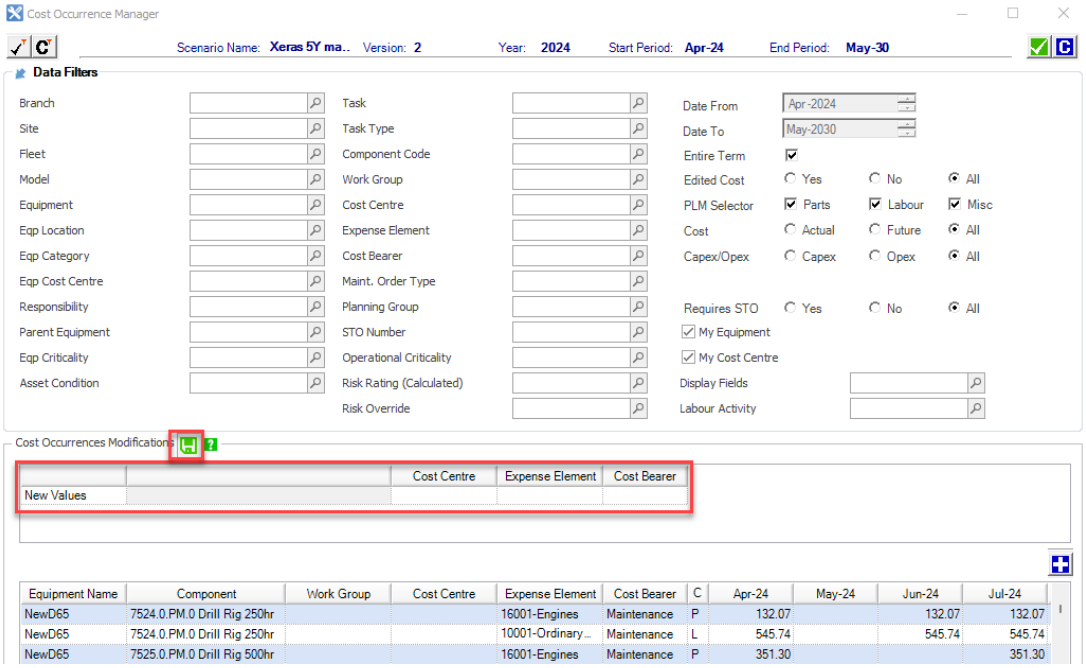


Procedure – Update Usages

1. Navigate to **Budget Header Manager**.
2. Use filters to select the **Asset** and **UOM**, then click **Apply Filter**.
3. Make changes as necessary.
4. Click **Save** and **Close**.
5. Click **Recalculation**.

If the usages are increased, potentially future months will not show any costs. This is because AMT only takes a snapshot of data for the Budget Start and Budget End Months. Therefore, there isn't future data to "back fill" the budget if usages are increased; causing maintenance to be forecast earlier. Hence why we recommend changes to usages are applied "live" AMT before adding the impacted assets to a budget.

Procedure – Labour Rates Management

The Budget module now fully handles labour rates and preserves a link between labour hours and labour costs. If the user chooses to, changing the labour hours on a given task can automatically change the associated labour costs and vice versa, keeping labour hours and costs consistent.

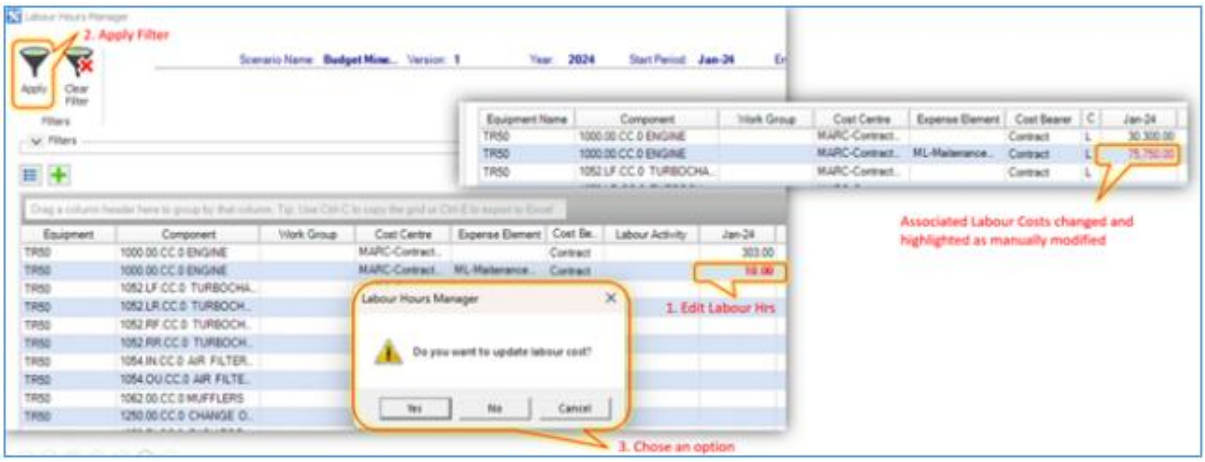

A warning message alerts users about the potential impact on labour costs before proceeding.

Changes in labour rates won't impact actual occurrences loaded into the budget.

Procedure – Change Downtime

1. Navigate to **Budget Header Manager**.
2. Click **Downtime**.
3. Use filters to select the required assets.
4. Edit future asset downtimes.
5. Click **Save** and **Close**.
6. Click **Recalculation**.

As with all changes in budgeting, modifications made to forecasted values will not update the source projection in the core of AMT. Actual durations (historic data) are not imported into budgeting.

Procedure – Deleting and Re-importing Overheads

1. Navigate to **Budget Header Manager**.
2. Click **Overheads Manager**.
3. Click **Delete**.
4. To re-import, follow the steps in **Add Overhead to Budget**.

Procedure – Edit Overheads

Check with your System Administrator to understand whether overheads apply to your specific AMT solution.

Perform the following steps to edit an existing overhead projection in a budget:

1. Navigate to **Budget Header Manager**.
2. Open **Overhead Details**.
3. Filter for relevant costs.
4. Edit costs.
5. Click **Add New Overhead** to add an additional overhead cost category into the projection.
6. Edit the new row as required.

Procedure - Edit Manpower

Entering manpower in AMT is available for a specific scenario. This data is not included the budget data exported to EPF.

1. Navigate to **Budget Header Manager**.
2. Click **Manpower**.
3. Use filters to find the required staff headcount data.
4. Edit the data.
5. Click **Add** to add additional headcount.

Procedure – Edit Projects

Entering project data only applies to specific customers who use AMT (such as contractors). This data is not included the budget data export.

1. Navigate to **Budget Header Manager**.
2. Click **Projects Manager**.
3. Use filters to find the required projects.
4. Click **Edit** and make changes as necessary.



If changes have been made to the plant rate scheduled in core AMT, and you'd like the budget to reflect these changes, the asset must be deleted from the budget and re-added. The delete process deletes all data relating to the asset in budgeting (such as costs, downtime, usages).

Procedure - Editing Plant Hire Revenue

Entering plant hire revenue data only applies to specific customers who use AMT, such as contractors. This data is not included the budget data export.

1. Navigate to **Budget Header Manager**.
2. Click **Plant Hire Revenue**.
3. Use filters to find the required plant hire revenue.
4. Click on a specific cell to edit its properties.
5. Click **Save** and **Close**.
6. Recalculate the budget for the changes to take effect.

Procedure – Apply Escalations to Asset Costs

1. Navigate to **Budget Header Manager**.
2. In the Cost Escalator section, click **Equipment Costs**.
3. In the **Equipment Cost Escalation (Adjustment)** form, flag whether the escalation will apply to **Parts**, **Labour**, **Misc**.
4. Select the **Date Range**.
5. Enter the **Escalation Adjustment**.
6. Enter notes and comments about the reason for the escalation.
7. Click **Apply Escalation**.
8. Repeat steps 1-6 if additional escalations are required.

Procedure – Apply Escalations to Overhead Costs

1. Navigate to **Budget Header Manager**.
2. In the **Cost Escalator** section, click **Overhead Costs**.
3. In the **Overhead Cost Escalation** (Adjustment) form, select the **Overhead category**.
4. Select the **Date Range**.
5. Enter the **Escalation Adjustment**.
6. Enter notes and comments about the reason for the escalation.
7. Click **Apply Escalation**.
8. Repeat steps 1-6 if additional escalations are required.

Procedure – Review and Analyse

1. Navigate to the **Budget Header Manager** form.
2. Click **Budget Reports**.
3. Click **Budget Summary**.
4. Hover over the report tree. These reports analyse the currently selected budget.
5. Click **Comparison Reports**.



Comparison reports can only compare like for like periods within the budgets selected.

The Budgets can have different start and end dates, however only where they have overlapping periods will the comparison be considered.

Procedure – Make Bulk Changes to Existing Budget Task Data

The following steps demonstrate how to bulk edit asset costs. The same mechanism can be used to bulk update usages, labour hours, downtime, and overhead data. However, the changes are limited to the grid being edited. Task data in other areas within the budget is unaffected. For example, changing asset costs following this procedure does not update labour hours nor downtime.

Perform the following steps to make bulk changes to an existing budget task data:

1. Navigate to **Budget Header Manager**.
2. Click **Equipment Costs**.
3. Right-click the grid and select **Copy the table**.
4. Open a Microsoft Excel file and paste the data into the cells (Right-click the appropriate cell in the spreadsheet and select **Paste**, OR click the appropriate cell in the spreadsheet and press **Ctrl+V**.)
5. Make the required changes to the data in the Microsoft Excel file.
6. Select only the data set (not the headings in the rows or columns) and copy it.



Only numeric monthly values can be pasted into the budget table.

7. Return to the Cost Occurrence Manager dialog, right-click and select **Paste**.



Right-click the cell directly, do not left-click it first.

8. The data set is pasted into AMT. All cells change to red to indicate a change was made manually.



The changes made do not update the corresponding task Labour Hours or Downtime data.

9. Review the changes.
10. Click **Save** and **Close**.
11. Recalculate the budget for the changes to take effect.

Procedure – Reschedule a Budget Task Occurrence

The most efficient approach to rescheduling a budget task occurrence, assuming that there is no change to asset utilisation, is to change the date of the occurrence on the cost grid. In this approach, the labour hours and downtime associated with this task are also moved automatically to the same date.

Following a different approach, such as copying values to Microsoft Excel, editing in Excel and pasting the changes back into AMT, described in the previous procedure, only updates the values in the grid that you are directly editing. It does not update values in other grids.

Perform the following steps to reschedule a budget task occurrence:

1. Navigate to **Budget Header Manager**.
2. Click **Equipment Costs**.



An occurrence of a task is represented by costs in a month.

3. In **Cost Occurrence Manager**, right-click the existing occurrence of the strategy task.
4. Click **Edit Occurrence**.
5. Highlight the desired task occurrence.
6. Select the new date when the task is to occur.
7. Click **Save** and **Close**.
8. When the save is complete, the cost has moved to the Month you selected.
9. Click **Save** and **Close**.
10. Recalculate the budget for the changes to take effect.



Following this approach, the labour hours and downtime associated with this task will show the corresponding changes.

Procedure – Delete a Budget Task Occurrence

Similar to rescheduling a budget task occurrence, following the steps below ensures that the corresponding Budget Task Labour Hours and Downtime data are updated automatically.

Perform the following steps to delete a budget task occurrence:

1. Navigate to **Budget Header Manager**.
2. Click **Equipment Costs**.



An occurrence of a task is represented by costs in a month.

3. In **Cost Occurrence Manager**, right-click the existing occurrence of the strategy task.
4. Click **Edit Occurrence**.
5. The **Change Occurrence Date** (Projected occurrences only) dialog displays. Highlight the desired task occurrence. There can be more than one occurrence of a task in a month.
6. Select the **Occurrence** and click **Delete**.
7. Click **Save** and **Close**.
8. When the save is complete, the cost is removed.
9. Click **Save** and **Close**.



Following this approach, the labour hours and downtime associated with this task will show the corresponding changes.

Procedure – Create a New Budget Task with Costs and Labour Hours

A new task can be added to the budget for an asset providing the task already exists in the projection of the asset imported into the budget.

Perform the following steps to create a new budget task with cost and labour hours:

1. Navigate to **Budget Header Manager**.
2. Click **Equipment Costs**.
3. Use filters to select the required asset.
4. View additional, relevant fields on the grid using the **Display Fields** option (for example, maintenance order types).



A budget may have Equipment from other users as well. Equipment added by other users to the same budget will be displayed on your screen in italics. You can view these Equipment details but cannot edit them.

*By selecting **My Equipment** and **My Cost Centre** check boxes, you can filter for the asset and cost centres that you have access to.*

5. Click **Add**.
6. Enter the relevant details.
7. Click **Save** and **Close**.
8. The task is added to the list. All changes show in RED colour to indicate a change has been made manually.
9. Repeat steps 4 to 9 if more costs (including expense elements) and/or occurrences for the same task are to be added to the budget.
10. **Comments** can be added to explain the reason for the changes made. To do this, right-click the cell and select **Comments**.
11. Enter comments into the text box.
12. Click **Save** and **Close**.



To add new comments and view or delete existing comments, right-click the cell again.

13. Recalculate the budget for the changes to take effect.
14. If you want to add **Labour Hours** for this task into the budget, click **Labour Hours** on the **Budget Head Manager** screen.
15. The **Labour Hours Manager** dialog displays.

16. Use filters to select the required asset.
17. Click **Add**.
18. Enter the relevant details.
19. Click **OK**.



All the changes show in RED colour to indicate a change has been made manually.

20. Repeat steps 13-18 to add more labour activities and/or occurrences for the same task into the budget.
21. Click **Save** and **Close**.
22. Recalculate the budget for the changes to take effect.

Procedure – Refresh Labour Rates

The Refresh Labour Rates function enables users to update labour rates that might have changed on AMT live, changing the associated costs for selected assets.

Perform the following steps to refresh labour rates within a budget:

1. In **Budget Header Manager**, click **Equipment**.
2. Filter for the desired equipment for which the labour rates will be refreshed.
3. Click **Refresh Labour Rates**.



Forecast labour costs will be changed.

Actual labour costs will not be updated.

Learning Check



Check your understanding of the workshop and ask any related questions.

Notes

3. Analyse Budgets

Procedure – Update Usages

1. Navigate to **Budget Header Manager**.
2. Use filters as required to select the **asset**, **UOM**.
3. Click **Apply Filter**.
4. Make changes as necessary.
5. Click **Save** and **Close**.
6. Click **Recalculation**.



If the usages are increased, additional cost occurrences may appear.

The DLCC slice AMT takes for the budget period selected contains and additional 12 months of occurrences for this to be achieved.

Equipment projected usages are updated in “live” AMT, and when the change is made, we import that Equipment with that projection into the budget. Remember, a Usage Profile is linked to a projection which is linked to an Equipment.

Note: The changes below update the usage profile linked to the equipment’s current projection. If this is a temporary change, before making the change, note the values in the usage profile or copy the current usage profile using Usage Profile Manager. You can follow similar steps when working with an Alternate projection.

Perform the following steps to update usages for single equipment:

1. On the right of the home screen, click **Filter Equipment** to open the **Equipment Selector** dialog.
2. Select fields from the **Group By** list and click **OK**.
3. Double-click the equipment.
4. On the Edit Equipment dialog, click **Quick Links** and select **Usage Profile**. In the **Select Equipment’s Projection** dialog, click **OK**.
5. On the **Edit Usage Profile** dialog, click **Add** in the **Usage Steps** section.
6. On the **Add Usage Step** dialog, enter the Usage **Step Start Date**. Click **Save**.
7. Enter the desired usage rate for the UOMs in the **Unit of Measure (UOMs)** section. Click **Refresh**.
8. Repeat steps 4-6 until the usage profile reflects the desired usage rates for the desired periods. Click **Refresh** when complete.
9. You can edit the usage rates at the monthly level by clicking **Edit Monthly Usage Rates**.
10. On the **Monthly Usage Profile** dialog, set the Start Month and number of months from the date when you want to view/edit the usage rates. Click **Apply Filters**.

11. You can edit cells one-by-one or in bulk. Changes made display in red. For more information on bulk changes, refer to the **Make bulk changes to existing budget task data** section in this document.
12. When the changes are complete, click **Save**.
13. On the **Edit Usage Profile** dialog, you will notice extra rows automatically created and the value in the columns represents the new rates entered in terms of the UOM. Click **Save**.

    This triggers a recalculation of the equipment's current projection.
14. Click **Yes**.
15. In the **Edit Equipment** dialog, take notice of the value in the **Projected Cost** column for the current projection in the **Equipment Projection List** section.
16. Click **Refresh**. The **Projected Cost** value is updated.
17. The equipment should now be added to the budget.

Procedure – Update Usages – Multiple Equipment

Equipment projected usages are updated in "live" AMT, and when the change is made, we import that equipment with that projection into the budget. Remember, a usage profile is linked to a projection which is linked to an equipment.

Note: The changes below update the usage profile linked to the equipment's current projection. If this change is temporary, note the values in the usage profile before making the changes.

Perform the following steps to update equipment usages:

1. Search Monthly Usage Profile using the Search field.



*Alternatively, from the **My Functions** hierarchy select **Setup & Admin** > **Usage Profile** > **Monthly Usage Profile**.*

2. On the **Monthly Usage Profile** dialog, select filters as required and click **Apply Filter**.
3. You can edit cells individually or many at once using any of the right-click options. Changes made manually display in red.
4. If the original values need to be restored after adding the equipment to the budget, copy the data from the grid into a Microsoft Excel file and save it.
5. Click **Save**. This triggers a recalculation of the life cycle projections linked to the usage profiles.
6. The equipment should now be added to the budget.

Procedure – Extend the Life of an Equipment

Extending the life of an equipment is performed in “live” AMT and then the equipment is imported into the budget. The life of an asset is extended in “live” AMT so additional future occurrences of tasks can be calculated and imported into the budget. We recommend that this activity is performed using an alternate projection since the end date/usage of an equipment’s current projection reflects the actual end date/usage of the equipment.

Perform the following steps to extend the life of an equipment:

1. Select **Filter Explorer** to open the **Equipment Selector** dialog. Use filters to select the relevant equipment and click **OK**.
2. Select fields from the **Group By** list and click **OK**.
3. Double-click the equipment.
4. On the **Edit Equipment** dialog, click **Add**.
5. On the **Add/Copy Projection** dialog, perform the following actions:
   - Set the **Projection Type** as **Alternate**.
   - Give the projection a meaningful name in the **Projection name** field and set the **Source** as **Current**.
   - Click **Process**.
6. Click **Refresh** on the Equipment Projection List section and double-click the new Alternate projection.
7. On the **Edit Projection** dialog, change **End Date** and **End Usage** and click **Save and close**.
8. On the **Edit Equipment** dialog, click the **Tasks** tab. Filter for the new projection and click **Apply Filter**. Click **Yes** in the Recalculation message box.
9. The projection will be recalculated to the new end date and end usage. You can now add the equipment to a budget but use the alternate projection as the source instead of the current projection.



If you want to compare, copy the original budget. In the copied budget, delete the existing equipment, then add the equipment again but this time with the new Alternate projection.

Otherwise, in the existing budget delete the existing equipment before this new version is added.

10. To copy the budget, open the **Budget & Forecast Manager** dialog as explained in the **Create Initial Budgets** section in this document.
11. Select the desired budget and click **Copy Budget**  .
12. On the Copy Budget dialog, enter the required budget details such as **Scenario Name, Version Number, Budget Type** and **Year**. Click **Create New Budget**.
13. On the **Budget Header Manager** screen, select the **Equipment** option.
14. Click **Apply Filter**. AMT displays a list of items.

15. To delete a budget, select the desired item and click **Delete**.
16. Click **Yes** to the notification asking to confirm the deletion.
17. To add the new equipment, click **Add** on the **Budget Equipment Manager** dialog.
18. On the **Add Equipment** dialog, select **Equipment**, **Projection Type**, the Alternate projection created and click **Add Equipment to Budget**.
19. On the **Budget Equipment Manager** dialog, click **Save** and **Close**.
20. You return to the **Budget Header Manager** screen. Click **Refresh** and the **Calculation Status** will show **Required**.
21. Click **Recalculation**.
22. When the recalculation is complete, click **Refresh** again to see the **Total Budget Cost** value in the centre of the screen change.

Procedure – Apply Cost Escalation Factors to a Budget

Under certain circumstances, there may be a requirement to apply future escalation to the costs within a budget.

Note: Like all Budget and Forecast Manager changes, changes here do not update “live” AMT.

Perform the following steps to apply cost escalation factors to a budget:

1. On the **Budget Header Manager** screen, select **Equipment Costs** from the **Cost Escalators** section.
2. On the **Equipment Cost Escalation** dialog, perform the following actions:
    a. Flag whether the escalation will apply to **Parts**, **Labour Misc**.
    b. Select the **Date Range**, use the up and down arrow keys to select past and future dates.
    c. Enter the **Escalation Adjustment**.
    d. Enter notes and comments about the reason for the escalation.
    e. Click **Apply Escalation**.
3. Click **Yes** in the notification to apply this escalation to all projected costs for filters selected and directly to the costs.



*Clicking **Yes** triggers another recalculation of the budget on the **Budget Header Manager** screen.*

The escalation is arithmetic and not compounded. A 3% increase will increase all costs by 3% and not increasingly by 3% over the preceding years.

4. On the **Budget Header Manager** screen, click **Recalculate Budget** to recalculate the budget.
5. Repeat steps 1-6 if additional escalations are required.
6. Recalculate the budget for the changes to take effect.

Procedure – Create a Budget with Alternate Projections for "What If" Comparisons

After creating the budget from Current projections, you may want to create a budget using alternate projections (which represent What If scenarios) and compare.

For information on creating alternate projections, copying, and running a budget with these alternate projections and comparing the budgets, refer to the **Strategy Optimisation** training manual.

Now that you have created alternate projections to represent a "what if" scenario, you can create a budget using the alternate projections rather than the current projections and run reports to compare them.

Perform the following steps to create a budget using alternate projections:

1. Navigate to **Budget & Forecast Manager**.
2. Click **Add New Budget**. Enter your budget details, then click **Create New Budget**.
3. In Budget Header Manager, click **Equipment**.
4. Click **Add New Equipment**.
5. Filter for the correct assets.
6. In **Projection Type**, select an alternate projection rather than the current projection.
7. Click **Add Equipment to Budget**.
8. The summary form advises of the number of assets to be added to the budget. Click **OK**.
9. A message dialog informs you of the outcome of the asset add process.
10. Refresh the filter on the **Budget Equipment Manager**. Ensure the new assets have been added.
11. Click **Save** and **Close**.



*Reports under the **Budget Reports** menu can be run to analyse the "What If" budget.*

Reports can also be run to compare the two budgets.

Procedure – Compare Two Budgets

When the new budget version has been updated, it can be compared to the original budget or another budget version.

Perform the following steps to compare two different budgets:

1. Navigate to **Budget & Forecast Manager**.
2. Open one of the two budgets you want to compare.
3. Click **Comparison Reports** > **Budget Summary** > **Compliance To Plan - Summary**.
    a. In the **Compare With** box, select the budget to compare.
    b. Set other mandatory and relevant reporting filtering and presentation options.
    c. Click **Preview**. Analyse and close the report when finished.

4. Click **Comparison Reports** > **Asset Cost Analysis** > **Cost Period Analysis**.
   a. In the **Compare With** box, select the budget to compare.
   b. Set other mandatory and relevant reporting filtering and presentation options.
   c. Click **Preview**. Analyse and close the report when finished.
5. Click **Comparison Reports** > **Asset Cost Analysis** > **Cost Analysis**.
   a. In the **Compare With** box, select the budget to compare.
   b. Set other mandatory and relevant reporting filtering and presentation options.
   c. Click **Preview**. Analyse and close the report when finished.

Procedure – Review and Analyse

1. Navigate to the **Budget Header Manager** form.
2. Click **Budget Reports**.
3. Click **Budget Summary**.
4. Mouse over the report tree. These reports analyse the currently selected budget.
5. Click **Comparison Reports**.
6. Mouse over the report tree. These reports compare the currently selected budget with another budget.



Comparison reports can only compare like for like periods within the budgets selected.

The budgets can have different start and end dates, however only where they have overlapping periods will the comparison be considered.

Procedure – Create an "Actuals" budget to assess Equipment utilisation impacts (Optional)

This optional method involves analysing specific data to understand cost variance drivers while keeping other data constant. Follow this method to demonstrate how the utilisation of an equipment is the key factor for actuals vs. budget performance and you need the level of detail AMT can provide to prove it. Don't use this method every time you want to compare budget to actuals.

Notes:

- Sometimes the reason actual costs are higher or lower than the budget is driven by changes in the asset's utilisation, rather than good or poor maintenance practices. The challenge is to prove this. In AMT, you can use this process to help prove it.
- You copy the budget, replace the budgeted usages with actual usages, recalculate the budget and then compare it to the original budget. The difference in cost between the two will be driven by usages.

So, you copy the approved budget or forecast and create a new budget. Then, replace equipment usage and costs with actuals.

Perform the following steps to create a new actuals budget:

1. In the Search field, search for Budget and Forecast Manager. Double-click **Budget and Forecast Manager**.



*Alternatively, from the **My Functions** hierarchy select **Budgeting & Forecasting** > **Budgeting** > **Budget and Forecast Manager**.*

2. In the **Budget and Forecast Manager** screen, copy a budget, performing these actions:
   a. Click **Apply Filter**.
   b. Select the budget to copy.
   c. Click **Copy Budget**.
3. On the **Copy Budget** dialog, enter relevant details such as **Scenario Name**, **Version Number**, **Budget Type** and **Year**. Click **Create New Budget**.
4. Click **Apply Filter** to refresh the list of budgets in AMT. Double-click the new budget to begin editing it.
5. On the **Budget Header Manager** screen, select **Equipment** from the **View/Edit Data** list.
6. On the **Budget Equipment Manager** dialog, use the **Data Filters** section to filter for specific Equipment and then click **Apply Filter**.
7. From the **Data Update Routines** section, click **Apply** against **Replace usage with actuals**. This will populate the usage with actuals.

With an increase or decrease in usages, the maintenance cost also increases or decreases.

It is also possible to import actual costs and actual/projected costs. If this is desired, import and analyse using comparison reports one at a time, to understand the impact of each incrementally.

When copying a budget, the start and end dates can be changed to any values within the original budget's date range.

8. Click **OK** in the routine initiation notifications displayed.
9. Click **OK** in the completion notifications displayed.
10. Click Save and close on the **Budget Equipment Manager** dialog.
11. On the **Budget Header Manager** screen, click **Refresh**.
12. The **Calculation Status** changes to **Required**. This status indicates that the budget must be recalculated.
13. Click **Recalculate Budget**.
14. Click **Yes** on the recalculation notification.
15. Click **OK** on the successful completion notification.
16. Click **Refresh**. The **Total Budget Cost** changes as per the actuals and the **Calculation Status** changes to **OK**.

Learning Check



Check your understanding of the workshop and ask any related questions.

Notes

4. Export the Budget

Procedure – Export a budget

If a budget is exported, it will be set to Exported automatically as part of the exported process. Therefore, manually setting the budget to Exported may not be necessary.

1. Navigate to **Budget Header Manager**.
2. Ensure a re-calculation isn't required.
3. Click **Export Budget**.
4. In the **Budget Export Wizard**, enter the **External Scenario Name** and **Version**.
5. Apply other filters as required.
6. Click **Create Export Files**.

Procedure – Export a Budget to EPF

If a budget is exported, it will be set to Exported automatically as part of the export process. Therefore, manually setting the budget to Exported may not be necessary.

1. Navigate to **Budget Header Manager**.
2. Ensure a re-calculation isn't required.
3. Click **Export Budget to Enterprise Planning Framework**.
4. In the **Export Wizard** form, select the configurations to export.
5. Click **Export**.

5. Other Budgeting Items

Procedure – Copy a Budget

1. Navigate to **Budget & Forecast Manager**.
2. Click **Copy**.
3. Enter new budget details then click **Create New Budget**.



When copying a budget, the new budget's Start Month and End Month can be changed, providing the months are within the source budget's timeframe. This is because there isn't data, within the source budget, beyond its Start Month and End Month.

Procedure – View Budget Header Details

1. Navigate to the **Budget & Forecast Manager**.
2. Double-click the budget to review.

Procedure – Create a New Actuals Budget

1. Navigate to the **Budget & Forecast Manager**.
2. Click **Add**.
3. Enter your budget details, then click **Create New Budget**.

Procedure – Run Budget Comparison Reports

1. Navigate to the **Budget & Forecast Manager**.
2. Click **Comparison Reports**.
3. Mouse over **Budget Summary**.
4. Click **Budget Comparison High-Level**.

Learning Check



Check your understanding of the workshop and ask any related questions.

Notes
