AMT – Short-term Planning

Training Manual

Copyright © 2024 RPM Software Pty Ltd. All Rights Reserved



RPM SOFTWARE – ASSET MANAGEMENT

Table of Contents

Introduction to AMT **5**

Processes **6**

Training Workshops (Job Ready Planning) **10**

1. Record and Validate Usage Readings 10
2. Capture a Defect (Backlog) 13
3. Planning 15
4. Planning Grid and Field Descriptions 17
5. Scheduling Gantt Chart and Field Descriptions 19
6. Work Order Authorisation and Validation 20
7. Work Order Authorisation Wizard 23
8. Job Ready Planning 24

Training Workshops (Scheduling) **41**

9. Definition of Scheduling 41
10. Schedule a Work Order – Advanced Planning 42
11. Schedule a Work Order – Standard Planning Mode 45
12. Refine a Work Plan 47
13. Associate Resources to a Work Order 54
14. Create a Shutdown 64
15. Export Work Plan to Microsoft Project 65
16. Communicate Plan with Production / Maintenance 66
17. Prepare Job Folders 68

Preface

The training workshops are developed to supplement instructor-led training. The guide is constructed in a way that teaches students the key functionality of the application through practical hands-on workshops. Each workshop details tasks that the student is required to complete. The workshops build on each other to help ensure a comprehensive understanding of the application is achieved at the completion of the course. Space is provided at the end of each workshop for learning checks and student notes.

Symbol Library



Note

A note for participants about the task.



Important Reminder

An important reminder for the participant about the task.



Learning Check

Check your understanding on the workshop and ask any related questions.


Course Outline

Pre-requisites	Getting Around AMT, AMT Key Concepts.
Target Audience	Store Coordinator, Short Term Planner
Nominal Duration	
Course Objectives	The objectives of the Job Ready Planning workshops are: • Plan to execute the maintenance strategy efficiently, safely and with high quality. • Manage defects (backlogs). • Minimise asset downtime. • Ensure maintenance history and labour allocations are recorded accurately. • Produce reliable maintenance and labour KPIs, and accurate maintenance costing. • Warranty management. The objectives of the Scheduling workshops are: • Ensure efficient use of resources. • Coordinate maintenance activities.

Course Objectives (cont.)	• Schedule planned maintenance efficiently, safely and with high quality. • Record labour allocations accurately.
Learning Outcomes	At the end of the course, participants will have learned to: • Usages o Open the Actual Usages screen. • Add new usages for a fleet of assets. • Enter valid and invalid readings. • Short Term Planning (standard planning) o Set planned date for work orders (Planning tab). • Set planned date for work orders. • Set Job Ready indicators for strategy tasks. o Schedule planned work orders • Review resource allocation of labour and work groups. • Check employee availability and clear up any conflicts. • Short Term Planning (advanced planning) o Term Planning Screen Review. • Understand the Planning tab. • Understand the Scheduling tab. • Understand the Shift log tab. • Understand the Equipment Down tab. • Understand the Events tab. • Understand the Workorder tab. • Understand the Backlogs tab. • Review Workorder created from Strategy.
Assessment Strategy	The completion of workshop tasks.
AMT version	8.26


Introduction to AMT

AMT is a comprehensive asset management system consisting of integrated modules as depicted below. The functionality covered by this training manual is identified by the Short-term Planning section in the diagram.

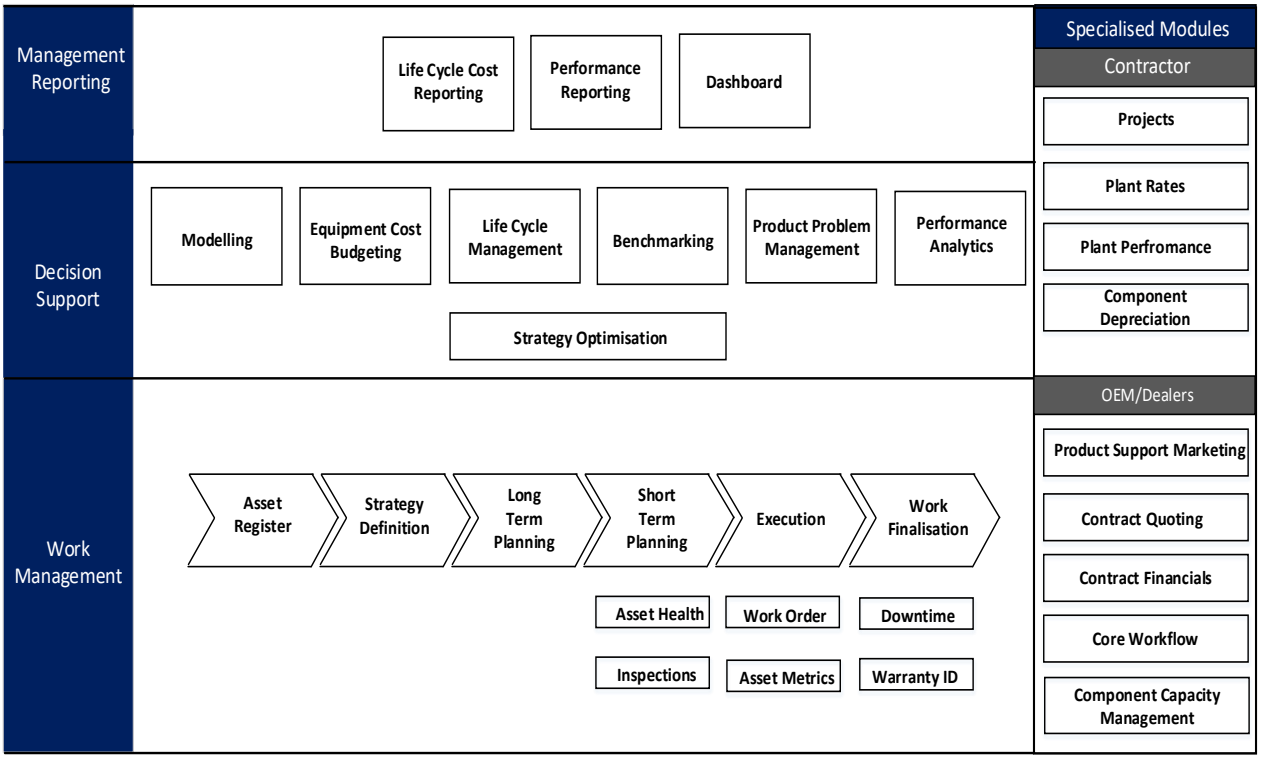

Processes

PROCESS DIAGRAM (JOB READY PLANNING)

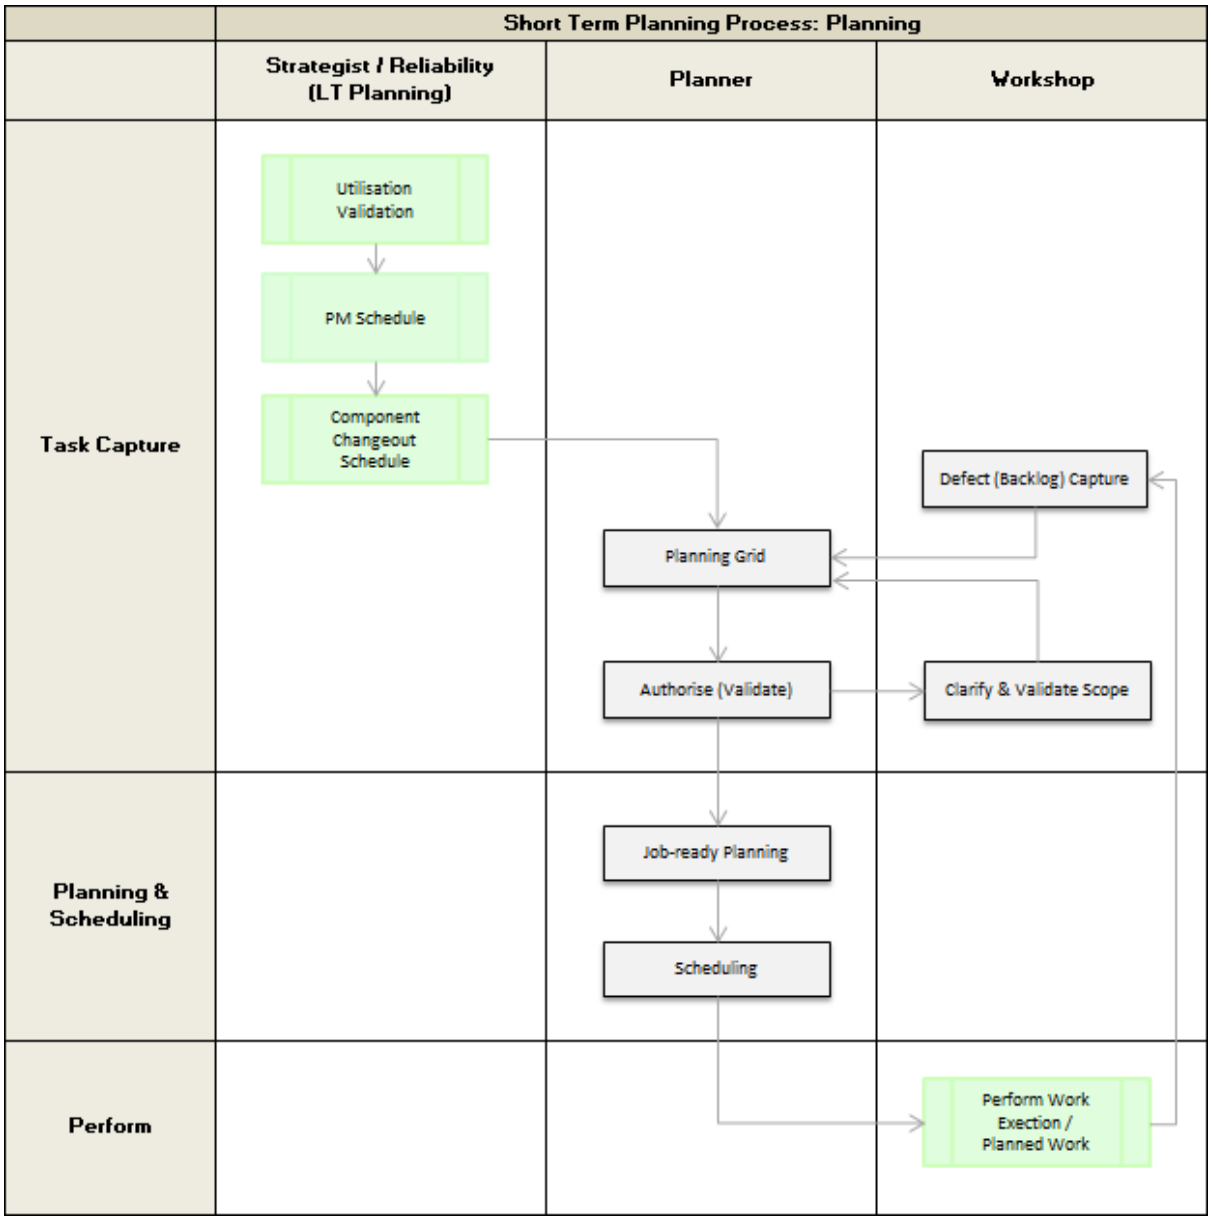

PROCESS INPUTS (JOB READY PLANNING)

The following inputs are required for this process:


1. Component changeout schedule from long-term planning.
2. PM schedule from long-term planning.
3. CBM/Condition monitoring.
4. Current backlogs.
5. Correctly updated usage readings from long-term planning.

PROCESS OUTPUTS (JOB READY PLANNING)

The following outputs can be expected from this process:

1. Open and authorised work orders.
2. Resources procured.
3. Job instructions.
4. Job readiness.

PROCESS DIAGRAM (SCHEDULING PROCESS)

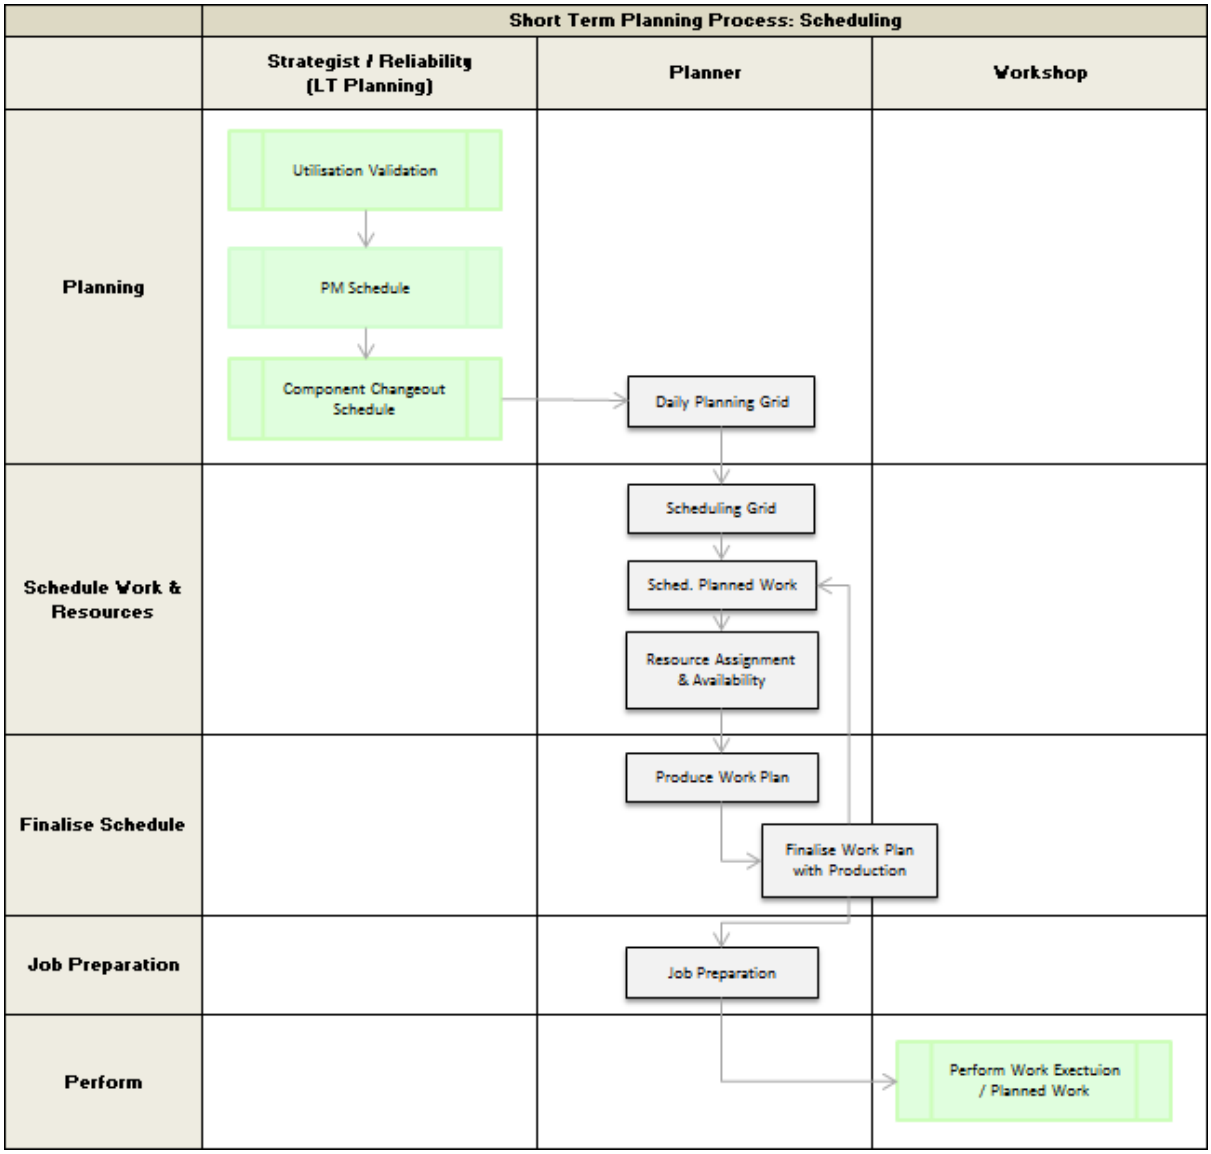

PROCESS INPUTS (SCHEDULING PROCESS)

The following inputs are required for this process:

1. Open and authorised work orders.
2. Resources procured.
3. Job instructions.
4. Job readiness.

PROCESS OUTPUTS (SCHEDULING PROCESS)

The following outputs can be expected from this process:

1. Daily work plans.
2. Agreed weekly work plans.
3. Shutdowns.
4. Job folders.
5. KPI reporting.

Training Workshops (Job Ready Planning)

1. Record and Validate Usage Readings

Procedure – Add Usage Readings

1. Under **Daily Operations > Usages & Measurements**, double-click **Record Actual Usages.**
2. Filter for a **Site**, set the date range to the last seven days and apply the filter. Sort the grid to see the most recent reading.
3. Click **Add** to record usage readings.
4. Enter the **Date** and **Time** that the reading was taken and click **Apply**.
5. Enter the new readings into the **New Reading** column. Select **Validate Readings** and make adjustments if anything is invalid.
6. Click **Save**.



You can right-click on the grid and copy the data into a spreadsheet program. In the spreadsheet, you can enter New Date Time, New Reading and/or New Offset values and paste the full grid back into AMT.

7. If the asset is linked to a usage profile that contains multiple UOMs, the **Unit of Measure** list contains multiple UOMs. However, you don't have to enter a usage for each UOM every time you want to record an actual usage.

Exercise – Add Usage Readings


1. Under **Daily Operations > Usages & Measurements**, double-click **Record Actual Usages**.
2. Set **Filters** for the required assets.
3. Set the date range.
4. Add **Usage Readings** for 5 assets.

Procedure – Validate Usage Readings

1. Validate new usage readings by clicking **Validate New Readings**.
    a. **Scenario 1 - Invalid**: Selected if the new reading is lower than the previous reading. AMT does not allow this type of entry for manual readings, but it is possible if the readings are imported.
    b. **Scenario 2 – Invalid**: Selected if the new reading is more than the projected usage in period and exceeds the threshold by more than 500%.
    c. **Exceeds Projected Usage**: Selected if the new reading is more than the projected usage in the period, but no more than the 500% threshold.

Exercise – Validate Usage Readings

1. Open **Record Actual Usages**.
2. Set **Filters** for the required assets.
3. Set date range.
4. Validate the most recently entered Usage Readings.

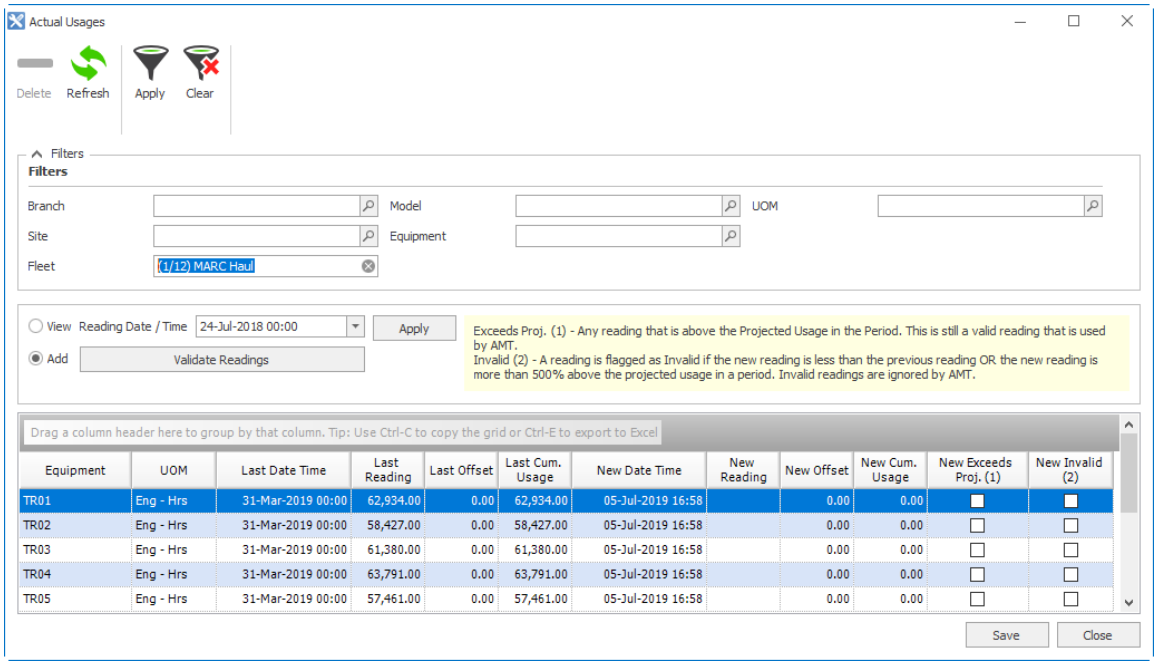


Exercise – Add an Offset Usage Readings

1. Open **Record Actual Usages**.
2. Set **Filters** for the required assets.
3. Set the date range.
4. Add an **Offset Usage Reading** for an asset.


2. Capture a Defect (Backlog)

Procedure – Add a Defect

1. Open **My Functions > Daily Operations > Quick Backlog Capture**.
2. Select an **Equipment** and any additional filters.
3. Click **OK**.
4. Click **Filter**.
5. If the backlog does not exist, continue to the next step.
6. If the backlog exists, stop this process.

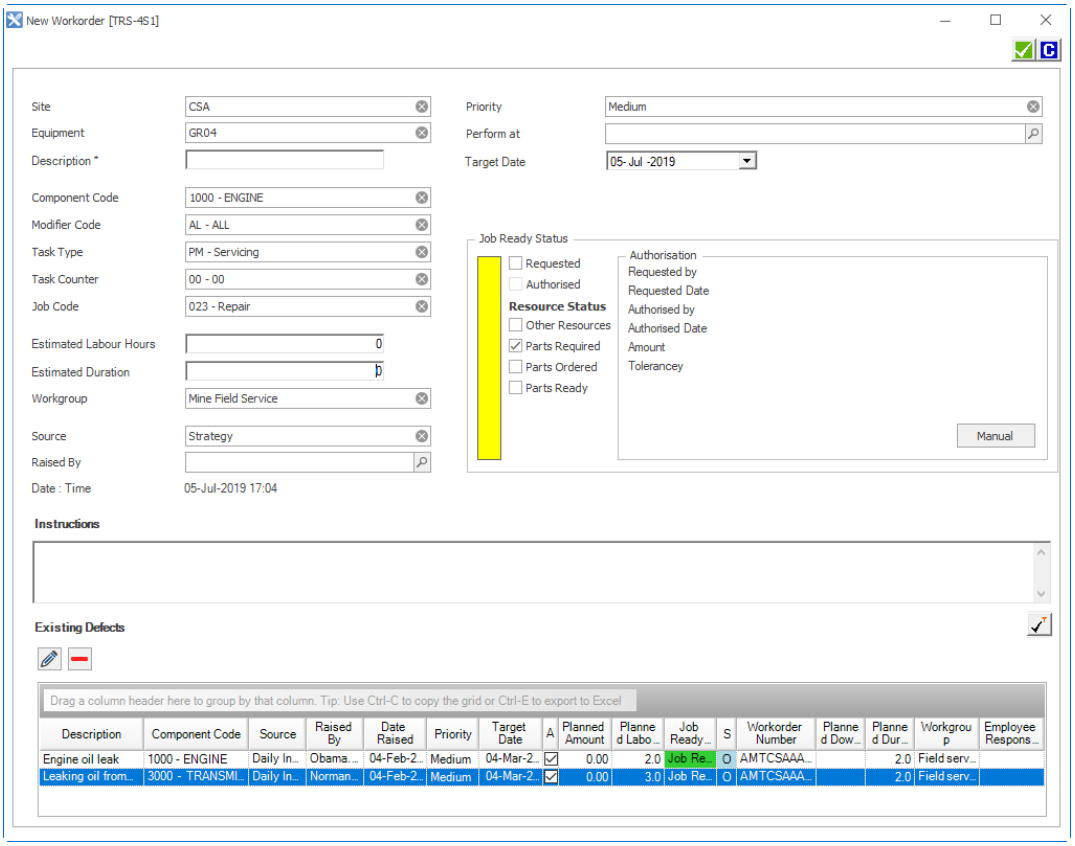

7. Complete all mandatory fields - **Description, Component Code, Task Type** and **Priority**.
8. If the job has been authorised to be performed, in the **Job Ready** section select the **Authorised** check box.
9. If you cannot authorise the work order, select **Requested**. The work order is flagged as requested. Other users with higher authority can search for work orders with requested authorisation.
10. If parts are required, select **Parts Required** in the **Job Ready** section.

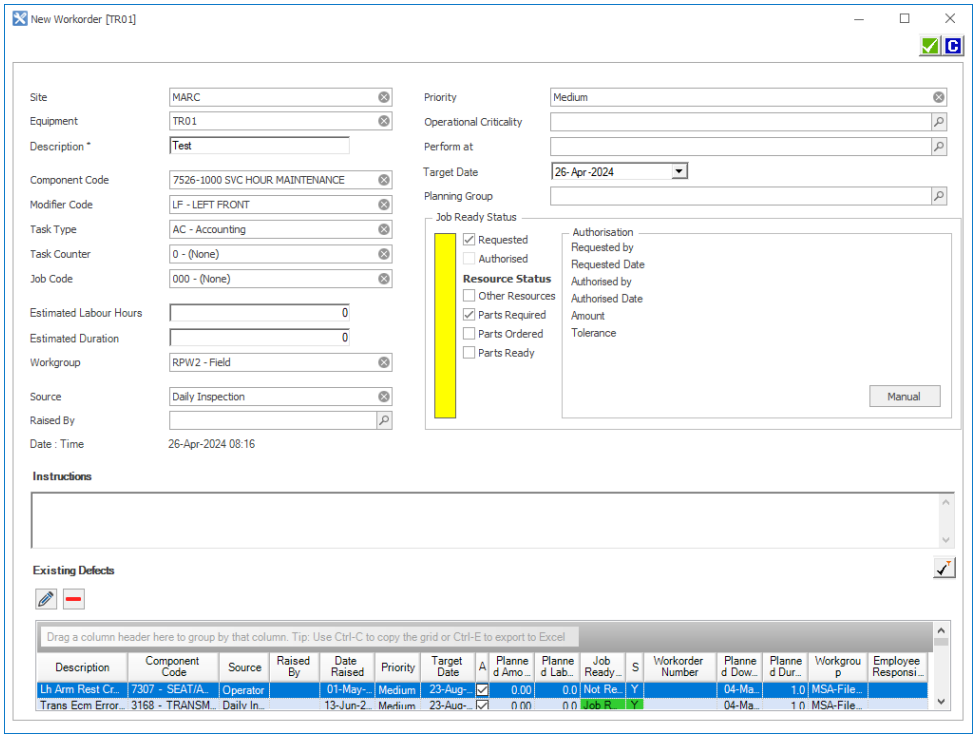

11. Enter additional information that will assist in the planning process (**Estimated Labour Hours**, **Estimated Duration**, **Perform At** and **Instructions**).
12. Click **Save**.

The majority of backlogs will have Task Type = GR (General Repair).

PM services (Task Type = PM) and component change outs (Task Type = CC) are usually strategy tasks and therefore do not need to be manually added as a backlog.

If unsure, check with the person who is responsible for the asset's maintenance strategy.

If you select the OH&S value (which is flagged in the OH&S system table as an "Auditable Record") in the work order, certain fields are disabled. This feature is designed to be used to lock work orders. The fields can be re-enabled by selecting a different OH&S entry.

*More information can be captured in AMT for a backlog; to do so, in **Planning**, search for the backlog task, open it and add the additional information.*


Exercise – Add a Defect (Backlog)

1. Add a defect (backlog) using the **Quick Backlog Capture** screen.
2. Verify that the backlog exists in AMT (use Backlog reports).

3. Planning

The **Planning** form helps the various stakeholders in the planning process to perform all AMT-related planning tasks.

The **Planning** form contains several tabs - **Planning** grid, **Scheduling** Gantt, **Shiftlog**, **Equipment Down**, **Events**, **Workorders** and **Backlogs**.

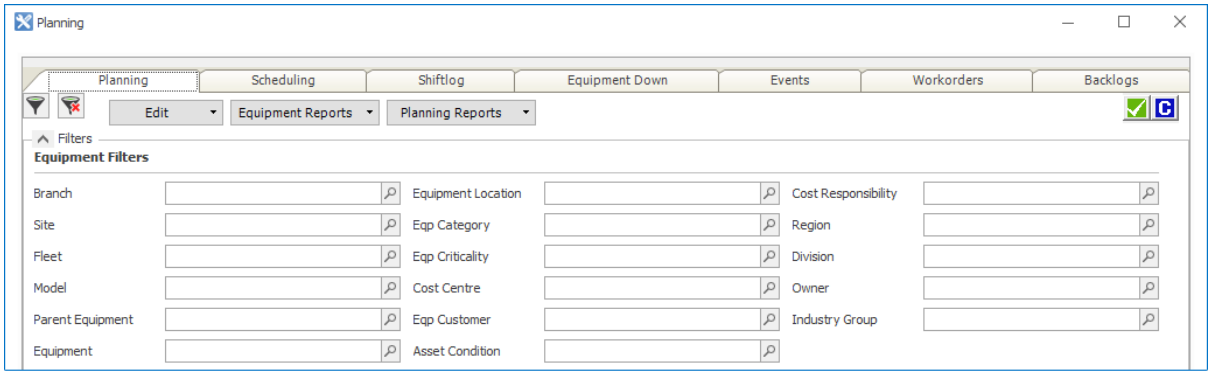

- **Planning grid**: The Planning grid shows all planning work orders – both strategy work orders (components and PMs) and defects.
- **Scheduling Gantt**: The Scheduling Gantt chart graphically represents a plan. You can manipulate the plan, and drag to allocate additional backlogs, workgroups and employees to the plan.
- **Shiftlog**: The Shiftlog shows events within a specified date range and is designed to quickly update the event status and create unplanned events with only the essential information. This is covered in-depth in the Work Execution and Finalisation training.
- **Equipment Down**: The Equipment Down screen graphically represents the live status of assets. Over a specified period of time, all yet-to-start, in-progress and completed events can be seen in a timeline.
- **Events**: You can create detailed events with their respective work order in this tab.
- **Workorders**: Review all planning work orders with additional details such as admin alerts.
- **Backlogs**: Review all planning work orders with the ability to generate backlog-specific reports.


Learning Check



Check your understanding of the workshop and ask any related questions.

Notes

4. Planning Grid and Field Descriptions

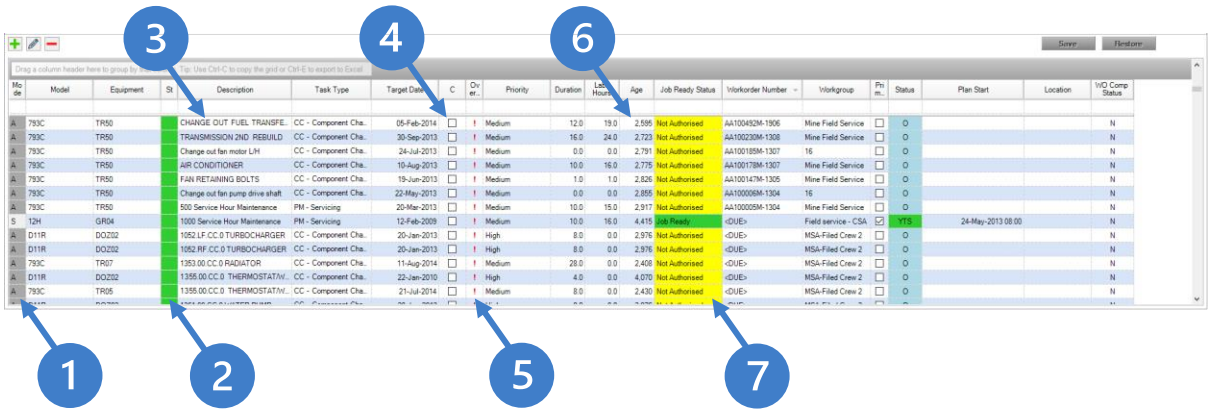

No.	Column	Description
1	Mode	**S** = Standard Planning Equipment **A** = Advance Planning Equipment
2	Strategy	**Green** = Strategy Task **Yellow** = CBM Follow Up **Blue** = General Defect
3	Description	Work order description
4	Confirmed	Checked if Confirmed by Strategy
5	Overdue	**!** = Overdue
6	Age	Time that Backlog has been in the system
7	Job Ready Status	**Yellow** = Not Authorised **Red** = Parts Not Ordered **Blue** = Parts Ordered not delivered **Green** = Job Ready

AMT has two planning modes:

- **Standard** – suitable for applications where downtime is not captured such as general line, PM contracts, process plants, and workshops.
- **Advanced** – mining-focused and suitable for downtime capture applications as it integrates with the **Equipment Status** module.

The **Planning** grid is used to manage planned work orders for both planning modes.

Planning Grid Columns


Column	Key	Description
Scheduling Mode	S A	**S** = Standard planning. **A** = Advanced planning.
Strategy		Strategy task. Condition monitoring intervention. Non-strategy and non-CBM task.
Target Date		The performed date set in the work order.
Confirmed		Strategy confirmed. This box is selected if the strategy date/usage (that is, target date/used) was flagged as locked in the **Long-Term Planning** screen.
Overdue	!	Future occurrences (beyond the next occurrence).
Duration		Number of hours required to perform the work order (elapsed time).
Labour Hours		Number of labour hours required to perform the work order.
Age		Number of days the work order has been in the planning window.
Job Ready Status		Captured, not authorised. Authorised, parts required. Authorised, parts ordered. Ready, authorised and parts ordered.
Workorder Number		Work order number settlement.
Work Group		Group scheduled to perform the work.
Primary		Primary task of event (Advanced Planning mode).
Status		**Outstanding** = Yet to be planned. **Yet To Start** = Work order has been planned. **In Progress** = Work order is currently being performed. **Completed** = Work order is finished.
Plan Start		Planned date when the work order will be performed.
Location		Location where the work order will be performed.



Double-click a work order to open it. If a work order is part of a planned event (that is, it has been scheduled) it will open the event first. The event shows all work orders and you can open the work order from there.

5. Scheduling Gantt Chart and Field Descriptions

This is the visual control that triggers the daily planning process into action for these strategy tasks.

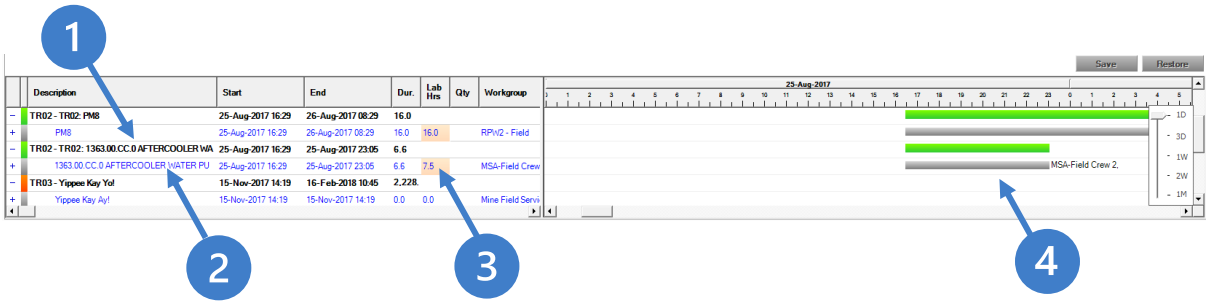

1	The event is shown in **bold** under the equipment.
2	The next level is the work order shown in blue.
3	If the downtime and/or uptime of a work order or operation does not fall within the planned downtime, red shading displays.
4	In this example, grey bars for the labour resources do not appear even though there are labour hours. This is because the operation's duration = 0.


6. Work Order Authorisation and Validation


Procedure – Advanced Authorisation

Each individual work order can be manually authorised. To authorise a single work order:


1. Open **Daily Planning** > **Workorder Authorisation**.
2. Filter and find the required work order.
3. Double-click the work order. The **Edit Workorder** screen opens at the **Base Details** tab.
4. In the **Job Ready Status** section select the **Authorised** check box.

   This is an automated authorisation and correlates to your authorisation level previously set up in your user profile.

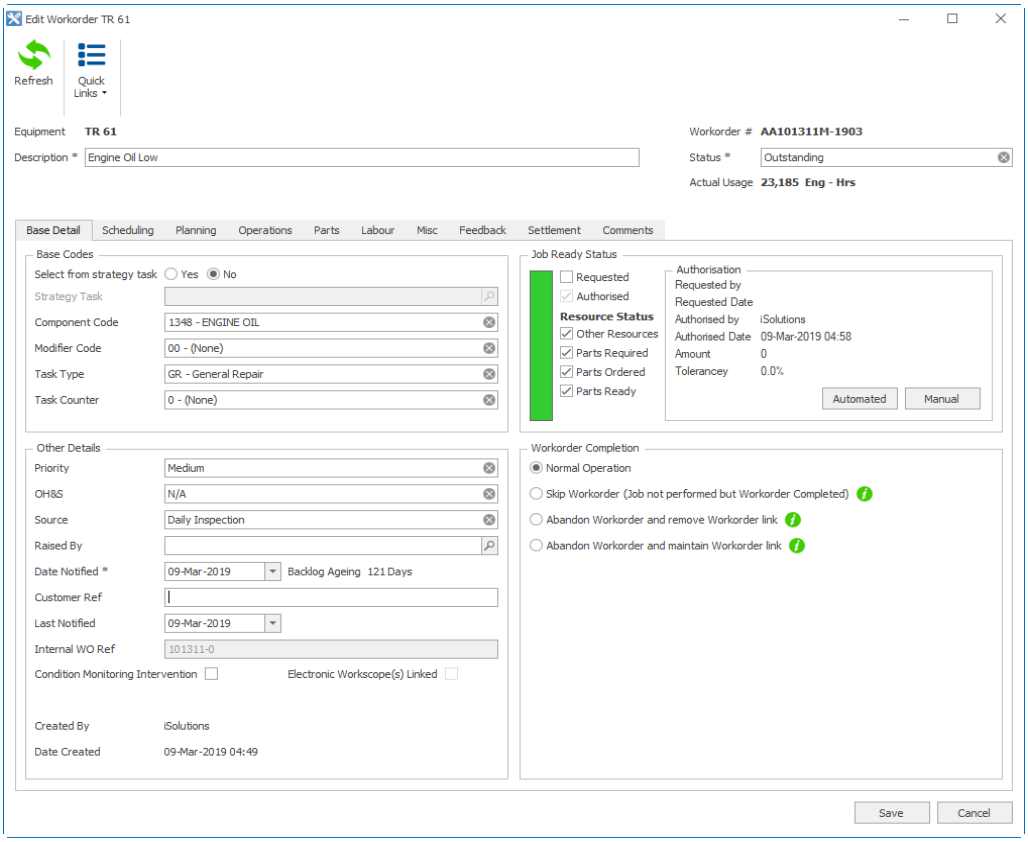

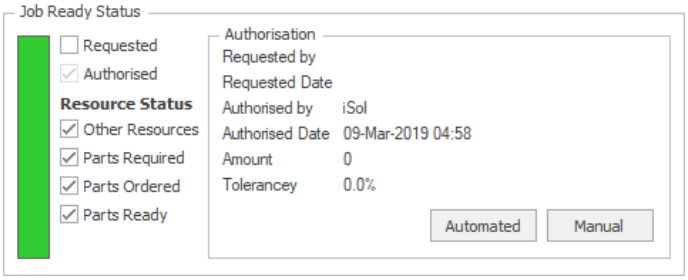

5. Click **Manual Authorisation** (**A_E**) to authorise the cost of a single job to a certain amount within a system-defined sign-off limit.

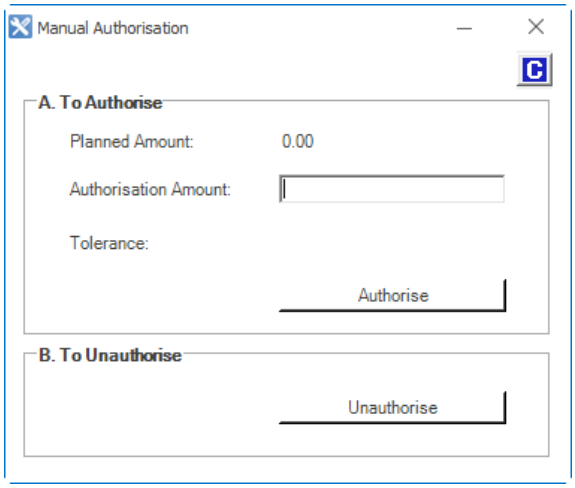

6. Click **Authorise**.

Learning Check



Check your understanding of the workshop and ask any related questions.

Notes

7. Work Order Authorisation Wizard

Procedure – Work Order Authorisation Wizard

1. Open **My Functions > Daily Planning > Workorder Authorisation**.
2. Enter filter criteria and click **Apply Filter**.



*The **Branch** and **Site** filters are now multi-select.*

3. Navigate to **Planning**.
4. Select the work orders that you want to authorise, and click **Apply Authorisation**.
5. AMT authorises the selected work orders based on your authorisation limits.



*By default, the authorised work order drops off the grid unless the authorised check box (flag) is set to **All**. Your authorisation limit is set in your user account. The AMT System Administrator can change your authorisation limit.*


Exercise – Authorise Work Orders (Advanced Mode)

1. Use the **A_E** button in the work order to authorise a work order.
2. Review the work orders to be authorised in the **Authorisation Wizard**.

8. Job Ready Planning

Procedure – Enter Required Parts into the Work Order

1. Open **My Functions > Daily Planning > Planning**.
2. Click the **Workorders** tab.
3. Set **Filters** for the assets.
4. Set the **Workorder Status**:
    a. Yet to Start (**YTS**).
    b. In Progress (**IP**).

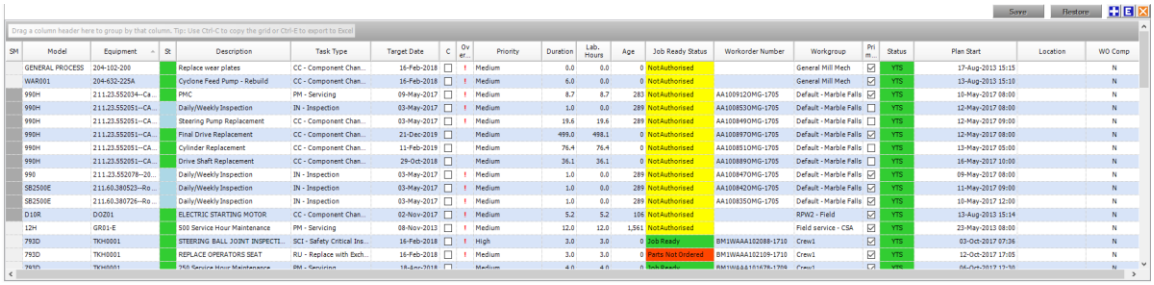

5. Click **Apply Filters**.
6. Double-click the work order that you want to add parts to.
7. Click the **Parts** tab.
8. Click **Refresh**.

*If no operations display on the parts grid, go to the Operations tab and click **Show Operations**. If no operations exist, add the operations and refresh the **Operations** screen.*

Procedure – Add Parts Manually

1. Highlight the operation you want to add parts to.
2. Click **Add**.
3. Enter the parts details directly into the grid.

Procedure – Add Parts Manually with Lookup

1. Highlight the operation you want to add parts to.
2. Click **Lookup Parts Details**.
3. Select the required parts.

Procedure – Add Parts from Clipboard

1. In Excel, select the parts to be copied and press **Ctrl+C**.
2. In the Work Order Editor, click **Edit > Add Parts - From Clipboard**.

   Use the drop-down menus at the top of each column to specify the AMT data for the columns.



*The minimum fields required for the functionality to work are **Planned Quantity**, with either **Part Number** or **Part Description**.*

3. Click **OK** to validate the data. If there are validation errors, the cells in error are highlighted.
4. Fix the errors in the source and re-copy the data.
5. Click **Refresh** to reload the corrected data, then click **OK**.



Once the parts data passes validation it is appended to the work order parts grid as new parts. The functionality does not try to match existing parts and update them.

Procedure – Import Parts from Standard Job

1. Highlight the operation you want to add parts to.
2. Click **Import Standard Job**.




If a strategy work order has a standard job linked to it, AMT automatically populates it with the standard job parts and labour details.

3. Set **Filters**.
4. Click **Apply Filters**.
5. Double-click on the standard job you want to raise.
6. You are asked if you want to override operations from standard jobs. All parts already under that operation will be overridden.
7. Add additional parts after importing the parts from a standard job.
8. When all parts are entered, click **Refresh**.

Procedure – Add Parts from the AMT Parts Table

1. On the **Parts** tab, highlight the operation you want to add parts to.
2. Click **Edit** and select **Add Parts – From AMT Parts Table**. The **Parts** table opens.
3. Refine the parts search and click **Apply Filters**.
4. Drag the appropriate part under the desired operation.

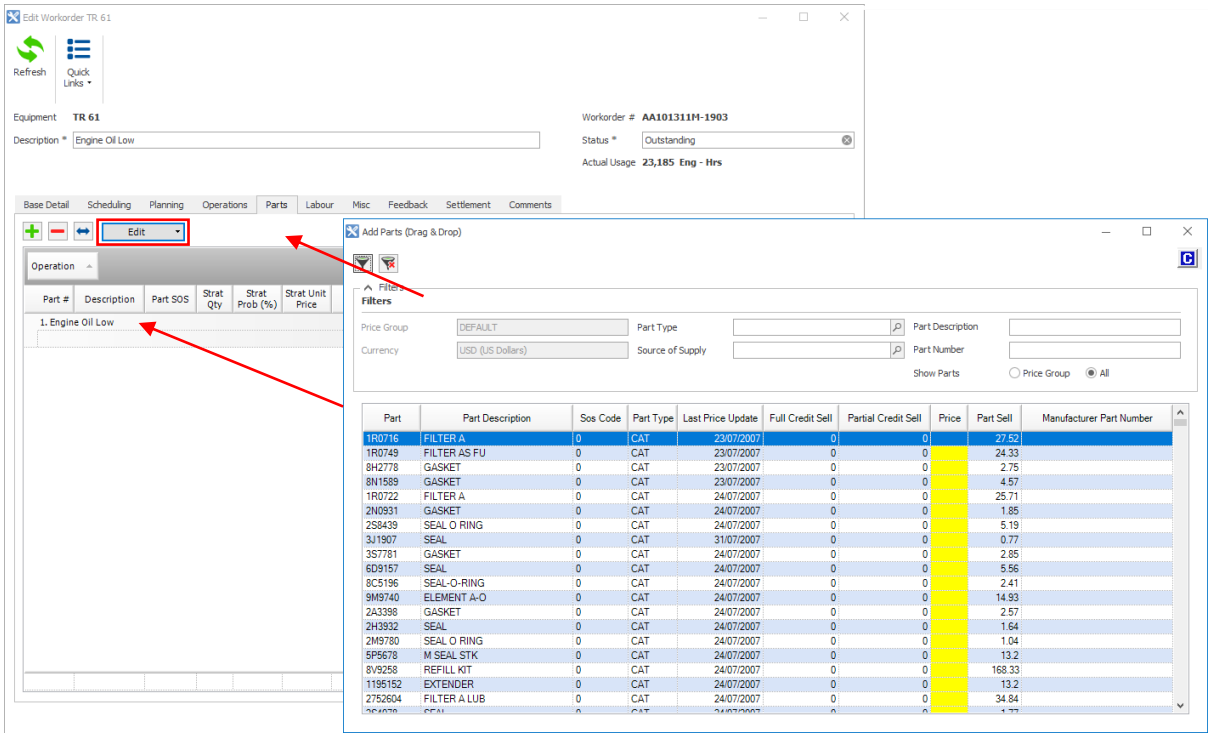

Edit Workorder TR 61
Refresh
Quick Links
Equipment TR 61
Description * Engine Oil Low
Workorder # AA101311M-1903
Status * Outstanding
Actual Usage 23,185 Eng - Hrs
Base Detail
Scheduling
Planning
Operations
Parts
Labour
Misc
Feedback
Settlement
Comments
Edit
Operation
Part #
Description
Part SOS
Strat Qty
Strat Prob (%)
Strat Unit Price
1. Engine Oil Low
Add Parts (Drag & Drop)
Filters
Price Group DEFAULT
Currency USD (US Dollars)
Part Type
Source of Supply
Part Description
Part Number
Show Parts
Price Group
All
Part
Part Description
Sos Code
Part Type
Last Price Update
Full Credit Sell
Partial Credit Sell
Price
Part Sell
Manufacturer Part Number
1R0716 FILTER A 0 CAT 23/07/2007 0 0 27.52
1R0749 FILTER AS FU 0 CAT 23/07/2007 0 0 24.33
8H2778 GASKET 0 CAT 23/07/2007 0 0 2.75
8N1589 GASKET 0 CAT 23/07/2007 0 0 4.57
1R0722 FILTER A 0 CAT 24/07/2007 0 0 25.71
2N0931 GASKET 0 CAT 24/07/2007 0 0 1.85
2S8439 SEAL O RING 0 CAT 24/07/2007 0 0 5.19
3J1907 SEAL 0 CAT 31/07/2007 0 0 0.77
3S7781 GASKET 0 CAT 24/07/2007 0 0 2.85
6D9157 SEAL 0 CAT 24/07/2007 0 0 5.56
8C5196 SEAL-O-RING 0 CAT 24/07/2007 0 0 2.41
9M9740 ELEMENT A-O 0 CAT 24/07/2007 0 0 14.93
2A3398 GASKET 0 CAT 24/07/2007 0 0 2.57
2H3932 SEAL 0 CAT 24/07/2007 0 0 1.64
2M9780 SEAL O RING 0 CAT 24/07/2007 0 0 1.04
5P5678 M SEAL STK 0 CAT 24/07/2007 0 0 13.2
8V9258 REFILL KIT 0 CAT 24/07/2007 0 0 168.33
1195152 EXTENDER 0 CAT 24/07/2007 0 0 13.2
2752604 FILTER A LUB 0 CAT 24/07/2007 0 0 34.84

Procedure – Add Parts Purchase History

1. On the **Parts** tab, highlight the operation you want to add parts to.
2. Click **Edit** > **Add Parts - Purchase History** to open the **Purchase History** table.
3. Select the check box of the required part and click **Save**.

> *Every time a work order is completed, the "planned parts" for that work order are copied to a history table. This method is useful when you know that you've previously done the same job.*

4. Select the parts that are required.

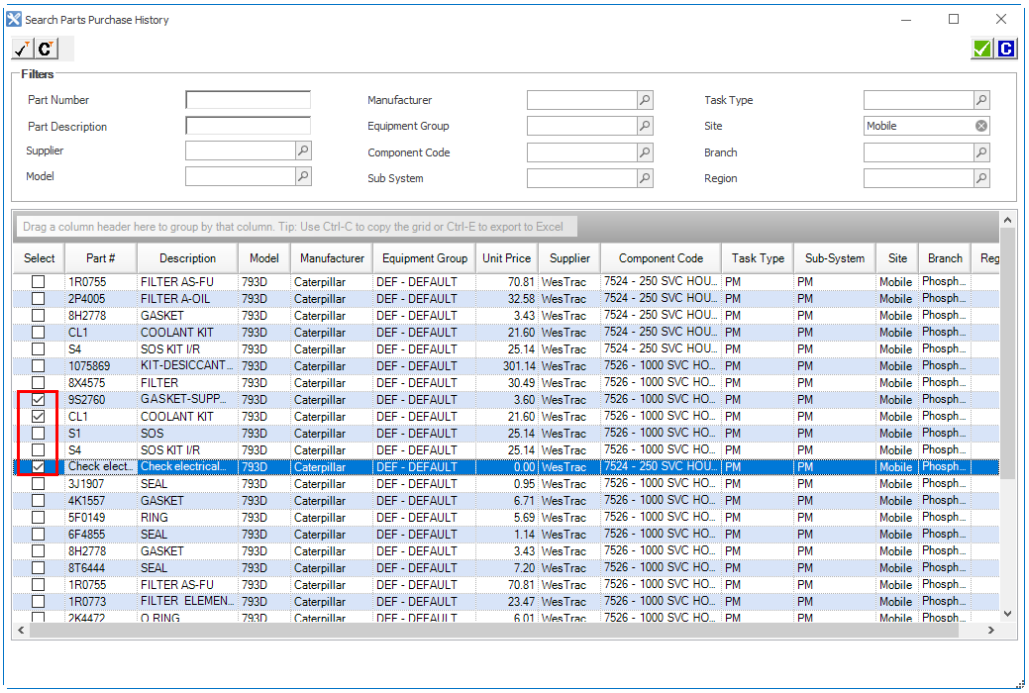


Select	Part #	Description	Model	Manufacturer	Equipment Group	Unit Price	Supplier	Component Code	Task Type	Sub-System	Site	Branch
☐	1R0755	FILTER AS-FU	793D	Caterpillar	DEF - DEFAULT	70.81	WesTrac	7524 - 250 SVC HOU...	PM	PM	Mobile	Phosph...
☐	2P4005	FILTER A-OIL	793D	Caterpillar	DEF - DEFAULT	32.58	WesTrac	7524 - 250 SVC HOU...	PM	PM	Mobile	Phosph...
☐	8H2778	GASKET	793D	Caterpillar	DEF - DEFAULT	3.43	WesTrac	7524 - 250 SVC HOU...	PM	PM	Mobile	Phosph...
☐	CL1	COOLANT KIT	793D	Caterpillar	DEF - DEFAULT	21.60	WesTrac	7524 - 250 SVC HOU...	PM	PM	Mobile	Phosph...
☐	S4	SOS KIT I/R	793D	Caterpillar	DEF - DEFAULT	25.14	WesTrac	7524 - 250 SVC HOU...	PM	PM	Mobile	Phosph...
☐	1075869	KIT-DESICCANT...	793D	Caterpillar	DEF - DEFAULT	301.14	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☐	8X4575	FILTER	793D	Caterpillar	DEF - DEFAULT	30.49	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☑	9S2760	GASKET-SUPP...	793D	Caterpillar	DEF - DEFAULT	3.60	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☑	CL1	COOLANT KIT	793D	Caterpillar	DEF - DEFAULT	21.60	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☐	S1	SOS	793D	Caterpillar	DEF - DEFAULT	25.14	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☐	S4	SOS KIT I/R	793D	Caterpillar	DEF - DEFAULT	25.14	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☑	Check elect...	Check electrical...	793D	Caterpillar	DEF - DEFAULT	0.00	WesTrac	7524 - 250 SVC HOU...	PM	PM	Mobile	Phosph...
☐	3J1907	SEAL	793D	Caterpillar	DEF - DEFAULT	0.95	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☐	4K1557	GASKET	793D	Caterpillar	DEF - DEFAULT	6.71	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☐	5F0149	RING	793D	Caterpillar	DEF - DEFAULT	5.69	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☐	6F4855	SEAL	793D	Caterpillar	DEF - DEFAULT	1.14	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☐	8H2778	GASKET	793D	Caterpillar	DEF - DEFAULT	3.43	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☐	8T6444	SEAL	793D	Caterpillar	DEF - DEFAULT	7.20	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☐	1R0755	FILTER AS-FU	793D	Caterpillar	DEF - DEFAULT	70.81	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☐	1R0773	FILTER ELEMEN...	793D	Caterpillar	DEF - DEFAULT	23.47	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...
☐	2K4472	O RING	793D	Caterpillar	DEF - DEFAULT	6.01	WesTrac	7526 - 1000 SVC HO...	PM	PM	Mobile	Phosph...

5. Click **Save** when all of the parts have been selected.

Procedure – Generate the Purchase Order / Internal Requisition Number

1. Under **Daily Planning**, double-click **Planning**.
2. Click the **Workorders** tab.
3. Set **Filters** for the assets.
4. Set the workorder **Status**:
    a. Yet to Start (**YTS**).
    b. In Progress (**IP**).

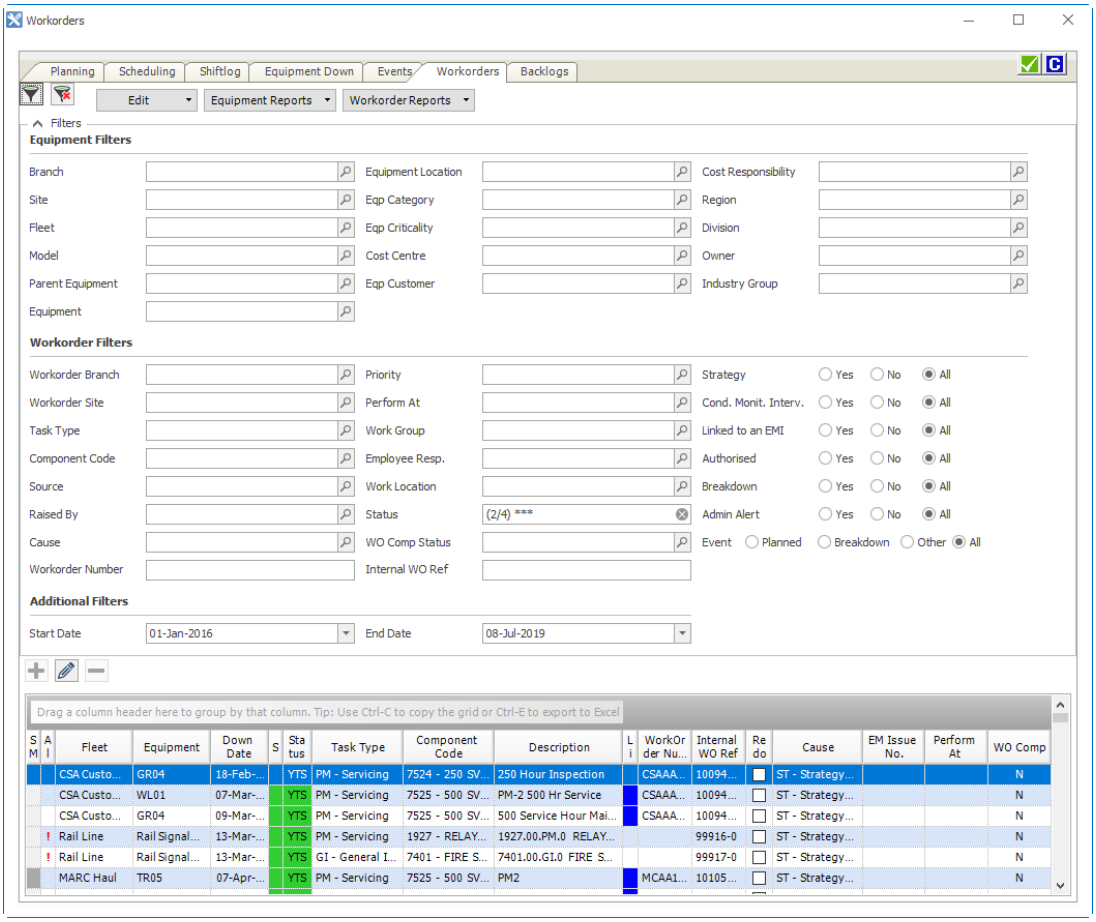


SM	AI	Fleet	Equipment	Down Date	S	Status	Task Type	Component Code	Description	Li	WorkOrder Nu...	Internal WO Ref	Redo	Cause	EM Issue No.	Perform At	WO Comp
		CSA Custo...	GR04	18-Feb-...		YTS	PM - Servicing	7524 - 250 SV...	250 Hour Inspection		CSAAA...	10094...		ST - Strategy...			N
		CSA Custo...	WL01	07-Mar-...		YTS	PM - Servicing	7525 - 500 SV...	PM-2 500 Hr Service		CSAAA...	10094...		ST - Strategy...			N
		CSA Custo...	GR04	09-Mar-...		YTS	PM - Servicing	7525 - 500 SV...	500 Service Hour Mai...		CSAAA...	10094...		ST - Strategy...			N
	!	Rail Line	Rail Signal...	13-Mar-...		YTS	PM - Servicing	1927 - RELAY...	1927.00.PM.0 RELAY...			99916-0		ST - Strategy...			N
	!	Rail Line	Rail Signal...	13-Mar-...		YTS	GI - General I...	7401 - FIRE S...	7401.00.GI.0 FIRE S...			99917-0		ST - Strategy...			N
		MARC Haul	TR05	07-Apr-...		YTS	PM - Servicing	7525 - 500 SV...	PM2		MCAA1...	10105...		ST - Strategy...			N

5. Click **Apply Filters**.
6. Double-click on the relevant work order.
7. Click the **Parts** tab.

If no parts show up on the parts grid, refer to pages 23, 24 and 25 of this document.

Procedure – Assign a Supplier Manually

1. On the **Edit Workorder** screen, click the **Parts** tab.
2. In the **Supplier** column, click **Search**.

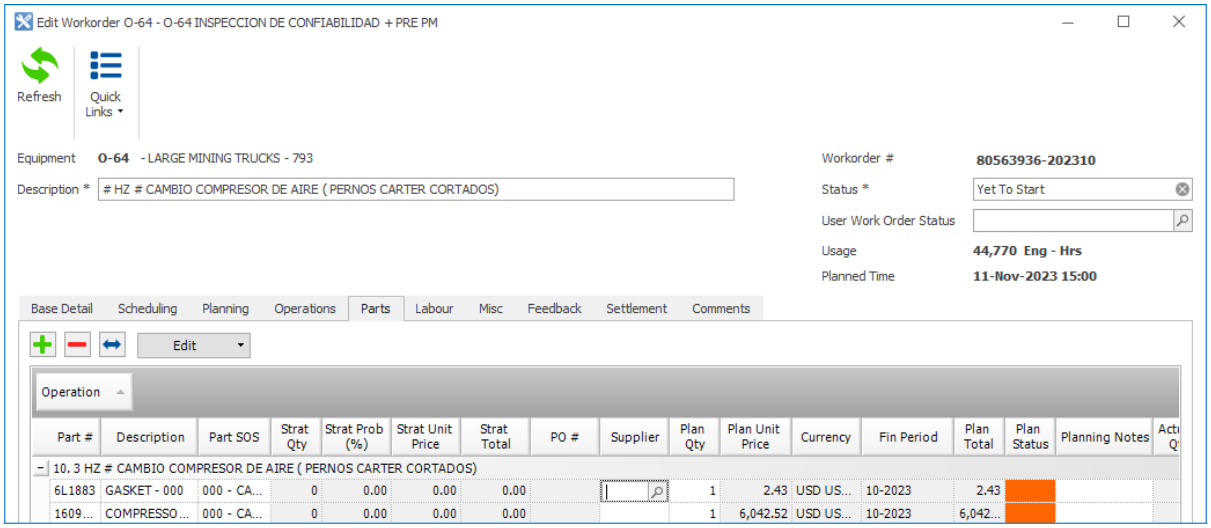

3. Select the appropriate supplier.
4. Click **Refresh**.


Procedure – Assign Suppliers Automatically

1. In the **Edit** list, select **Assign Supplier**.
2. Click **Refresh**.
3. AMT automatically assigns the supplier by looking at the purchase history for the asset involved.



The assigned supplier can be edited afterwards.

4. Click the **Planning** tab.
5. Assign a purchase order number for each supplier in the **Purchase Order** column. You can either enter the number manually or select **Assign Number**.



6. Click **Refresh**.
7. Automatically generated purchase order numbers can be overridden with another reference number.


Procedure – Send off the Purchase Orders / Parts Requisitions

1. After the purchase order number has been assigned, click **Refresh**.
2. Select the appropriate option to send the purchase order by email or by printing a hardcopy.

*If no operations display on the parts grid, go to the **Operations** tab and click **Show Operations**; if no operations exist, add the required operations.*

Procedure – Reporting the Planning Status of Parts

1. Under **Daily Planning > Daily Planning Reports**, double-click **Planning Status**.
2. Click the relevant filters and generate the report.

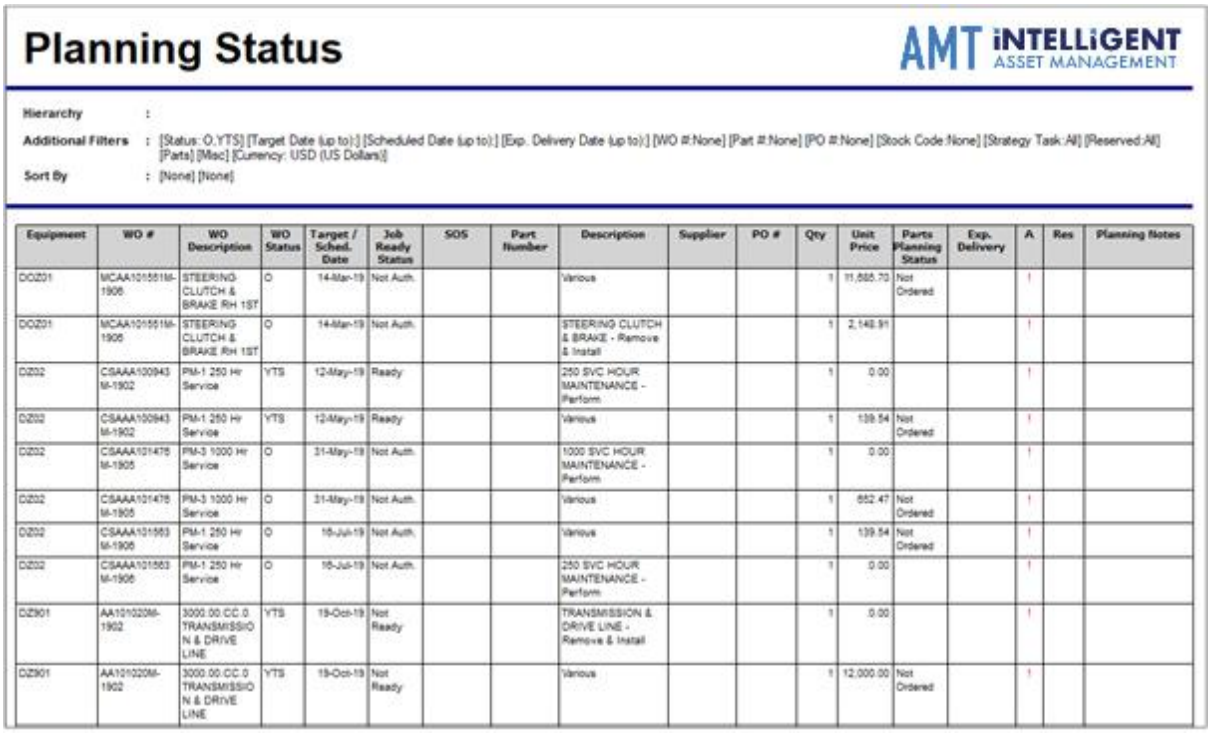

Planning Status

AMT INTELLIGENT ASSET MANAGEMENT

Hierarchy :

Additional Filters : [Status: O,YTS] [Target Date (up to):] [Scheduled Date (up to):] [Exp. Delivery Date (up to):] [WO #:None] [Part #:None] [PO #:None] [Stock Code:None] [Strategy Task:All] [Reserved:All] [Parts] [Misc] [Currency: USD (US Dollars)]


Sort By : [None] [None]

Equipment	WO #	WO Description	WO Status	Target / Sched. Date	Job Ready Status	SOS	Part Number	Description	Supplier	PO #	Qty	Unit Price	Parts Planning Status	Exp. Delivery	A	Res	Planning Notes
DOZ01	MCAA1015516M-1906	STEERING CLUTCH & BRAKE RH 1ST	O	14-Mar-19	Not Auth.			Various			1	11,585.70	Not Ordered		!		
DOZ01	MCAA1015516M-1906	STEERING CLUTCH & BRAKE RH 1ST	O	14-Mar-19	Not Auth.			STEERING CLUTCH & BRAKE - Remove & Install			1	2,148.91			!		
DZ02	CSAAA100943M-1902	PM-1 250 Hr Service	YTS	12-May-19	Ready			250 SVC HOUR MAINTENANCE - Perform			1	0.00			!		
DZ02	CSAAA100943M-1902	PM-1 250 Hr Service	YTS	12-May-19	Ready			Various			1	139.54	Not Ordered		!		
DZ02	CSAAA101475M-1905	PM-3 1000 Hr Service	O	31-May-19	Not Auth.			1000 SVC HOUR MAINTENANCE - Perform			1	0.00			!		
DZ02	CSAAA101475M-1905	PM-3 1000 Hr Service	O	31-May-19	Not Auth.			Various			1	552.47	Not Ordered		!		
DZ02	CSAAA101583M-1906	PM-1 250 Hr Service	O	16-Jul-19	Not Auth.			Various			1	139.54	Not Ordered		!		
DZ02	CSAAA101583M-1906	PM-1 250 Hr Service	O	16-Jul-19	Not Auth.			250 SVC HOUR MAINTENANCE - Perform			1	0.00			!		
DZ901	AA1010206M-1902	3000.00.CC.0 TRANSMISSION & DRIVE LINE	YTS	19-Oct-19	Not Ready			TRANSMISSION & DRIVE LINE - Remove & Install			1	0.00			!		
DZ901	AA1010206M-1902	3000.00.CC.0 TRANSMISSION & DRIVE LINE	YTS	19-Oct-19	Not Ready			Various			1	12,000.00	Not Ordered		!		


Procedure – Assign Labour to a Work Order – Employee Level

Ensure the **Site** is set to **Employee Level Resourcing**.


1. Navigate to **System Administration > System Tables > Organisation**. Double-click **Site Administration**.
2. Click **Apply Filters**.
3. Double-click your site to open the **Edit Site** screen.
4. Tick **Enable Employee Level Resourcing**.
5. Open a work order in **Planning** or **Advanced Planning** and navigate to the **Labour** tab.
6. The work order must have at least ONE operation to be able to assign labour to it. Click **Add** on the **Operation** tab to create operations.

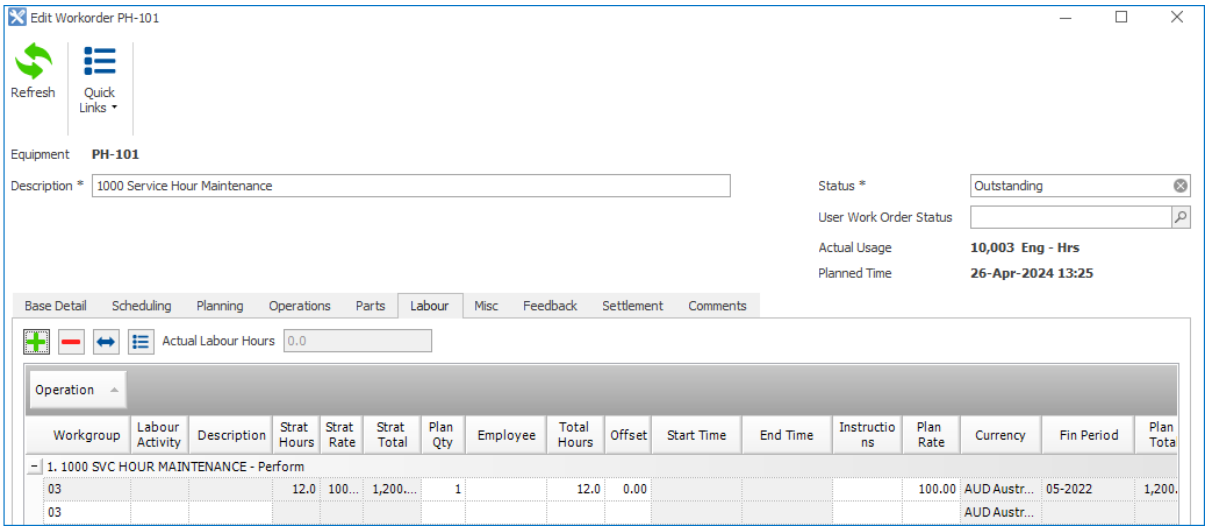

7. To add employees to an operation, highlight the operation on the **Labour** tab and click **Quick Links > Assign Employees**. The **Employee Availability** window opens.
8. The **Employee Availability** window displays the availability status of each employee to help with employee scheduling.
9. To assign an employee to an operation, select the check box next to the employee's name and save.

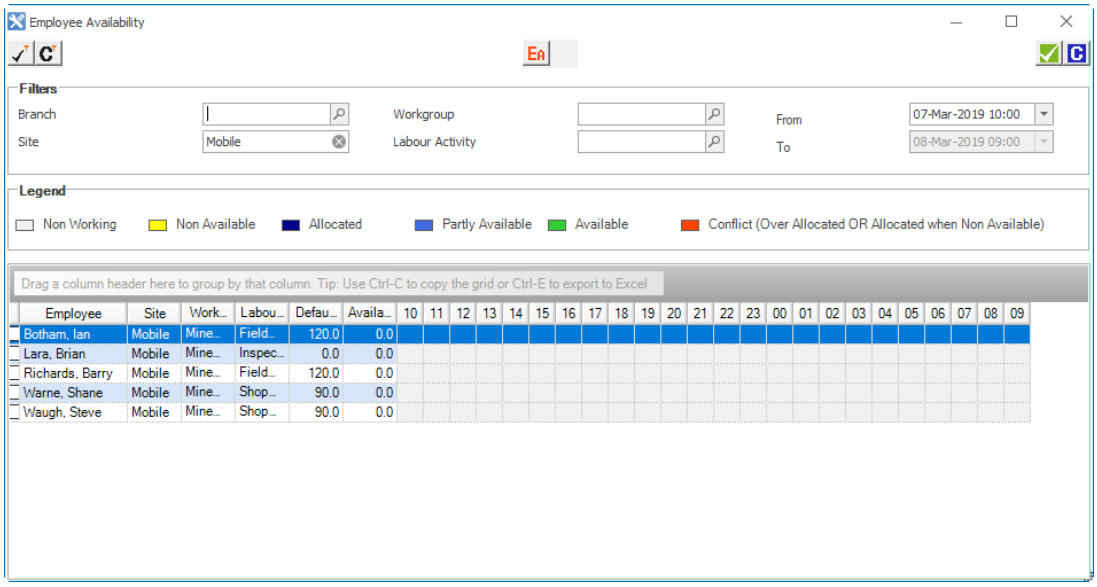
Employee Availability
Filters
Branch
Site
Mobile
Workgroup
Labour Activity
From
07-Mar-2019 10:00
To
08-Mar-2019 09:00
Legend
Non Working
Non Available
Allocated
Partly Available
Available
Conflict (Over Allocated OR Allocated when Non Available)
Drag a column header here to group by that column. Tip: Use Ctrl-C to copy the grid or Ctrl-E to export to Excel
Employee
Site
Work...
Labou...
Defau...
Availa...
10 11 12 13 14 15 16 17 18 19 20 21 22 23 00 01 02 03 04 05 06 07 08 09
Botham, Ian Mobile Mine... Field... 120.0 0.0
Lara, Brian Mobile Mine... Inspec... 0.0 0.0
Richards, Barry Mobile Mine... Field... 120.0 0.0
Warne, Shane Mobile Mine... Shop... 90.0 0.0
Waugh, Steve Mobile Mine... Shop... 90.0 0.0

10. Click **Employee Allocation Report** under the **Quick Links** list to run the report.

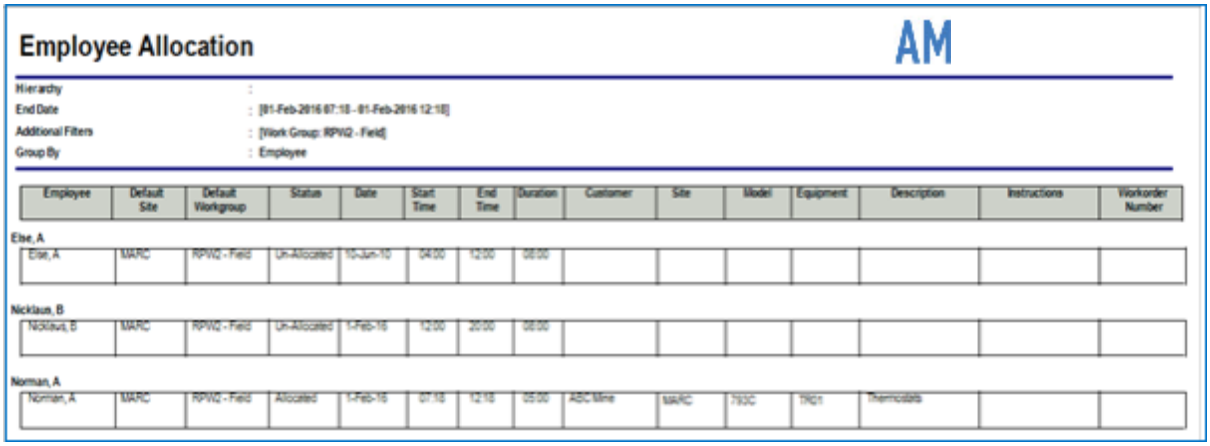


11. After adding employees to an operation, check for scheduling conflicts by clicking **Show Scheduling Conflicts** under the **Quick Links** list.

Conflicts display in red.


12. We recommend that you use the **Employee Resource Availability** and **Fill Report** to help with employee scheduling.
13. This report shows **surpluses** and **deficiencies** in available employee rosters. A negative number indicates an over-allocation. A positive number indicates that there is a resource surplus.

Procedure – Attaching Standard Work Order Instructions

1. Under **Daily Planning**, double-click **Planning**.
2. Click the **Workorders** tab.
3. Set **Filters** for the assets.
4. Set the **Workorder Status**:
    a. Yet to Start (**YTS**).
    b. In Progress (**IP**).

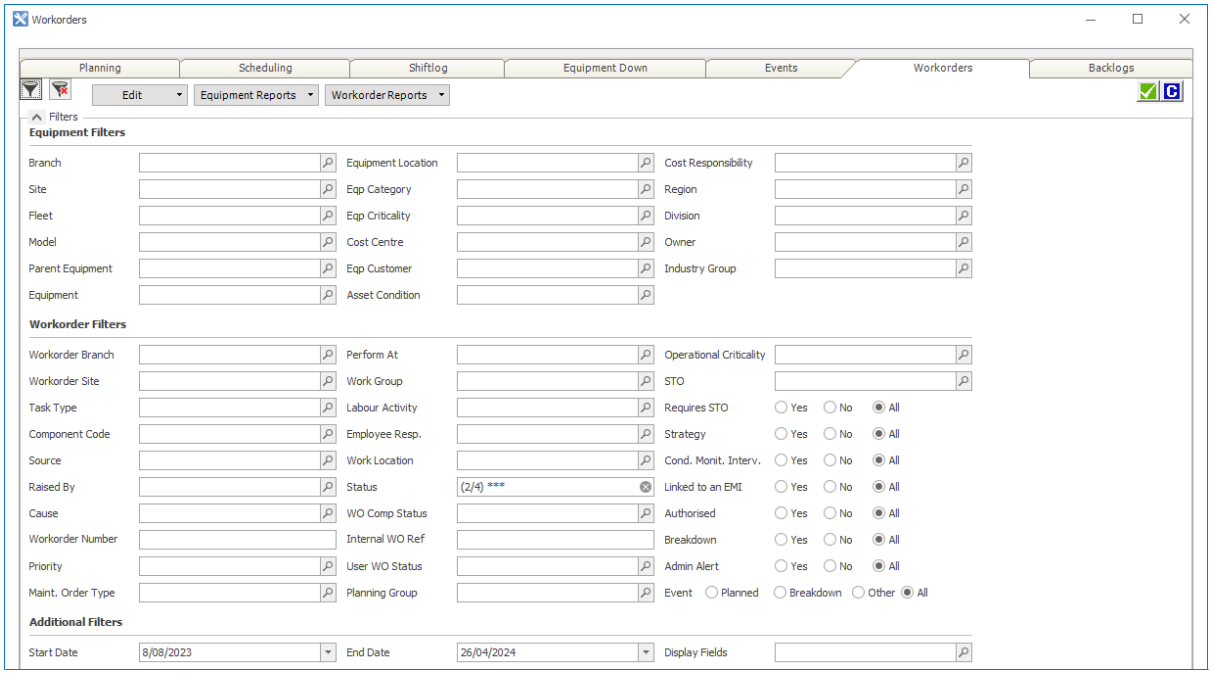


5. Click **Apply Filters**.
6. Double-click on the relevant work order.

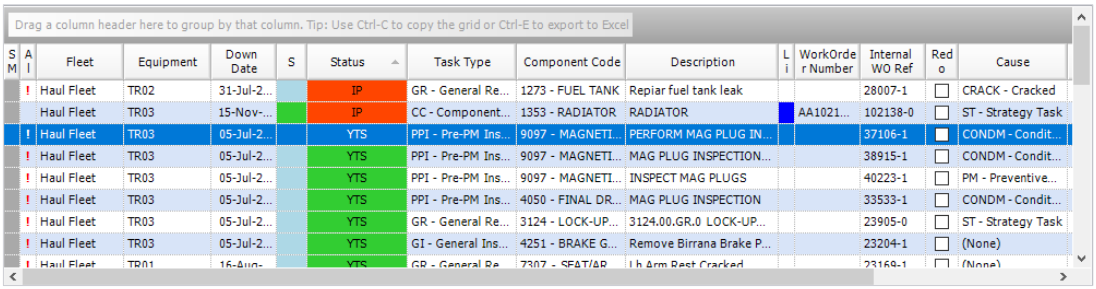


7. Click the **Planning** tab.

   The document must already exist in the library to allocate it to the work order.


8. In the **Linked Documents** section, click **Add** to select the document.

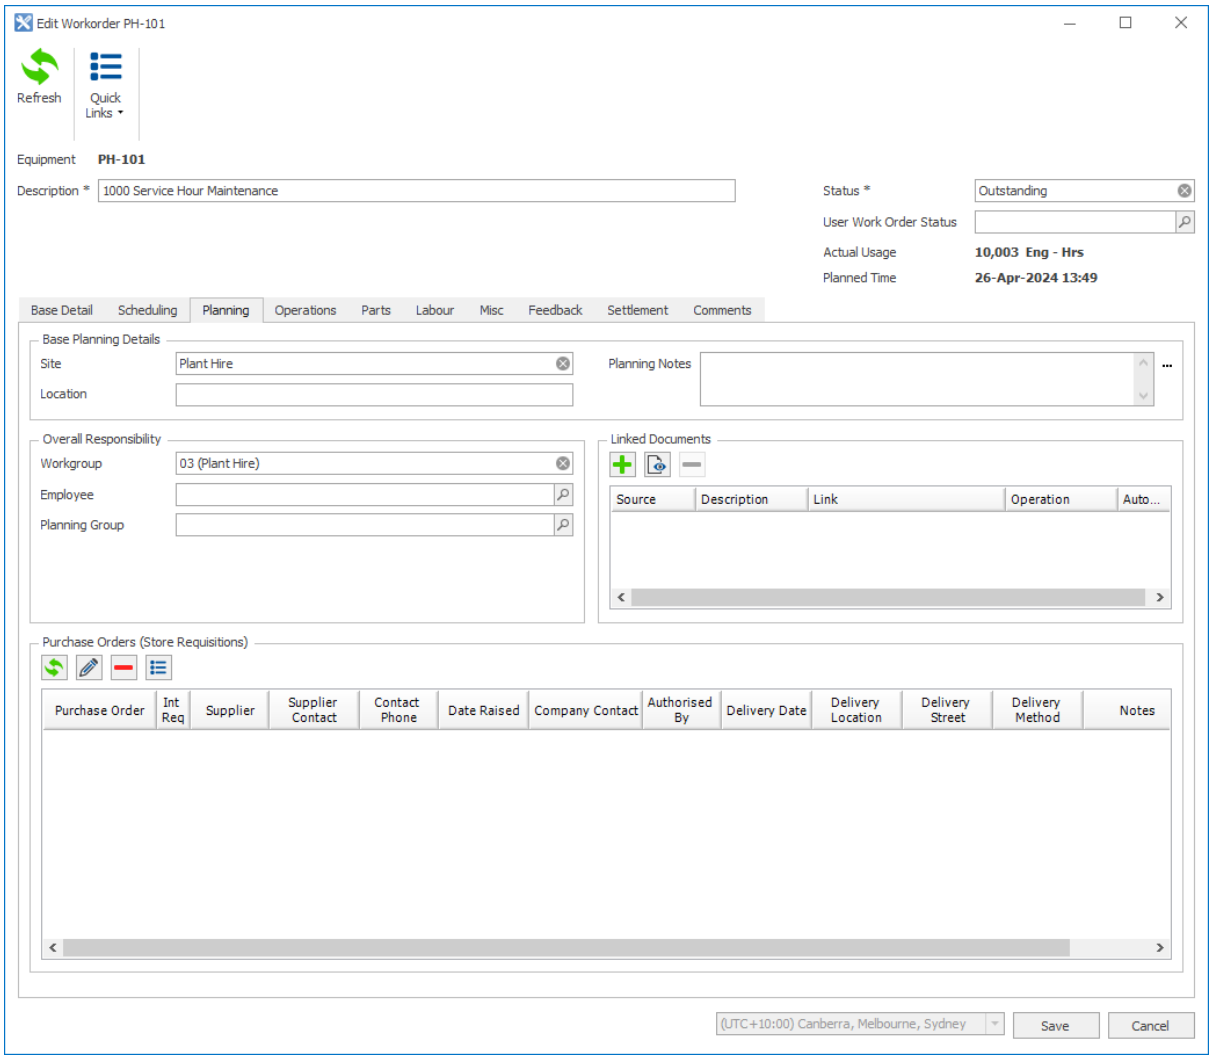

Click **>>**, and filter for the relevant document. Select it and click **Save**.

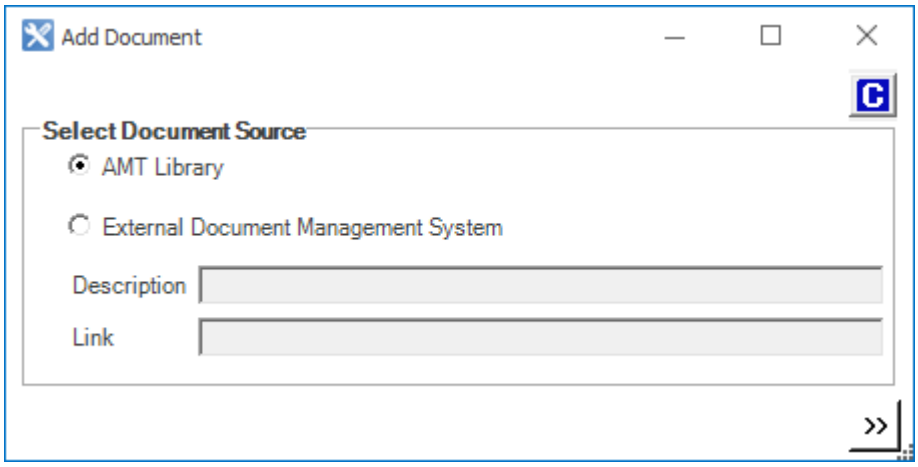


9. Select **Auto Print** to ensure that the attached document is printed with the job folders.

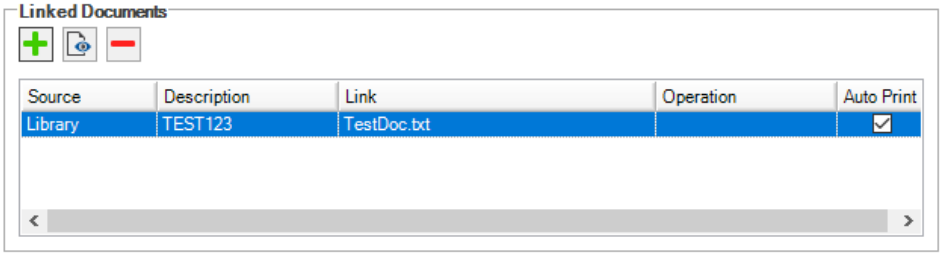

Procedure – Opening an ERP Work Order

1. Under **Daily Planning**, double-click **Planning**.
2. Select appropriate filers.
3. Click **Apply Filters**.
4. Select the relevant work order and click **Edit**.
5. Click the **Settlement** tab.
6. Check the default accounting codes and change them if required (select **Enter and use specific operation codes** to edit the specific codes).
7. Click **Create ERP WO** to send the file to the ERP system and create the work order in it.

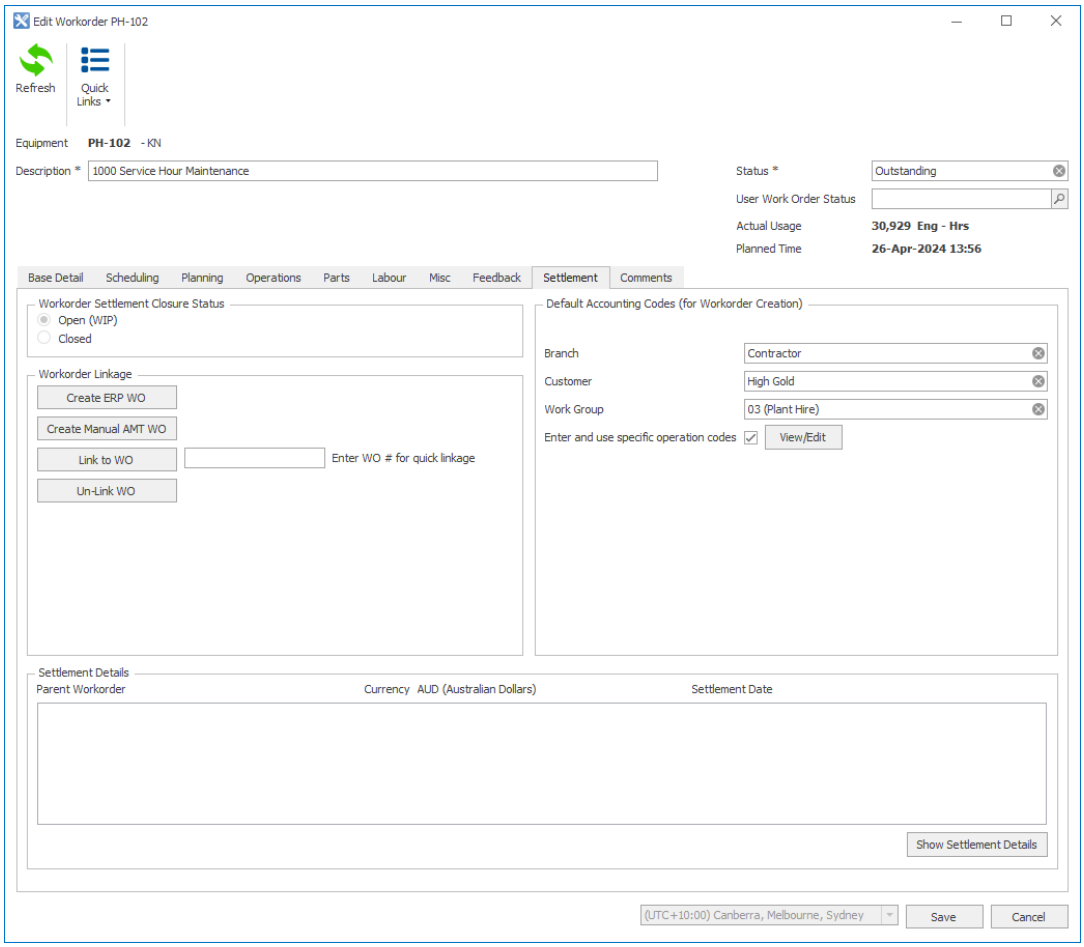

Exercise – Job Ready

1. Enter parts, labour, and miscellaneous requirements into the backlog that you created in a previous exercise.
2. If AMT is configured to work with an external work order system:
    a. Create an ERP work order.
    b. Perform steps in the ERP work order so that all parts are ready.
3. Set Labour and Misc. to ready.
4. Authorise the work order.
5. Check that the work order is now *Job Ready*.



Repeat the above exercises for a strategy work order.

Learning Check



Check your understanding of the workshop and ask any related questions.

Notes

Training Workshops (Scheduling)

9. Definition of Scheduling

Functionality Overview

Scheduling involves setting the **when**, **where** and **who** for work orders.

In **Advanced Planning** mode, a work order is scheduled in AMT if it is linked to a planned down event.


In **Standard Planning** mode, a work order is scheduled in AMT if it has status yet to schedule (YTS).

In practical terms, if the work order shows a Plan down date on the Planning grid, it is scheduled (**Note**: In Advanced Planning mode, if you open that work order it will first open the event).

10. Schedule a Work Order – Advanced Planning


Procedure – Schedule a Work Order (Advanced Planning)

1. Under **Daily Planning**, double-click **Planning**.
2. Select appropriate **Filters**.
3. For advanced planning assets, set **Display Fields** to **Event Start**.
4. Click **Apply Filters**.

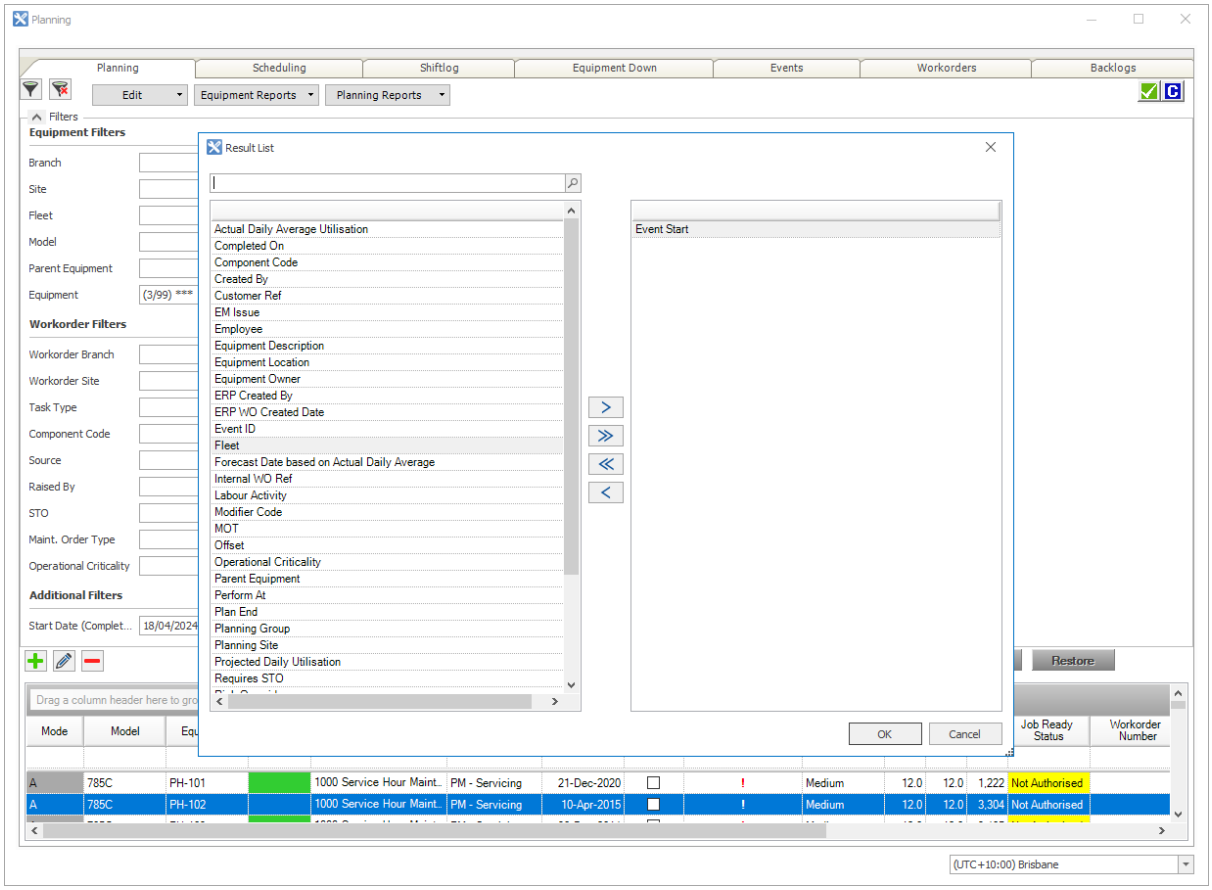

Event Start applies to advanced planning assets only (the SM cell is light grey if the asset uses standard planning, or dark grey if the asset uses advanced planning).

5. Create the event by editing the **Event Start** field for the required work order.
6. Click **Save**.
7. This work order will become the primary work order of the event, and its status will be **YTS**.
8. To edit the details of the event, select the work order and select **Edit > Edit Event**.
9. After the **Edit Event** window is open, you can:
    a. Edit base event information.
    b. Adjust planned downtime information.
    c. Add, edit and delete downtime allocations.
    d. Add, edit and delete work orders.
10. To print a work plan, select the report from **Planning Reports > Daily/Weekly Work Plan**.
11. This report defaults to show the work plan for the next seven days.

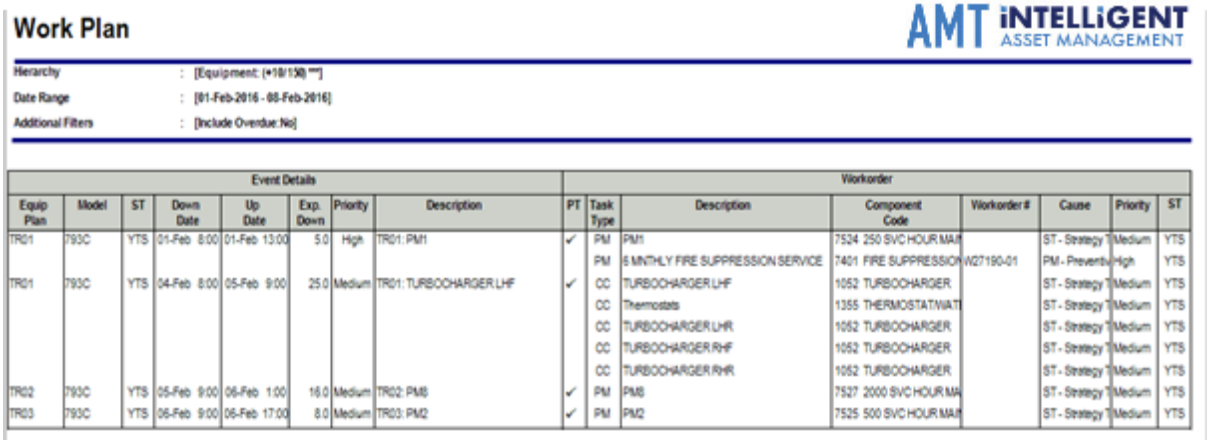

Work Plan

AMT iNTELLiGENT ASSET MANAGEMENT

Hierarchy : [Equipment: (+10/150,"*")]
Date Range : [01-Feb-2016 - 08-Feb-2016]
Additional Filters : [Include Overdue:No]

Event Details								Workorder						
Equip Plan	Model	ST	Down Date	Up Date	Exp. Down	Priority	Description	PT	Task Type	Description	Component Code	Workorder #	Cause	Priority	ST
TR01	793C	YTS	01-Feb 8:00	01-Feb 13:00	5.0	High	TR01: PM1	✓	PM	PM1	7524 250 SVC HOUR MAI		ST - Strategy T	Medium	YTS
									PM	6 MNTHLY FIRE SUPPRESSION SERVICE	7401 FIRE SUPPRESSION	WZ7190-01	PM - Preventa	High	YTS
TR01	793C	YTS	04-Feb 8:00	05-Feb 9:00	25.0	Medium	TR01: TURBOCHARGER LHF	✓	CC	TURBOCHARGER LHF	1052 TURBOCHARGER		ST - Strategy T	Medium	YTS
									CC	Thermostats	1355 THERMOSTAT/WAT		ST - Strategy T	Medium	YTS
									CC	TURBOCHARGER LHR	1052 TURBOCHARGER		ST - Strategy T	Medium	YTS
									CC	TURBOCHARGER RHF	1052 TURBOCHARGER		ST - Strategy T	Medium	YTS
									CC	TURBOCHARGER RHR	1052 TURBOCHARGER		ST - Strategy T	Medium	YTS
TR02	793C	YTS	05-Feb 9:00	06-Feb 1:00	16.0	Medium	TR02: PM8	✓	PM	PM8	7527 2000 SVC HOUR MA		ST - Strategy T	Medium	YTS
TR03	793C	YTS	06-Feb 9:00	06-Feb 17:00	8.0	Medium	TR03: PM2	✓	PM	PM2	7525 500 SVC HOUR MAI		ST - Strategy T	Medium	YTS

12. To run the report for a longer period of time, or to include additional assets, navigate to the main menu, search for the Daily/Weekly Work Plan report and run it using customised filters.

Exercise – Create a Planned Event

1. Identify advanced planning assets.
2. Find a strategy work order for a PM service.
3. Create a new planned event using the PM service as the primary work order.
4. Set the planned downtime and uptime for the event.

Learning Check




Check your understanding of the workshop and ask any related questions.

Notes

11. Schedule a Work Order – Standard Planning Mode


Procedure – Schedule a Work Order (Standard Planning Mode)

1. Set the **Plan Start** date and time in the grid.
2. Click **Save**.
3. The work order's status will be **YTS (Yet to Start)**.
4. To edit the details of the work order, highlight the work order in the **Planning** grid and click **Edit**.
5. To print a work plan, select the report from **Planning Reports > Work Plan – Workorder Summary**.

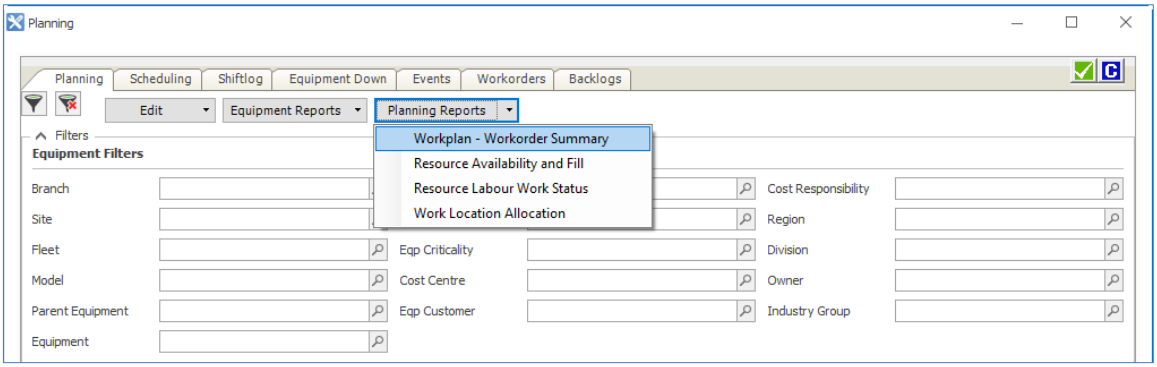

This report defaults to show the work plan for the next 7 days.

6. To run the report for a longer period of time, or to include more assets, navigate to the main menu, search for the **Workplan – Workorder Summary** and run it using customised filters.

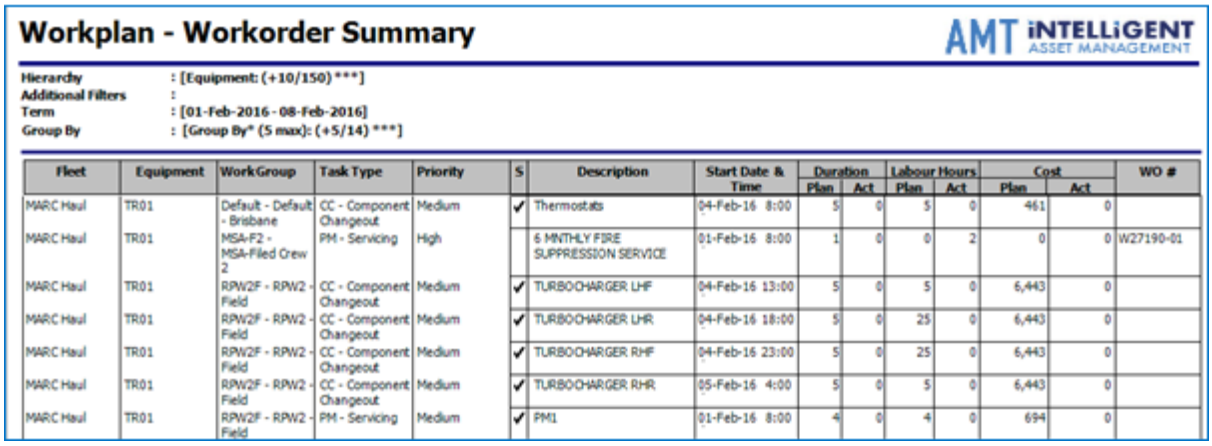

Workplan - Workorder Summary

AMT iNTELLiGENT ASSET MANAGEMENT

Hierarchy : [Equipment: (+10/150) ***]
Additional Filters :
Term : [01-Feb-2016 - 08-Feb-2016]
Group By : [Group By* (5 max): (+5/14) ***]

Fleet	Equipment	Work Group	Task Type	Priority	S	Description	Start Date & Time	Duration		Labour Hours		Cost		WO #
								Plan	Act	Plan	Act	Plan	Act	
MARC Haul	TR01	Default - Default - Brisbane	CC - Component Changeout	Medium	✓	Thermostats	04-Feb-16 8:00	5	0	5	0	461	0	
MARC Haul	TR01	MSA-F2 - MSA-Filed Crew 2	PM - Servicing	High		6 MNTHLY FIRE SUPPRESSION SERVICE	01-Feb-16 8:00	1	0	0	2	0	0	W27190-01
MARC Haul	TR01	RPW2F - RPW2 - Field	CC - Component Changeout	Medium	✓	TURBOCHARGER LHF	04-Feb-16 13:00	5	0	5	0	6,443	0	
MARC Haul	TR01	RPW2F - RPW2 - Field	CC - Component Changeout	Medium	✓	TURBOCHARGER LHR	04-Feb-16 18:00	5	0	25	0	6,443	0	
MARC Haul	TR01	RPW2F - RPW2 - Field	CC - Component Changeout	Medium	✓	TURBOCHARGER RHF	04-Feb-16 23:00	5	0	25	0	6,443	0	
MARC Haul	TR01	RPW2F - RPW2 - Field	CC - Component Changeout	Medium	✓	TURBOCHARGER RHR	05-Feb-16 4:00	5	0	5	0	6,443	0	
MARC Haul	TR01	RPW2F - RPW2 - Field	PM - Servicing	Medium	✓	PM1	01-Feb-16 8:00	4	0	4	0	694	0	


Exercise – Schedule a Work Order (Standard Planning)

1. Identify a standard planning asset.
2. Find a strategy work order for a PM service.
3. Schedule the PM service work order and set the Planned Start Time and End Time.

12. Refine a Work Plan

Procedure – Add More Backlogs to a Planned Event

1. To add a work order to an event, click the relevant work order and drag it to the **Event** bar on the Gantt chart.

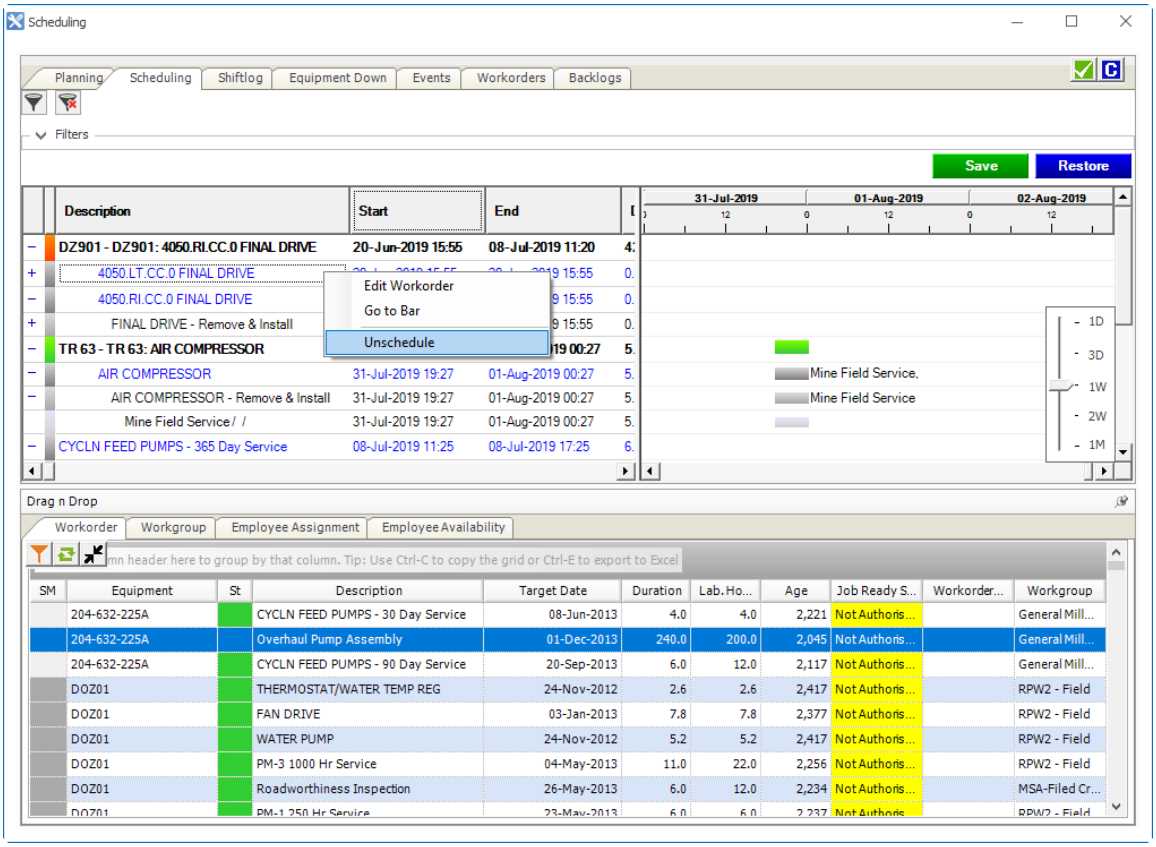

2. Right-click **Event** and select **Edit Event** to view the details of an event.
3. Add a work order based on an unplanned strategy task or a standard job by viewing the details of the event, and right-clicking the work order section of the event.

*To remove a work order from an event, right-click on the work order and select **Unschedule**.*

The Event Bar expands when you hover over it with a work order.

Exercise – Add more Work Orders to an Event

1. Add some more work orders to the event created in a previous exercise.


Procedure – Make Changes to Work Plan

You can refine a work plan using the **Scheduling** tab to edit existing events, create new events, or unschedule existing events (in **Advanced Mode** only).

1. Under **Daily Planning**, double-click **Planning**.

> *It is important to understand whether the asset is set up to use **Advanced** or **Standard** Planning mode (check with your AMT System Administrator).*


2. Click the **Scheduling** tab.
3. Select the appropriate filters.
4. Select group **by level** (normally = **Site**).
5. Click **Apply Filters**.
6. Consider simplifying the initial display of the schedule by setting **Display Op-Lab** to **None** and clear the **Operation Bar** option.

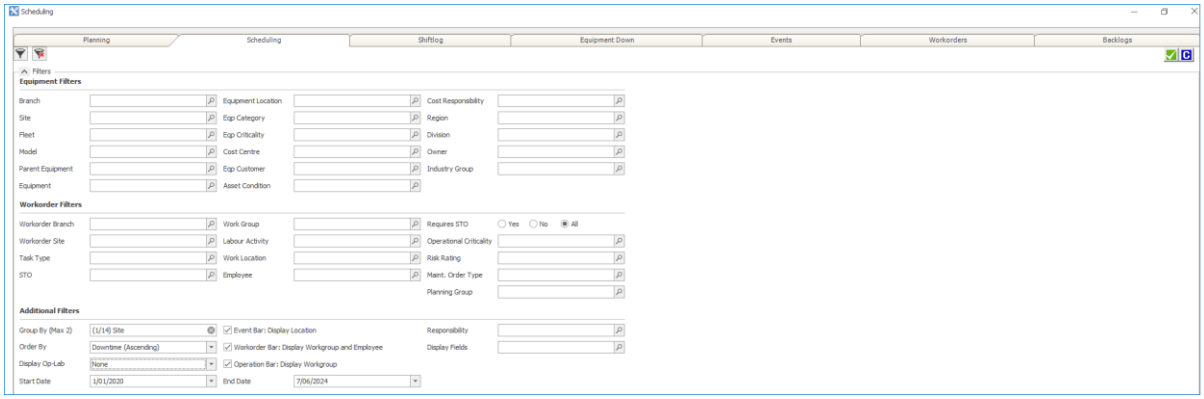

> *To simplify the initial view of schedule set **Display Op-Lab** = None.*

7. In the grid, text in **black** is the event level. Text in blue is the work order level. On the Gantt chart, In Progress and Yet to Start events will display.

8. To reschedule an event, modify the event's **Start** and **Duration** values directly in the grid. AMT will calculate **End = Start + Duration**.

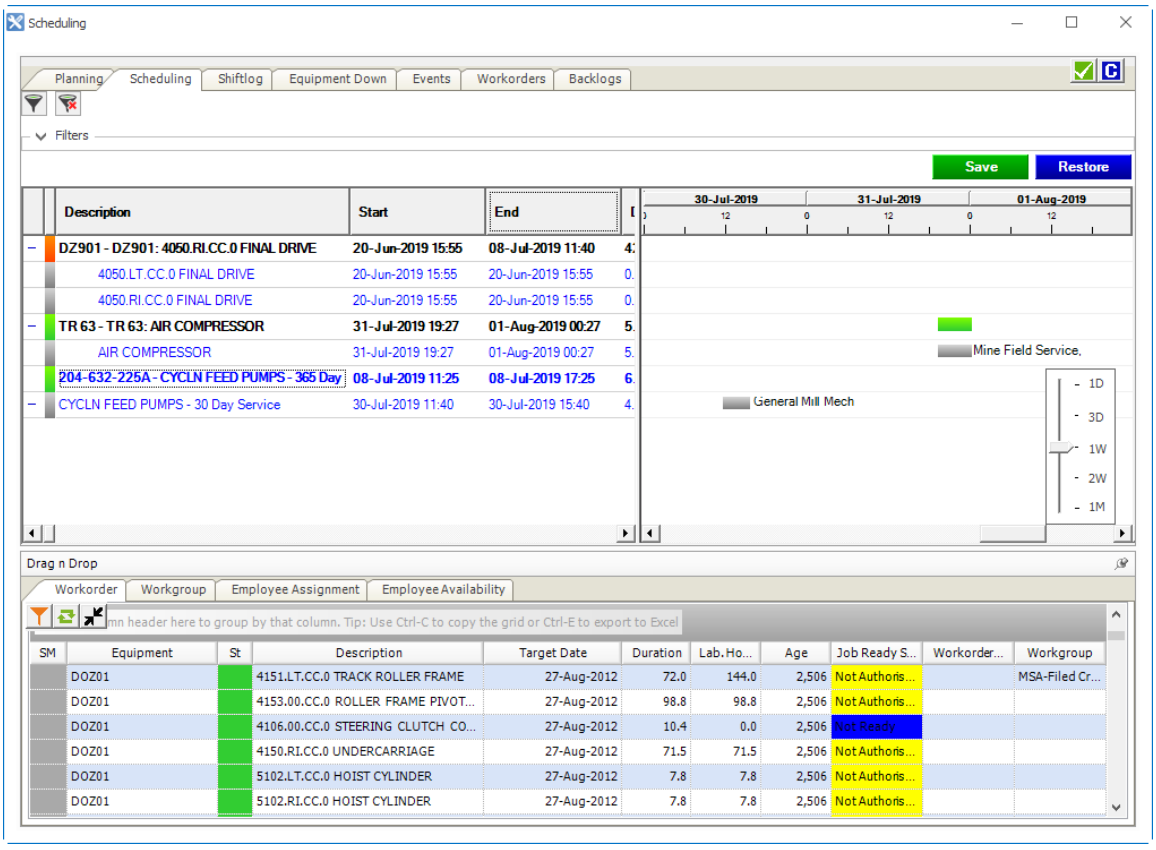

9. Click **Save**.

*If a bar in the Gantt chart cannot be seen for an event, highlight the event in the grid, right-click and select **Go To Bar**.*

Procedure – Unschedule an Event and its Work Orders

This procedure removes an event and its work orders from the work plan.

1. Click the **Workorder** tab on the **Drag n Drop** menu (located at bottom of the screen).
2. Filter for all **work orders** for at least the same asset (recommend filtering for the same site).
3. Right-click each work order in the relevant event, on the main **Scheduling** grid, and click the option **Unschedule**.
4. The work order is removed from the schedule and placed back in the backlog of work orders, where its status will now show **O** (**Outstanding**) instead of **YTS** (**Yet to Start**).
5. Click **Save**.
6. If the **Unschedule** option is not highlighted, ensure the **Drag n Drop** > **Workorder** tab has been filtered so that it contains the same asset. The event itself cannot be unscheduled; however, by unscheduling each work order in the event, the event will be unscheduled.

Procedure – Add a Work Order to an Existing Event on the Scheduling Grid

1. Click the **Workorder** tab on the **Drag n Drop** menu.
2. Click **Filter** for all work orders for at least the same asset (recommend filtering for the same site).
3. Highlight and then drag the work order onto the event. The **Event** bar should expand; after it has, drop the work order. It will appear in the **Scheduling Grid** and **Gantt Chart** under the event.
4. Click **Save**.

Procedure – Add a new Event to a Work Plan

1. Click the **Workorder** tab on the **Drag n Drop** menu.
2. Click **Filter** for all work orders for at least the same asset (recommend filtering for the same site).
3. Select and then drag it onto the white space in the **Gantt Chart**. A new event appears in the **Grid** and on the **Gantt Chart**.
4. Click **Save**.

Exercise – Modify the Work Plan

1. Go to the **Scheduling** tab.
2. Smooth the schedule by manipulating the **Start Date: Time** and **Duration** fields of events and work orders.
3. Find and drag work orders onto events in the Gantt chart (green bars).
4. Adjust the **Start: Date** and **Duration** fields in the work orders to schedule them accurately within the event.

Procedure – Merge Events

If you want to merge two events into a single event, you can do this by opening the event you want to attach to a **YTS Event** and click **Merge Yet to Start Event**.

1. Under **Daily Operations**, double-click **Equipment Status**.
2. Click the **Shiftlog** tab.
3. Set appropriate filters (such as, site, fleet) and set **Event Status** to **In Progress** to see recent downtime notifications imported from an external system.
4. Click **Apply Filters**.
5. External downtime events imported into AMT are flagged in the **E column**.
6. The fields sourced from the external system **Asset**, **(Event) Description**, **Downtime**, **Uptime**, and **Planned / Breakdown**.
    - Downtime and Uptime cannot be modified.
    - The notification may be flagged as Planned or Breakdown
7. AMT creates a work order for the event using AMT's default task type and component code. The description of the work order is sourced for the external downtime notification.
8. An event in AMT must have at least ONE work order, otherwise AMT will create a "dummy" work order attached to the event.
9. Edit the event by clicking **Edit** or double-clicking the row.
10. To merge the event with another planned event in AMT, click **Merge Yet to Start Event**.
11. Select the AMT event from the list (this list is automatically filtered to show YTS events for the same asset).
12. Click **Save** to merge.



When merging Yet to Start events with external events, if the Default Unallocated Downtime is defined in the Variance Cause System Table, AMT will retain planned and actual downtown hours entered.

The merge process cannot be reversed. However, you can unlink the resultant event from the downtime notification if a mistake is made.


The following details from the existing event are moved to the event being edited:

a. Event description
b. Work orders

We recommend that you check the following information:

a. Planned vs. Breakdown flag
b. Downtime Allocation fields
c. Status of each work order

13. Click **Save**.

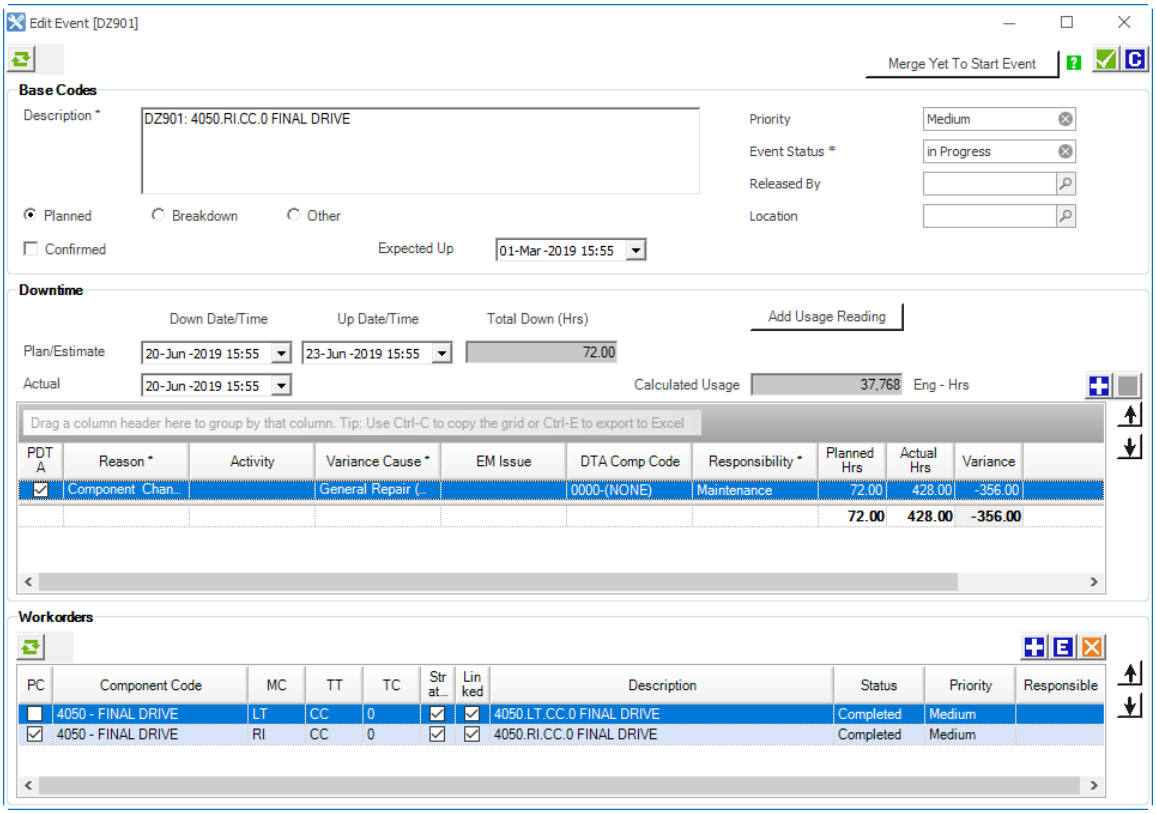
Edit Event [DZ901]
Merge Yet To Start Event
Base Codes
Description *
DZ901: 4050.RI.CC.0 FINAL DRIVE
Priority
Medium
Event Status *
in Progress
Released By
Location
Planned
Breakdown
Other
Confirmed
Expected Up
01-Mar-2019 15:55
Downtime
Down Date/Time
Up Date/Time
Total Down (Hrs)
Add Usage Reading
Plan/Estimate
20-Jun-2019 15:55
23-Jun-2019 15:55
72.00
Actual
20-Jun-2019 15:55
Calculated Usage
37,768
Eng - Hrs
Drag a column header here to group by that column. Tip: Use Ctrl-C to copy the grid or Ctrl-E to export to Excel
PDTA
Reason *
Activity
Variance Cause *
EM Issue
DTA Comp Code
Responsibility *
Planned Hrs
Actual Hrs
Variance
Component Chan...
General Repair (...
0000-(NONE)
Maintenance
72.00
428.00
-356.00
72.00
428.00
-356.00
Workorders
PC
Component Code
MC
TT
TC
Str at...
Linked
Description
Status
Priority
Responsible
4050 - FINAL DRIVE
LT
CC
0
4050.LT.CC.0 FINAL DRIVE
Completed
Medium
4050 - FINAL DRIVE
RI
CC
0
4050.RI.CC.0 FINAL DRIVE
Completed
Medium

Learning Check




Check your understanding of the workshop and ask any related questions.


Notes

13. Associate Resources to a Work Order

Procedure – Assign Location

1. Under **Daily Planning**, double-click **Planning**.
2. Navigate to the **Shiftlog** tab.
3. Select the appropriate filters.
4. Click **Apply Filters**.
5. Select the relevant event, right-click and select **Edit Event**.
6. Select the relevant location where the work will be carried out.
7. Click **Save**.
8. Highlight the relevant work order, click Planning Reports and run the **Work Location Allocation report** to see whether certain locations have been over- or under-booked.

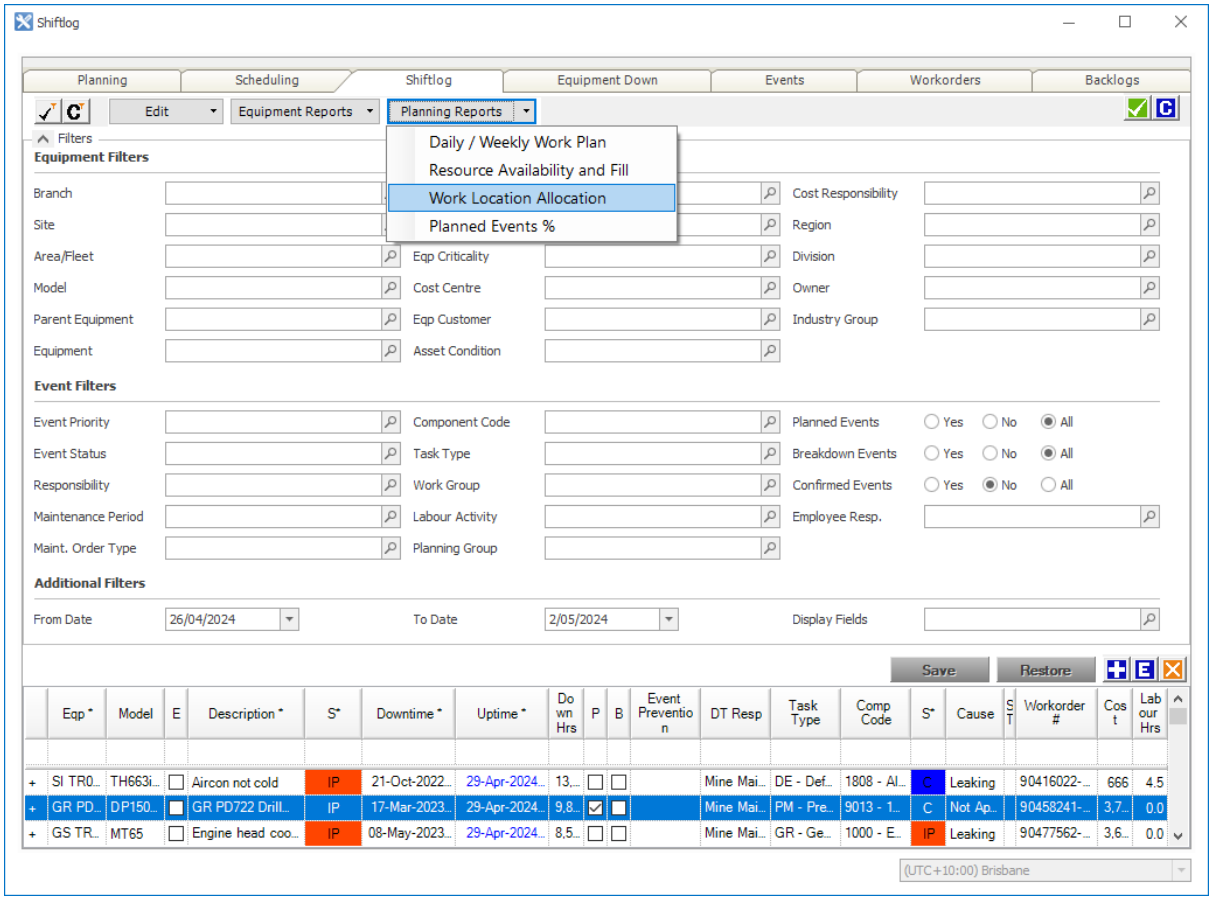

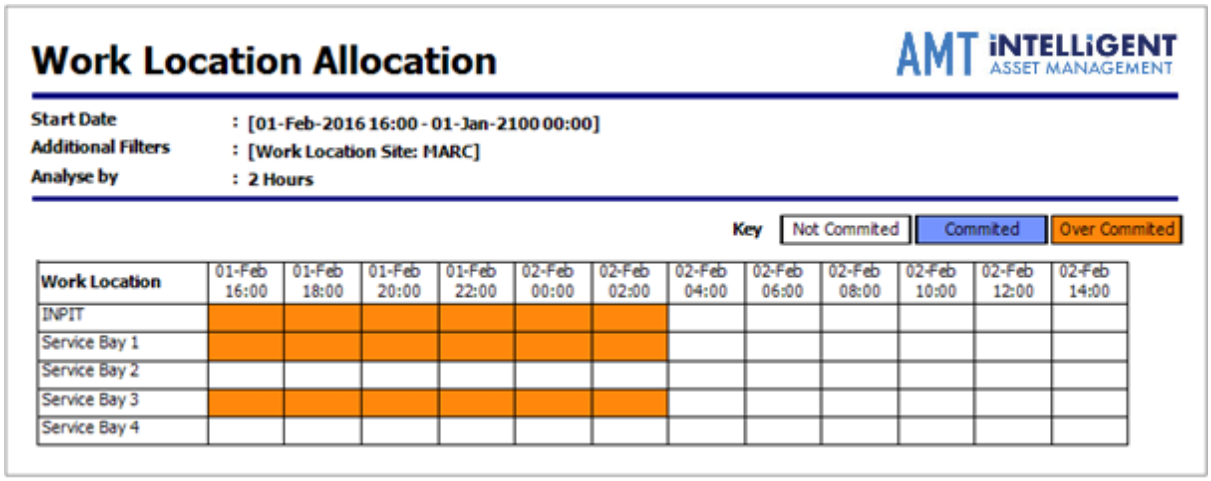

Work Location Allocation

AMT INTELLIGENT ASSET MANAGEMENT

Start Date : [01-Feb-2016 16:00 - 01-Jan-2100 00:00]
Additional Filters : [Work Location Site: MARC]
Analyse by : 2 Hours

Key: Not Commited | Commited | Over Commited

Work Location	01-Feb 16:00	01-Feb 18:00	01-Feb 20:00	01-Feb 22:00	02-Feb 00:00	02-Feb 02:00	02-Feb 04:00	02-Feb 06:00	02-Feb 08:00	02-Feb 10:00	02-Feb 12:00	02-Feb 14:00
INPIT												
Service Bay 1												
Service Bay 2												
Service Bay 3												
Service Bay 4												

Exercise – Assign Locations to Events

1. Assign locations (such as workshop bays) to events.
2. Use the **Work Location Allocation** report to view over and under allocations of locations.

Exercise – Assign Labour (Workgroup Level Resourcing)

- The site in AMT is not enabled for employee-level resourcing.
- The work groups are set up against the site in AMT system tables.
- Available man hours for each work group have been added.


Procedure – Assign Labour (Create Manpower Roster – Work Group Level)

1. Ensure that the site is set to **Workgroup Level Resourcing**.
2. Open the **Site Administration** system table.
3. Apply **Filter**, then double-click on your site to open the **Edit Site** window.
4. Clear **Enable Employee Level Resourcing**.

Work groups in AMT are site-specific.

5. To set up the work groups for each site, open the **Work Group** system table.
    a. Select a site.
    b. Click **Apply Filters**.
    c. Click **Add**.
    d. Enter the **Site**, **Work Group Code** and **Code**.
    e. Click **Save**.

6. To set up available man hours for each work group, open the **Set Available Resource Hours**.
    a. Select a **Site**, **Workgroup** and **Labour Activity**.
    b. Set a date range.
    c. Click **Apply Filters**.
7. Available hours can be entered by using one of the following methods:
    a. Entering manually into each field.
    b. Click **Refresh Data From Employees** (this option draws employees' hours set using the **Set Employee Working Time function**)
    c. Export the data into Excel (by right-clicking on the data and selecting **Copy the table**), modify it, then pasting the changed results back into the grid.

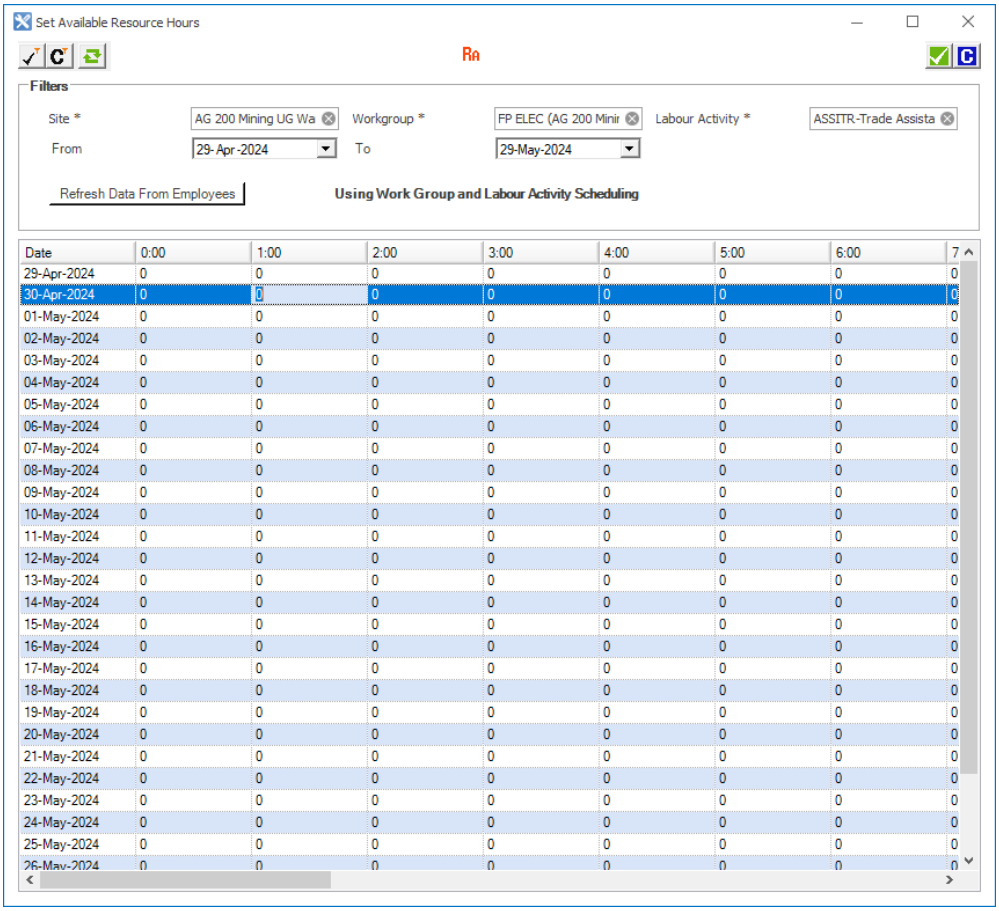

If you are having problems pasting data back into AMT, ensure that the format of the data is identical.

Work groups can then be assigned to work orders from the **Scheduling** tab or by the individual work order details screen.


Procedure – Assign Labour (Scheduling and Allocation Review – Work Group Level)

1. Open a work order in **Planning** or **Advanced Planning** and navigate to the **Labour** tab.

   You must ensure that the work order has at least one operation to be able to assign labour.

2. On the Operations tab, click **Add** to create an operation.

3. To add employees to an operation, highlight the operation on the **Labour** tab and in the **Quick Links** menu click **Assign Employees**. The **Employee Availability** window opens.

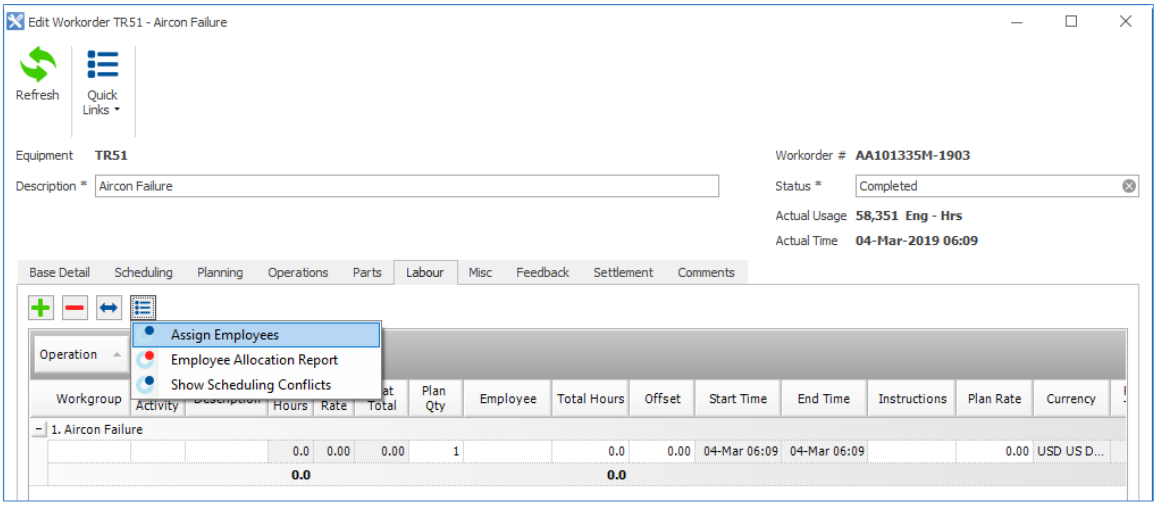


   The **Employee Availability** window displays the availability status of each employee and allows for easy employee scheduling.

4. To assign an employee to an operation, select the check box next to the employee's name and click **Save**.

5. After adding the employees to an operation, check for scheduling conflicts by clicking **Show Scheduling Conflicts**.


6. Conflicts display in red.

7. Click **Employee Allocation Report** to run the report.

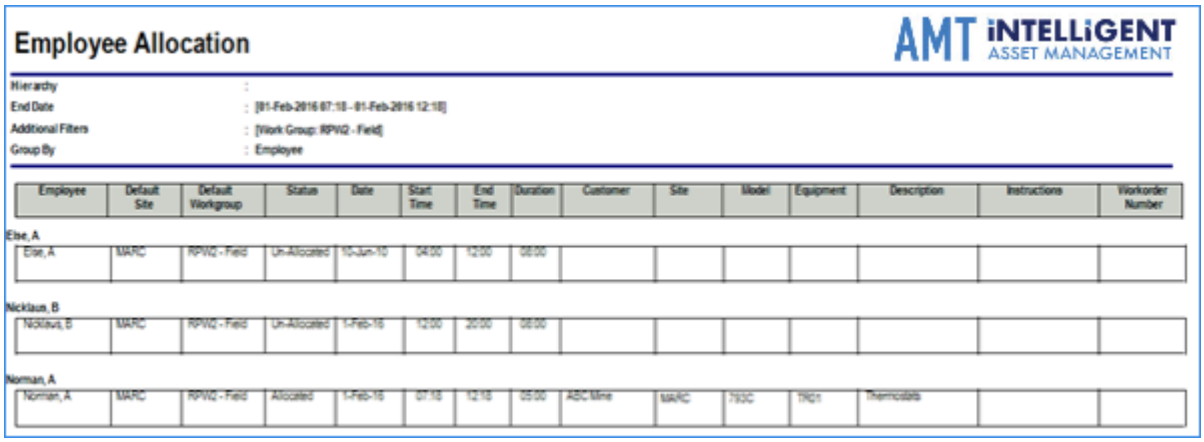

Procedure – Assign Labour (Assigning Labour to a Work Order – Work Group Level)

1. Open a work order in **Planning** or **Advanced Planning** and navigate to the **Labour** tab.
2. Ensure that the work order has at least one operation to be able to assign labour.
3. On the **Operations** tab, click **Add** to create an operation.
4. To add workgroups to an operation, select the operation on the **Labour** tab and click **Add**.
5. To assign a work group to an operation, enter the relevant information in the new row.
6. Use the **Resource Availability and Fill – Workgroup** report to help with scheduling.
7. This report shows surpluses and deficiencies.
8. A negative number indicates an **overallocation** and a positive number indicates there is a resource surplus.
9. Run the **Resource Availability and Fill – Workgroup** report after allocating labour to review the man-hour allocation.

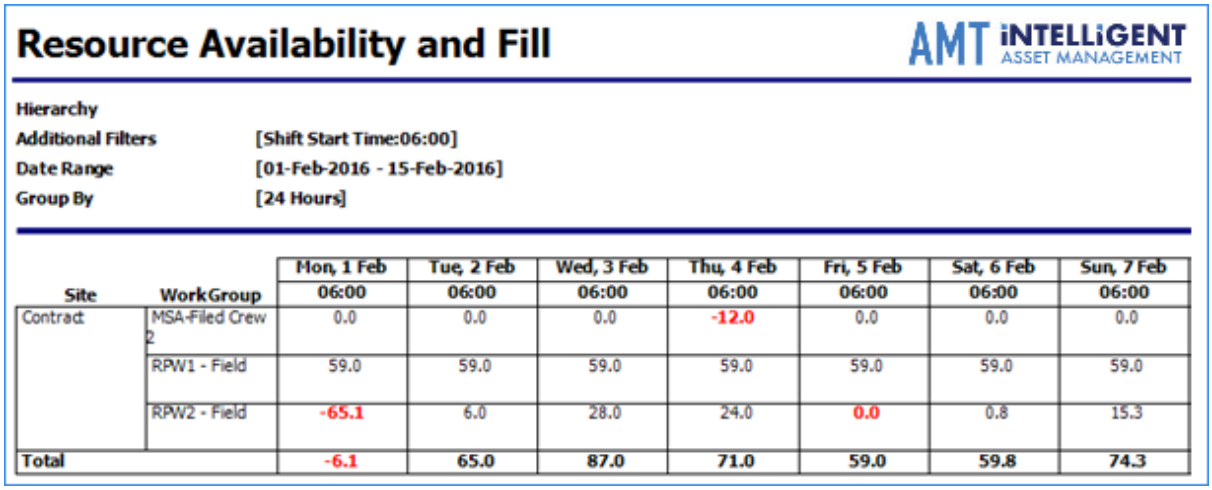

Resource Availability and Fill

AMT iNTELLiGENT ASSET MANAGEMENT

Hierarchy
Additional Filters [Shift Start Time:06:00]
Date Range [01-Feb-2016 - 15-Feb-2016]
Group By [24 Hours]

Site	WorkGroup	Mon, 1 Feb 06:00	Tue, 2 Feb 06:00	Wed, 3 Feb 06:00	Thu, 4 Feb 06:00	Fri, 5 Feb 06:00	Sat, 6 Feb 06:00	Sun, 7 Feb 06:00
Contract	MSA-Filed Crew 2	0.0	0.0	0.0	-12.0	0.0	0.0	0.0
	RPW1 - Field	59.0	59.0	59.0	59.0	59.0	59.0	59.0
	RPW2 - Field	-65.1	6.0	28.0	24.0	0.0	0.8	15.3
Total		-6.1	65.0	87.0	71.0	59.0	59.8	74.3

Exercise – Assign Labour (Employee Level Resourcing)


- The site in AMT is enabled for employee-level resourcing.
- Work groups are registered.
- Labour activities are registered.
- An employee roster has been created.
- The roster hours have been added in the **Set Employee Work Time** AMT function.
- The roster has been copied to the relevant employees.

Procedure – Assign Labour (Create Manpower Rosters – Employee Level)

1. Ensure that the site is set to employee-level resourcing.
2. Navigate to **Site Administration**.
3. Click **Apply filter**, then double-click your site to open the **Edit Site** window.
4. Select the **Enable Employee Level Resourcing** check box.
5. Click **Save**.

Create an **Employee Roster**.


6. Navigate to **Employee**.
7. Click **Add**.
8. Select a **Site**.
9. Select a name for the roster employee. Use the **Surname** to identify the roster type (such as, 4 on, 4 off, Night shift).

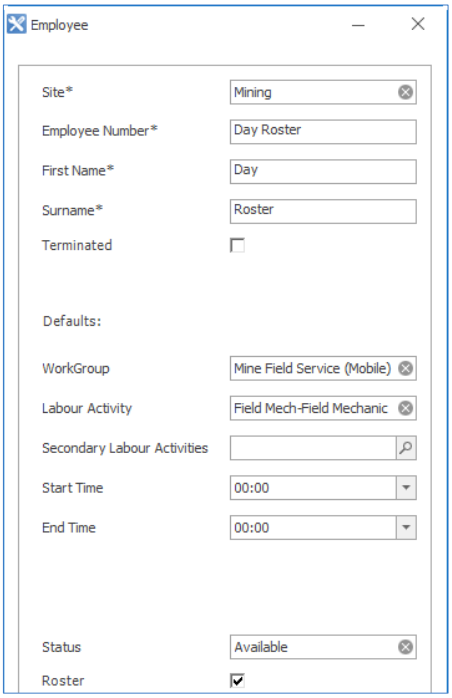

10. Fill in the **Workgroup** and **Labour Activity** fields.
11. Set the **Start** and **End Time** for the roster employee.
12. Ensure that you set the **Status** to **Available** and select **Roster**.

Set up the roster hours.


13. Navigate to **Set Employee Working Time**.
14. Create one cycle of the roster by allocating work hours for each workday during the roster cycle.
15. Click **Add** and fill in the form details to add a day to the roster cycle.

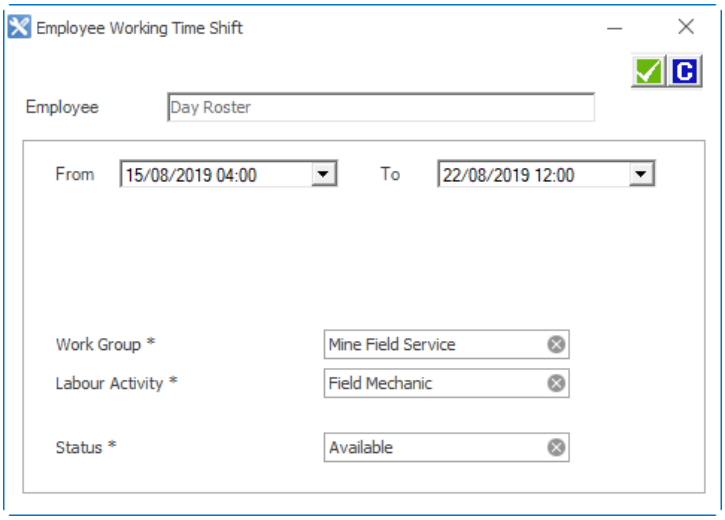

Entering 15-Aug-19 04:00 to 15-Aug-19 12:00 (Status = Available) means that the person is available between ***those hours*** *on that* ***specific day****.*

Entering 15-Aug-19 04:00 to 22-Aug-19 12:00 (Status = Available) means that the person is available ***every single hour*** *from 15-Aug-19 04:00 to 22-Aug-19 12:00.*

16. Non-work time (such as annual leave) can be added as a work time allocation to provide a complete picture for the employee availability.

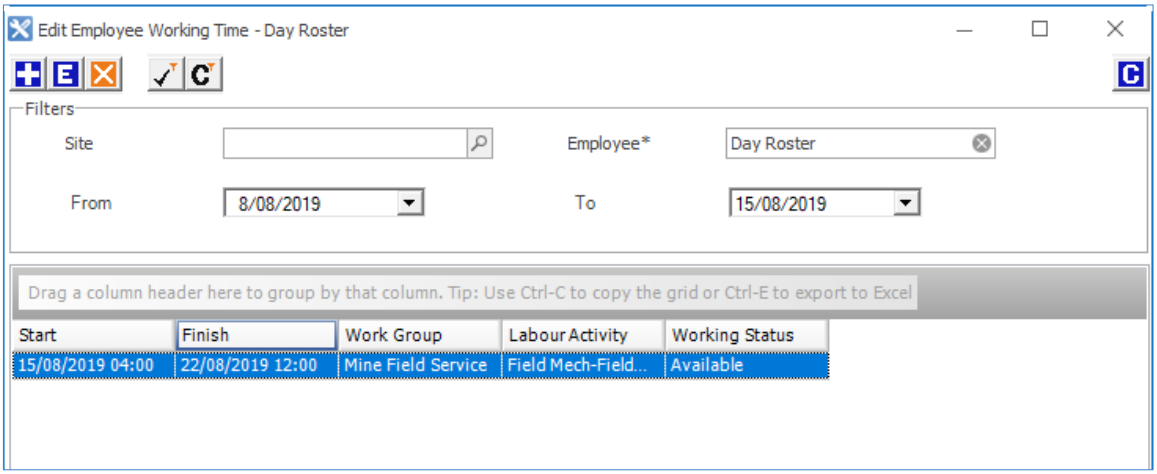


Allocate work hours for each day of work during the roster cycle.

Procedure – Assign Labour (Copy Manpower Rosters – Employee Level)

1. Navigate to **Daily Planning > Employee Setup > Copy Employee Working Time**.
2. Click the **Source** (that is, the roster employee).
3. Click **Apply Filter** to view hours to be copied.
4. Select **Destination Employee** and the date to which the roster is to be copied.
5. Repeat as many times as necessary to create the desired roster.
6. Employees can then be assigned to work orders from the **Scheduling** tab or by the individual work order details screen.


Procedure – Assign Labour (Assigning Labour to a Work Order – Employee Level)

1. Navigate to the **Site Administration system table** and ensure that the site is set to **Employee Level Resourcing**.
2. Click **Apply Filter**.
3. Double-click your site to open the **Edit Site** window.
4. Select **Enable Employee Level Resourcing**.
5. Open a work order in **Planning** or **Shutdown Planning** and navigate to **Labour** tab.
6. The work order must have at least one operation to be able to assign labour. Click **Add** on the **Operations** tab to create an operation.
7. To add employees to an operation, select the operation on the **Labour** tab and click **Assign Employees**. The **Employee Availability** window opens.
8. The **Employee Availability** window displays the availability status of each employee and allows for easy employee scheduling.
9. To assign an employee to an operation, select the check box next to the employee's name and click **Save**.
10. Click **Employee Allocation Report** to run the report.

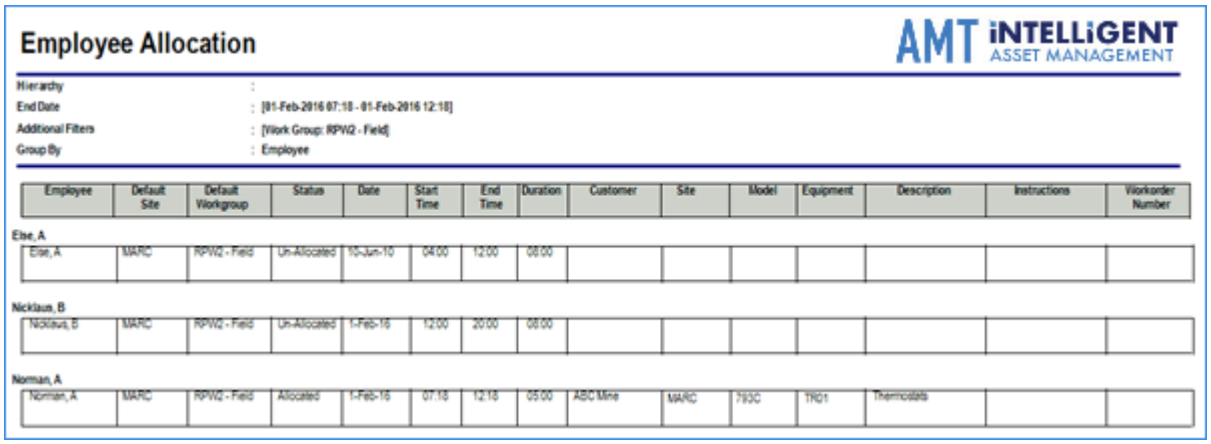

11. After adding employees to an operation, click **Show Scheduling Conflicts** to check for scheduling conflicts. Conflicts display in red.

12. Use the **Resource Availability and Fill report** to help with employee scheduling.
13. This report shows **Surpluses** and **Deficiencies** in available employee rosters. A negative number indicates an over allocation. A positive number indicates that there is a resource surplus.

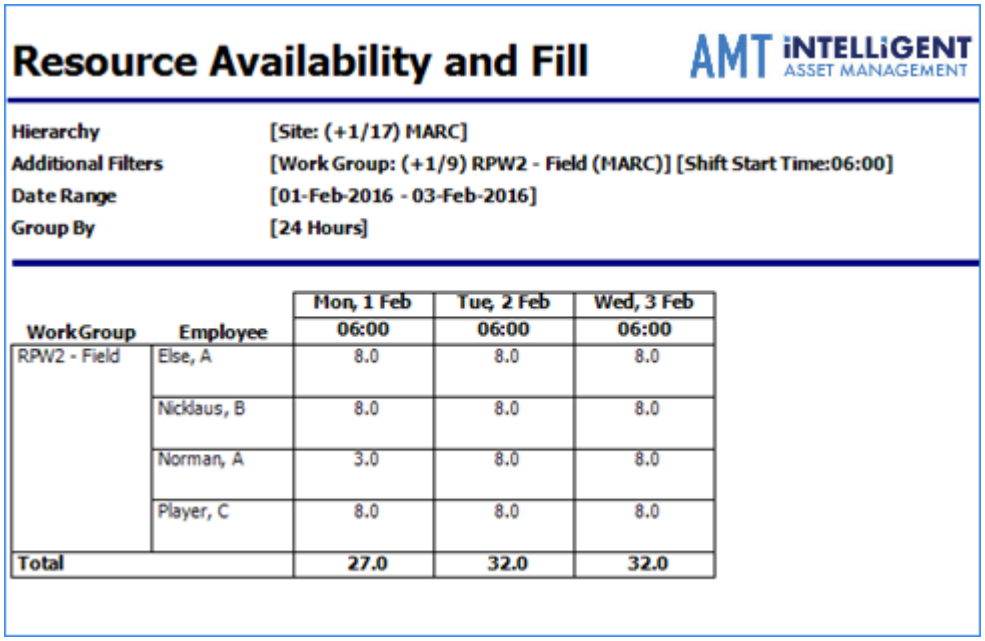

Resource Availability and Fill

AMT iNTELLiGENT ASSET MANAGEMENT

Hierarchy	**[Site: (+1/17) MARC]**
Additional Filters	**[Work Group: (+1/9) RPW2 - Field (MARC)] [Shift Start Time:06:00]**
Date Range	**[01-Feb-2016 - 03-Feb-2016]**
Group By	**[24 Hours]**

Work Group	Employee	Mon, 1 Feb 06:00	Tue, 2 Feb 06:00	Wed, 3 Feb 06:00
RPW2 - Field	Else, A	8.0	8.0	8.0
	Nicklaus, B	8.0	8.0	8.0
	Norman, A	3.0	8.0	8.0
	Player, C	8.0	8.0	8.0
Total		**27.0**	**32.0**	**32.0**

Learning Check




Check your understanding of the workshop and ask any related questions.

Notes

14. Create a Shutdown

Procedure – Steps to Create a Shutdown

1. Under **Daily Planning**, double-click **Planning**.
2. Select appropriate filters.
3. Set **Display Fields** to **Shutdown**.

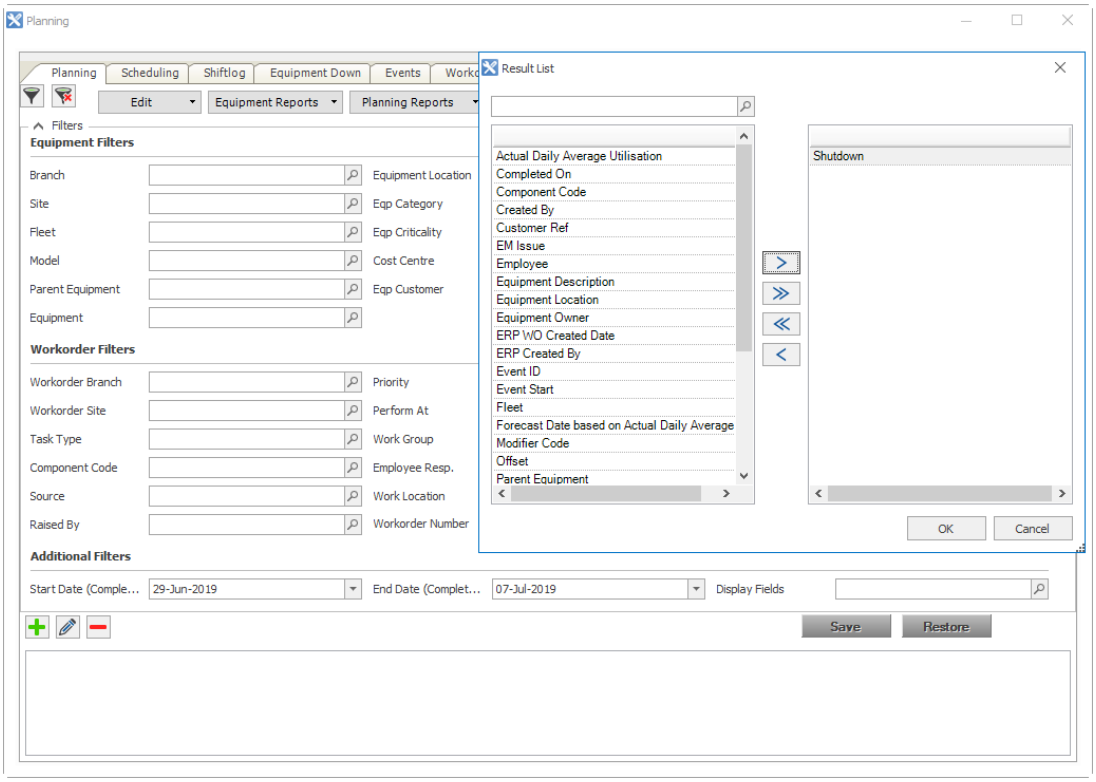

4. Click **Apply Filters**.
5. Click **Add / Edit Shutdown** from the **Edit** list.
6. Click **Add** and fill in the form details required to create a shutdown.
7. Click **Save**.
8. Allocate the relevant **IP** or **YTS** work orders to the shutdown and click **Save**.
9. All work orders within the same event will be associated to the same shutdown.
10. Click **Scheduling** and apply the same filters.
11. The shutdown appears at the top of the hierarchy on the left side of the screen; represented by a black bar on the Gantt chart. The length of the shutdown is determined by the downtime of the work orders associated with it.

Shutdowns do not affect the downtime or availability calculations of the assets to which they are associated.

15. Export Work Plan to Microsoft Project

Procedure – Export Work Plan to Microsoft Project

1. Navigate to **My Functions > Daily Planning Reports > Workplan – Export to MS Project**.

   AMT can export planning data for advanced planning and standard planning mode assets in the same export file.

2. Use filters to determine the planning data exported to Microsoft Project.
3. Click **Export**.
4. Specify the location for the Microsoft Project file, and its file name
5. Open Microsoft Project and open the exported file.

16. Communicate Plan with Production / Maintenance

Meet with production and maintenance to agree on the plan for the daily/weekly process.

Learning Check



Check your understanding of the workshop and ask any related questions.

Notes

17. Prepare Job Folders


Procedure – Steps to Prepare Job Folders

1. Navigate to **Daily Planning > Planning**.
2. Select appropriate filters.
3. For advanced planning assets, set **Display Fields** to **Event Start**.
4. Click **Apply Filters**.
5. Event start applies to advanced planning assets only (**Mode** = **A** and is **light grey** if the asset uses standard planning, **Mode** = **S** and is **dark grey** if the asset uses advanced planning).
6. Select the work order to print.
7. Select **Equipment Reports > Print Job Folder**.
8. Below is an explanation of the reports that can be printed as part of the **Job Folder (Daily Planning** > **Daily Planning Reports** > **Job Folders – Bulk Printing**.
9. Library documents are electronic documents linked to a work order either manually by the user, by the AMT library or by external document system such as SharePoint.

Report – Eventscope

This report gives a summary breakdown of the activities scheduled to be performed during the downtime event.

The second page of this report is used to capture actual downtime allocation information.

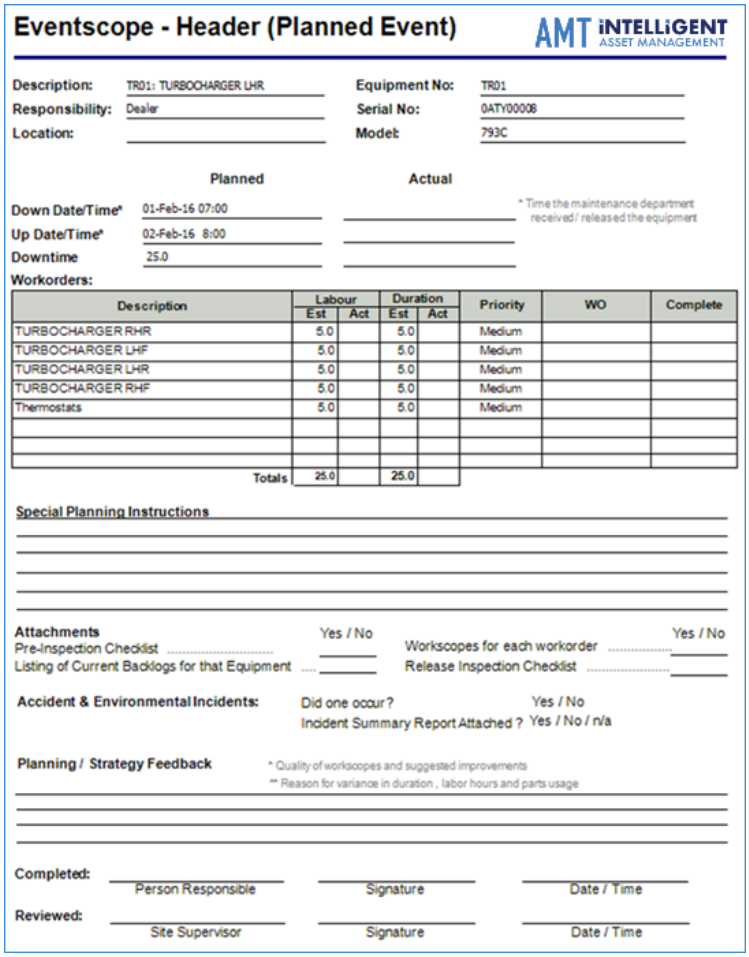

Eventscope - Header (Planned Event)

AMT iNTELLiGENT ASSET MANAGEMENT

Description: TR01: TURBOCHARGER LHR
Responsibility: Dealer
Location:
Equipment No: TR01
Serial No: 0ATY00008
Model: 793C

	Planned	Actual
Down Date/Time*	01-Feb-16 07:00	
Up Date/Time*	02-Feb-16 8:00	
Downtime	25.0	

* Time the maintenance department received / released the equipment

Workorders:

Description	Labour Est	Labour Act	Duration Est	Duration Act	Priority	WO	Complete
TURBOCHARGER RHR	5.0		5.0		Medium		
TURBOCHARGER LHF	5.0		5.0		Medium		
TURBOCHARGER LHR	5.0		5.0		Medium		
TURBOCHARGER RHF	5.0		5.0		Medium		
Thermostats	5.0		5.0		Medium		
Totals	25.0		25.0				

Special Planning Instructions

Attachments
Pre-Inspection Checklist ..... Yes / No
Listing of Current Backlogs for that Equipment .... Yes / No
Workscopes for each workorder ..... Yes / No
Release Inspection Checklist ..... Yes / No

Accident & Environmental Incidents: Did one occur? Yes / No
Incident Summary Report Attached ? Yes / No / n/a


Planning / Strategy Feedback
* Quality of workscopes and suggested improvements
** Reason for variance in duration , labor hours and parts usage

Completed: Person Responsible ____ Signature ____ Date / Time ____
Reviewed: Site Supervisor ____ Signature ____ Date / Time ____

*This report is only relevant to **Advanced Planning** assets.*

Report – WorkScope (Multiple Operations)

This report summarises the operation and provides the planning notes, and only displays when the work order has multiple operations.

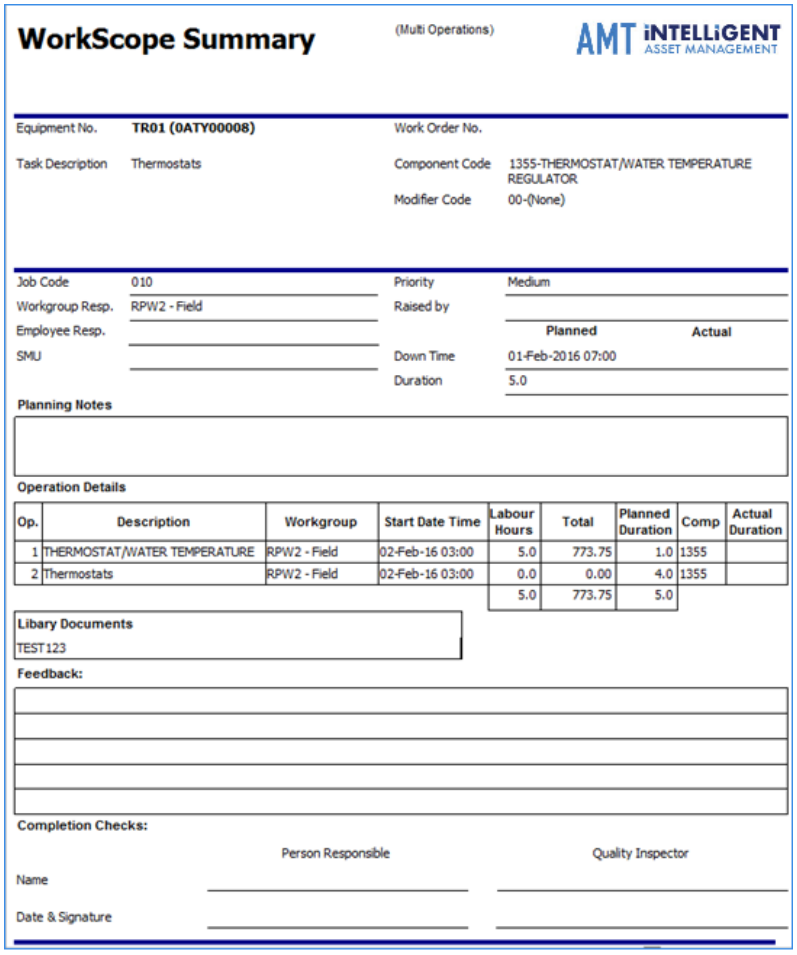

WorkScope Summary (Multi Operations) AMT iNTELLiGENT ASSET MANAGEMENT

Equipment No.	**TR01 (0ATY00008)**	Work Order No.	
Task Description	Thermostats	Component Code	1355-THERMOSTAT/WATER TEMPERATURE REGULATOR
		Modifier Code	00-(None)

Job Code	010	Priority	Medium
Workgroup Resp.	RPW2 - Field	Raised by	
Employee Resp.			**Planned** **Actual**
SMU		Down Time	01-Feb-2016 07:00
		Duration	5.0

Planning Notes

Operation Details

Op.	Description	Workgroup	Start Date Time	Labour Hours	Total	Planned Duration	Comp	Actual Duration
1	THERMOSTAT/WATER TEMPERATURE	RPW2 - Field	02-Feb-16 03:00	5.0	773.75	1.0	1355	
2	Thermostats	RPW2 - Field	02-Feb-16 03:00	0.0	0.00	4.0	1355	
				5.0	773.75	5.0		

Libary Documents
TEST123


Feedback:

Completion Checks:

	Person Responsible	Quality Inspector
Name		
Date & Signature		

Report – Operation Workscope

This report details the planned duration, parts, and labour for each operation.

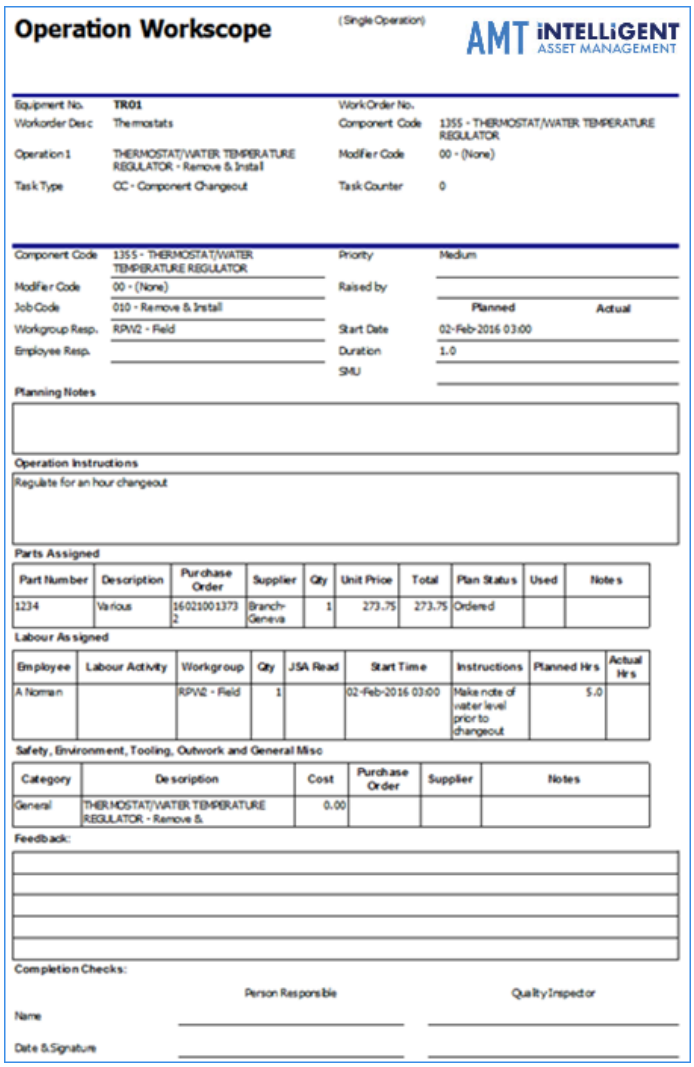

Operation Workscope (Single Operation) AMT iNTELLiGENT ASSET MANAGEMENT

Equipment No.	TR01	Work Order No.	
Workorder Desc	Thermostats	Component Code	1355 - THERMOSTAT/WATER TEMPERATURE REGULATOR
Operation 1	THERMOSTAT/WATER TEMPERATURE REGULATOR - Remove & Install	Modifier Code	00 - (None)
Task Type	CC - Component Changeout	Task Counter	0

			Planned	Actual
Component Code	1355 - THERMOSTAT/WATER TEMPERATURE REGULATOR	Priority	Medium	
Modifier Code	00 - (None)	Raised by		
Job Code	010 - Remove & Install			
Workgroup Resp.	RPW2 - Field	Start Date	02-Feb-2016 03:00	
Employee Resp.		Duration	1.0	
		SMU		

Planning Notes

Operation Instructions

Regulate for an hour changeout

Parts Assigned

Part Number	Description	Purchase Order	Supplier	Qty	Unit Price	Total	Plan Status	Used	Notes
1234	Various	160210013732	Branch-Geneva	1	273.75	273.75	Ordered		

Labour Assigned

Employee	Labour Activity	Workgroup	Qty	JSA Read	Start Time	Instructions	Planned Hrs	Actual Hrs
A Norman		RPW2 - Field	1		02-Feb-2016 03:00	Make note of water level prior to changeout	5.0	

Safety, Environment, Tooling, Outwork and General Misc

Category	Description	Cost	Purchase Order	Supplier	Notes
General	THERMOSTAT/WATER TEMPERATURE REGULATOR - Remove &	0.00			


Feedback:

Completion Checks:

	Person Responsible	Quality Inspector
Name		
Date & Signature		

Report – Operation Workscope (Single operation)

The report only displays when a work order has exactly one operation. It summarises the operation and provides the planning notes.

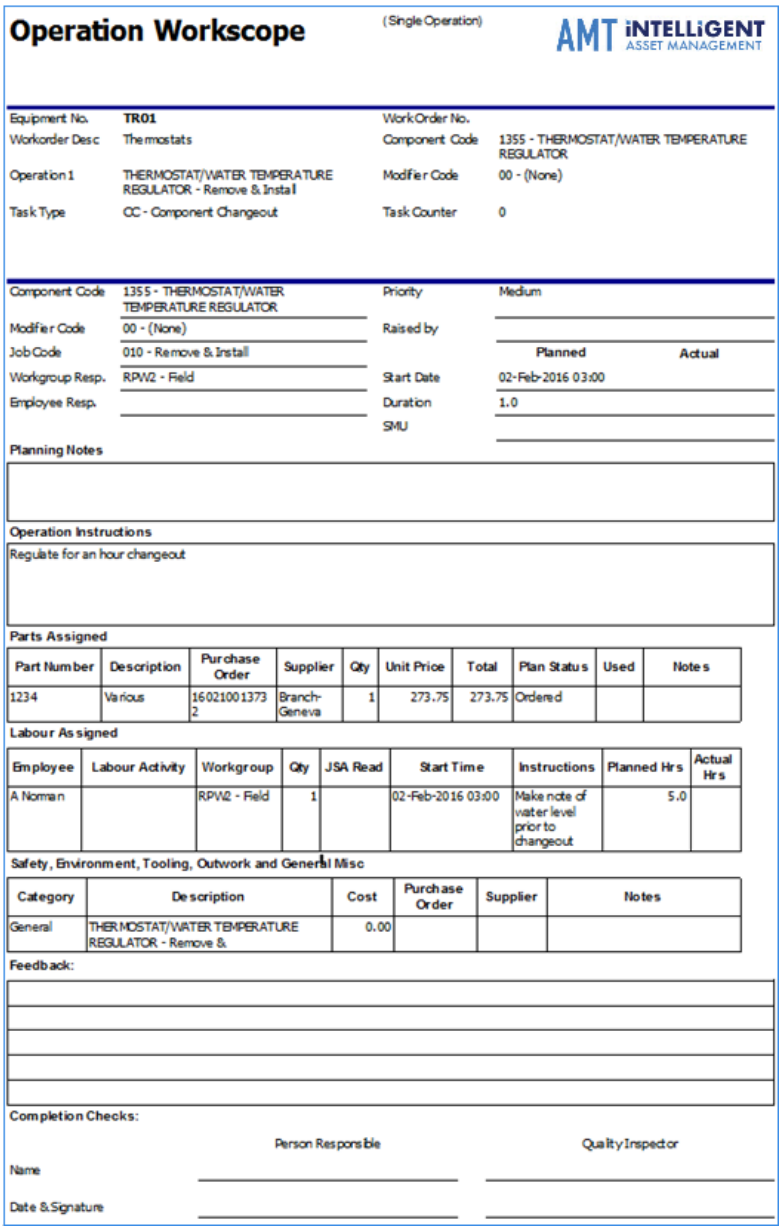

Operation Workscope

(Single Operation)

AMT iNTELLiGENT ASSET MANAGEMENT

Equipment No.	TR01	Work Order No.	
Workorder Desc	Thermostats	Component Code	1355 - THERMOSTAT/WATER TEMPERATURE REGULATOR
Operation 1	THERMOSTAT/WATER TEMPERATURE REGULATOR - Remove & Instal	Modifier Code	00 - (None)
Task Type	CC - Component Changeout	Task Counter	0

			Planned	Actual
Component Code	1355 - THERMOSTAT/WATER TEMPERATURE REGULATOR	Priority	Medium	
Modifier Code	00 - (None)	Raised by		
Job Code	010 - Remove & Install			
Workgroup Resp.	RPW2 - Field	Start Date	02-Feb-2016 03:00	
Employee Resp.		Duration	1.0	
		SMU		

Planning Notes

Operation Instructions

Regulate for an hour changeout

Parts Assigned

Part Number	Description	Purchase Order	Supplier	Qty	Unit Price	Total	Plan Status	Used	Notes
1234	Various	160210013732	Branch-Geneva	1	273.75	273.75	Ordered		

Labour Assigned

Employee	Labour Activity	Workgroup	Qty	JSA Read	Start Time	Instructions	Planned Hrs	Actual Hrs
A Norman		RPW2 - Field	1		02-Feb-2016 03:00	Make note of water level prior to changeout	5.0	

Safety, Environment, Tooling, Outwork and General Misc

Category	Description	Cost	Purchase Order	Supplier	Notes
General	THERMOSTAT/WATER TEMPERATURE REGULATOR - Remove &	0.00			

Feedback:

Completion Checks:

	Person Responsible	Quality Inspector
Name		
Date & Signature		

Exercise – Print Job Folders - Perform Work

Work plans and job folders are given to the supervisor on-site to perform the work.

The mechanic completes the following documents:

- **Eventscope** – record the downtime details and update the work order status (if completed, and the duration of each work order).
- **Workorder** – record the repair notes and sign-off details on the workscopes.
- **Labour** – depending on the processes followed, the mechanics may complete timesheets or enter labour details directly onto the workscopes.
- **Parts Return Advice** – details of parts to be returned to stores.

When you return to the workshop, all documentation (including the defect capture forms from above) is given to the supervisor.

Learning Check



Check your understanding of the workshop and ask any related questions.

Notes
